

Construction Status Update Report

April 2018

Thompson Middle School

Project Manager – Craig Lamp

Contractor – K.R. Miller Contractors, Inc.

Accomplishments

- Classroom addition steel & deck installed
- Taping of drywall progressing
- Air barrier, insulation and brick work
- Plumbing, HVAC, electrical and fire protection rough-ins ongoing
- Underground plumbing & electric in addition
- Kitchen equipment delivered and install started
- Interior plaster patching @ ceilings & walls
- Locker room addition foundation started
- Loading dock foundation complete
- Pouring slab on grade and 2nd floor slab
- Interior masonry walls
- Interior painting
- Started ceiling grid

Schedule

Project on schedule

- Upcoming Milestones
 - Complete foundation work for locker room addition
 - Complete brick for classroom addition
 - Masonry & steel for Locker room addition
 - Set light fixtures
- Anticipated Completion Date: 8/1/19
- Status Meetings: Thursdays at 11:00 am in Thompson LRC Conference Room

Budget

Total Project Budget = \$47,100,000 (pre-bid) \$44,496,000 (post bid)

Contract to K.R. Miller \$36,724,550 + \$994,812 = \$37,719,362

KR Miller paid as of 3/1/18 = \$8,640,622.72

Change Orders

- Fully Executed
 - Change Order #1 \$400,013
 - Change Order #2 \$62,384
 - Change Order #3 \$248,505
 - Change Order #4 \$283,910
- Approved in Process (Change Order #5)
 - Site revisions \$36,928
 - Infill duct openings \$9,262
 - Infill slab room 107 \$5,143
 - CUH-B2, RFI #86 \$3,114
 - Additional chilled beams \$4,496
- Pending
 - Backflow preventer B141 \$8,720
 - Power/IT requirements \$23,431
 - Gym floor striping \$3,049
 - Add fire pump \$67,510
 - Emergency shower floor drains \$72,877
 - Science rooms tempered water \$26,880
 - Sensory room/tech room revisions \$12,615
 - Connect existing roof drains \$14,232
 - Lintel replacement \$28,577
 - Parapet wall replacement \$91,218
 - Furring @ existing exterior walls T&M \$49,632
 - RTU-4 rework per ASI #3 \$9,278
 - Remove CMU between windows 1st & 2nd floor \$18,025
 - Additional tuck pointing \$18,820
- Rejected
 - Sound door alternate manufacturer (\$31,300)
 - Steel allowance (\$10,002)

Progress Photos – Next page

Classroom addition structural steel installation 3/26/18



Interior painting Choir room



Structural steel & masonry



Pouring of 2nd floor slab



Removal of existing roofing



Rough grading of parking, slope and detention



Installing roof deck



1st floor slab pour



Masonry block to top of wall height



2nd floor interior masonry wall



Delivery of cabinets



South & west elevation



Courtyard brick



HVAC units being installed in mechanical penthouse



Classroom addition plumbing rough-in



Locker room foundation



Thompson Middle School
Change Order Summary Sheet

Total Projected Budget = \$44,496,000

#	Date Issued	Description	Status	Generated By (A,O,GC)	Cost	Final Determination
RFCOP #1	8/1/2017	Acoustic Windows @ Music Area	Rejected	Owner	\$18,900	Void
RFCOP #1(a)	8/1/2017	Acoustic Windows @ Music Area (Alt)	Approved	Owner	\$10,835	Change Order #1
RFCOP #2	8/25/2017	Replace Existing Hall Lockers	Rejected	Owner	\$23,063	Void
RFCOP #3	8/25/2017	Glass Marker Boards @ Science Rooms	Rejected	Owner	\$53,490	Void
RFCOP #4	9/6/2017	Extra Cabinetry Demolition	Approved	Architect	\$1,357	Change Order #1
RFCOP #5	9/15/2017	Sitework/Parking Lot Revisions	Approved	Architect	\$55,612	Change Order #1
RFCOP #6	9/20/2017	Revise Feeder to RTU 3	Approved	Architect	\$0	Change Order #1
RFCOP #7	10/2/2017	Existing Door 17 to Remain	Approved	Architect	(\$2,099)	Change Order #1
RFCOP #8	10/10/2017	Replace hall lockers E&F	Rejected	Owner	\$41,727	Void
RFCOP #9	10/10/2017	Site changes Bulletin #2	Approved	Architect	\$68,907	Change Order #2
RFCOP #10	10/10/2017	Site changes Bulletin #3	Approved	Architect	\$36,550	Approved
RFCOP #11	10/24/2017	ERU VFD's	Approved	Architect	\$0	Change Order #2
RFCOP #12	10/26/2017	Chilled water piping	Approved	Architect	\$13,894	Change Order #4
RFCOP #13	11/6/2017	Revise wall tile	Approved	Architect	(\$4,050)	Change Order #3
RFCOP #14	11/8/2017	Renumber existing lockers	Approved	Owner	\$2,082	Change Order #2
RFCOP #15	11/8/2017	Revisions to FACS area	Approved	Architect	\$51,206	Change Order #2
RFCOP #16	11/10/2017	Band & Choir revisions	Approved	Architect/Owner	\$14,650	Change Order #2
RFCOP #17	11/9/2017	Cafeteria ceiling	Approved	Architect	\$12,638	Change Order #4
RFCOP #18	11/8/2017	Added steel at front entry	Approved	Architect	\$7,079	Change Order #2
RFCOP #19	11/16/2017	VCT in Cafeteria	Approved	Architect/Owner	(\$35,216)	Change Order #2
RFCOP #20.1	11/16/2017	Marmoleum tile in Classrooms	Approved	Architect/Owner	(\$145,254)	Change Order #2
RFCOP #20.2	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$81,848)	Void
RFCOP #20.3	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$28,199)	Void
RFCOP #21	11/16/2017	Marmoleum tile in Corridors	Approved	Architect/Owner	(\$54,514)	Change Order #2
RFCOP #22	11/16/2017	VT in Cafeteria	Void	Architect/Owner	(\$6,000)	Void
RFCOP #23	11/16/2017	VT in Classrooms	Void	Architect/Owner	Void	Void
RFCOP #24	11/20/2017	Modify running track	Void	Architect/Owner	\$132,825	Void
RFCOP #24A	11/20/2017	Modify running track Alternate	Rejected	Architect/Owner	\$193,515	Void
RFCOP #25	11/20/2017	Prep field for turf	Approved	Architect/Owner	\$28,712	Change Order #2
RFCOP #26	11/20/2017	Toilet room B130 revision	Approved	Architect	28,534	Change Order #3

RFCOP #27	11/20/2017	Skylight shaft	Approved	Architect	\$9,175	Change Order #2
RFCOP #28	11/22/2017	Cafeteria/Kitchen modifications	Approved	Architect	\$71,722	Change Order #4
RFCOP #29	11/22/2017	Area B,C,D sanitary	Approved	Architect	\$15,854	Change Order #3
RFCOP #30	11/22/2017	Area B sanitary	Approved	Architect	\$9,455	Change Order #3
RFCOP #31	11/27/2017	Electric water cooler A108	Approved	Architect	\$8,801	Change Order #3
RFCOP #32	11/28/2017	Casework changes A114	Void	Architect	Void	Void
RFCOP #33	12/12/2017	Sensory room relocation	Approved	Architect/Owner	\$21,127	Change Order #2
RFCOP #34	12/7/2017	Delete sanitary to west addition	Approved	Architect	\$536	Change Order #2
RFCOP #35	12/15/2017	Additional exterior windows	Approved	Owner	\$81,609	Change Order #4
RFCOP #36	12/8/2017	Classroom mobile casework	Approved	Architect/Owner	\$33,643	Change Order #3
RFCOP #37	12/14/2017	Backflow preventer B141	Pending	Architect	\$8,720	
RFCOP #38	12/14/2017	New radiation room A112	Approved	Architect	\$7,809	Change Order #2
RFCOP #39	12/14/2017	Water cooler B205	Approved	Architect	\$4,850	Change Order #3
RFCOP #40	12/14/2017	New door to conf. rm. B	Approved	Owner	\$10,163	Change Order #3
RFCOP #41	1/8/2018	Power & IT requirements	Approved	Architect	\$23,431	Approved
RFCOP #42	1/10/2018	Storefront finish	Approved	Architect	(\$4,037)	Change Order #2
RFCOP #43	1/12/2018	Reroute stormwater	Approved	Architect	\$3,439	Change Order #3
RFCOP #44	1/12/2018	Replace 2 existing columns	Approved	Architect	\$12,527	Change Order #4
RFCOP #45	1/12/2018	City water main revisions	Approved	City	\$6,441	Change Order #2
RFCOP #46	2/27/2018	Gym floor striping	Pending	Architect	\$3,049	
RFCOP #47	1/29/2018	Fritz tile	Approved	Owner/Architect	\$31,425	Change Order #4
RFCOP #48	1/30/2018	Subfloor patching/prep				T&M
RFCOP #49	1/30/2018	Fire pump	Approved	Architect	\$53,959	Approved
RFCOP #50	Void	Void	Void	Void	Void	Void
RFCOP #51	Void	Void	Void	Void	Void	Void
RFCOP #52	2/12/2018	MCT floor patterns	Approved	Architect	\$0	Change Order #4
RFCOP #53	2/19/2018	Emergency shower floor drains	Pending	Architect	\$72,877	
RFCOP #54	2/16/2018	Revise tempered water	Pending	Architect	\$26,880	
RFCOP #55	2/14/2018	Frosted glass @ Science rooms	Approved	Architect	\$657	Change Order #3
RFCOP #56	2/14/2018	Water cooler A106 & A127		Architect		
RFCOP #57	2/15/2018	Ceiling modifications B140 & B141	Approved	Architect	\$4,088	Change Order #3
RFCOP #58	2/15/2018	Modify existing light wells		Architect		
RFCOP #59	2/16/2018	Safety goggle cabinets	Approved	Architect	\$3,849	Change Order #4
RFCOP #60	2/21/2018	B213 mechanical chase		Architect		

RFCOP #61	2/21/2018	Sensory room/tech room revisions	Pending	Architect	\$12,615	
RFCOP #62	2/21/2018	Band/Orchestra exterior windows	Approved	Architect	\$1,154	Change Order #4
RFCOP #63	2/21/2018	Science B213 wall modification		Architect		
RFCOP #64	2/27/2018	Locker revision		Architect		
RFCOP #65	2/27/2018	Marker board modifications	Approved	Architect	(\$183)	Change Order #4
RFCOP #66	3/6/2018	Cafeteria ceiling tile revision	Rejected	Architect	\$8,354	Rejected
RFCOP #67	3/12/2018	Subfloor remedial work		Architect		
RFCOP #68	3/26/2018	Connect existing roof drains	Pending	Architect	\$14,232	T&M NTE
RFCOP #69	3/22/2018	Spandrel glass modifications	Approved	Architect	\$6,269	Approved
RFCOP #70	4/4/2018	Synthetic turf field		Owner		
RFCOP #71	4/17/2018	Added window E206		Architect/Owner		
COR #1	9/20/2017	Remove & Replace 2 Existing Manholes	Approved	Katco/RFI	\$15,462	Change Order #1
COR #2	9/27/2017	Remove & Replace Water Lines Corr 108	Approved	Owner	\$28,175	Change Order #1
COR #3	10/4/2017	Lintel Replacement	Approved	Iwanski/Architect	\$97,818	Change Order #1
COR #3A	3/27/2018	Lintel replacement Area 1D	Pending	Iwanski/Architect	\$28,175	
COR #4	10/4/2017	Parapet Wall Replacement	Pending	Iwanski/Architect	\$91,218	\$258,021 T&M NTE
COR #5	11/6/2017	Mezzanine demolition RFI #47	Approved	Miller/RFI	\$7,482	Change Order #2
COR #6		New chase walls RFI #5	Void	Void	Void	Void
COR #7	11/4/2017	Barrier curb removal RFI #7&8	Approved	Miller/RFI	\$9,075	Change Order #1
COR #8	11/1/2017	Remove floor substrate RFI #19	Approved	Miller/RFI	\$6,795	Change Order #1
COR #9	11/4/2017	Revised ramp curb detail RFI #20	Approved	Miller/RFI	\$427	Change Order #1
COR #10	11/4/2017	Revised foundation wall detail RFI #21	Approved	Miller/RFI	\$1,573	Change Order #1
COR #11	2/23/2018	Infill openings @ duct RFI #27	Approved	Miller/RFI	\$9,262	Approved
COR #12	11/4/2017	Concrete infills RFI #30&73	Approved	Miller/RFI	\$5,008	Change Order #1
COR #13	11/28/2017	Demolition of LBP RFI #35	Approved	Miller/RFI	(\$5,432)	Change Order #2
COR #14	1/3/2018	Remove blower motor	Approved	Miller/RFI	\$3,584	Change Order #2
COR #15	11/28/2017	Furring @ exterior walls RFI #45,46&70	Pending	Miller/RFI	\$49,634	T&M
COR #16		Sump pit @ elevator RFI #52	Void	Void	Void	Void
COR #17		Revise mezz wall construction RFI #53	Void	Void	Void	Void
COR #18	11/3/2017	Brick ledge @ retaining wall RFI #54&57	Approved	Miller/RFI	\$1,879	Change Order #1
COR #19	2/22/2018	Demo conc. wall in lieu of mas. RFI #55	Approved	Miller/RFI	\$2,986	Change Order #3
COR #20		Chilled water piping RFI #58	Void	Void	Void	Void

COR #21		Floor underlayment RFI #64	Void	Void	Void	Void
COR #22		Undercuts per Oz Engineering				
A	11/3/2017	Pond #1 9/15 - 9/17	Approved	Oz Engineering	\$66,776	Change Order #1
B	11/3/2017	Report #24 & #28	Approved	Oz Engineering	\$36,924	Change Order #1
C	11/3/2017	Report #38, #40 & #44	Approved	Oz Engineering	\$16,932	Change Order #1
D	11/3/2017	Report #48, #52 & #58	Approved	Oz Engineering	\$44,880	Change Order #1
E	11/3/2017	Report #73 & #81	Approved	Oz Engineering	\$2,584	Change Order #1
F	11/21/2017	Report 11/1/17, 11/2/17	Approved	Oz Engineering	\$11,900	Change Order #2
G	11/21/2017	Report 11/6/17 - 11/11/17	Approved	Oz Engineering	\$53,924	Change Order #2
H	12/18/2017	Report 11/13/17 - 11/25/17	Approved	Oz Engineering	\$6,392	Change Order #3
I	12/18/2017	Report 11/27/17 - 12/2/17	Approved	Oz Engineering	\$62,356	Change Order #3
J						
K						
COR #23	11/3/2017	Drain tile @ retaining wall RFI #77	Approved	Miller/RFI	\$8,139	Change Order #2
COR #24		Roof parapet replacement	Void	Void	Void	Void
COR #25	11/28/2017	Electric cost above allowance	Approved	Miller/Allowance	\$1,700	Change Order #2
COR #26	1/3/2018	Manhole 33 to parkway	Approved	Rettler	\$41,447	Change Order #3
COR #27		Hot and chilled water ERU-6	Void	Void	Void	Void
COR #28		Piping to VAV	Void	Void	Void	Void
COR #29	2/2/2018	Kitchen piping revisions	Approved	Miller/RFI	\$2,768	Change Order #3
COR #30	2/22/2018	Coal shoot infill @ courtyard	Approved	Miller/RFI	\$2,082	Change Order #3
COR #31	2/23/2018	Deadwall revisions	Approved	Miller/RFI	\$693	Change Order #3
COR #32	2/23/2018	Infill opening 107	Approved	Miller/RFI	\$5,143	Approved
COR #33	2/23/2018	Retaining wall demo	Approved	Miller/RFI	\$5,916	Change Order #4
COR #34	2/2/2018	CR Leonard RFI #109	Approved	Miller/RFI	\$6,450	Change Order #3
COR #35	2/2/2018	Additional piping RFI #115	Approved	Miller/RFI	\$1,680	Change Order #3
COR #36	12/22/2017	Remove T&G flooring room 107A	Approved	Miller/RFI	\$2,602	Change Order #2
COR #37		Waterline revision per City	Void	Void	Void	Void
COR #38		Void	Void	Void	Void	Void
COR #39	2/22/2018	ASI #10	Approved	Architect	\$2,,300	Change Order #3
COR #40	1/31/2018	Sound door & frames to match window	Rejected	Miller	(\$31,300)	Rejected
COR #41	2/23/2018	CUH-B2 RFI #86	Approved	Miller/RFI	\$3,114	Approved
COR #42	2/2/2018	ASI #9 ductwork B212	Approved	Architect	\$3,918	Change Order #3
COR #43	2/2/2018	ASI #3 RTU-4	Pending	Architect	\$9,278	

COR #44	2/23/2018	Chilled beams added after bid	Approved	Miller/RFI	\$4,496	Approved
COR #45	2/21/2018	Fire sprinkler plan review	Approved	Miller	\$788	Change Order #4
COR #46	3/6/2018	Hardware finish	Approved	Miller/RFI	\$11,025	Change Order #4
COR #47	3/8/2018	Remove additional UG tank	Approved	Miller	\$13,352	Change Order #4
*COR #48	3/8/2018	Remove CMU @ windows	Approved	Architect	\$18,025	Approved/ATSR pay
COR #49	3/8/2018	Revise steel 2nd floor cafeteria	Approved	Architect	\$15,822	Change Order #4
COR #50	3/8/2018	Outlet for water cooler B126	Pending	Architect	\$315	Change Order #4
COR #51	3/8/2018	Remove burried conc pad water line	Approved	Miller	\$3,928	Change Order #4
COR #52	3/19/2018	IT floor mounted cabinet	Approved	Owner	\$1,848	Change Order #4
COR #53	3/19/2018	AT&T allowance	Approved	Miller	\$4,375	Change Order #4
COR #54	3/23/2018	Beam lead paint removal	Approved	Miller	\$4,656	Change Order #4
COR #55	3/23/2018	Anti-static flooring	Rejected	Miller	\$2,247	Rejected
COR #56	3/23/2018	Steel allowance	Rejected	Architect	(\$10,002)	Rejected
COR #57	3/27/2018	Additional tuckpointing	Pending	Iwanski/Architect	\$18,820	
			Change Order #1		\$400,013	
			Change Order #2		\$62,384	
			Change Order #3		\$248,505	
			Change Order #4		\$283,910	
			Approved Changes		\$160,249	
			Pending Changes		\$335,498	
*COR #48		ATS&R to reimburse cost \$18,025				
			Total Changes		\$1,490,559	
			Rejected Changes		\$299,994	

Thompson Middle School					%
K.R. Miller Contract				\$36,724,550.00	
		Change Order #1		\$400,013.00	
		Change Order #2		\$62,384.00	
		Change Order #3		\$248,505.00	
		Change Order #4		\$283,910.00	
	Paid to Date	Pay App 1		-670,788.90	
		Pay App 2		-691,703.10	
		Pay App 3		-1,251,562.50	
		Pay App 4		-1,696,042.75	
		Pay App 5		-2,269,936.97	
		Pay App 6		-1,067,888.49	
		Pay App 7		-992,700.01	
		Balance Due		\$29,078,739.28	77%
	Contingency Allocation			\$ 2,500,000.00	
	Signed Change Orders				
		Change Order #1		\$ 400,013.00	
		Change Order #2		\$62,384	
		Change Order #3		\$248,505	
		Change Order #4		\$283,910	
	Pending Change Orders			\$495,747	
	Remaining Contingency			\$ 1,009,441.00	40%

ARMSTRONG, TORSETH, SKOLD AND RYDEEN, INC.
ARCHITECTS AND ENGINEERS
MEMORANDUM NO. 39C

Project Number: 16045
Page 1

DATE April 12, 2018

PROJECT Thompson Middle School Additions and Alterations

SUBJECT Construction Meeting

PRESENT School District #303
Craig Lamp
Seth Chapman
Steve Morill
John Baird

K.R. Miller
Robert Richards
Michael Cwienkala
Paul Ingraham
Cody LaBeck

Katco
Kevin

Rettler Corporation
Mike Helmrick (phoned in)

City of St. Charles
Rainier Galliano
Jeff Stengler

ATS&R
Mark Hayes
Stewart Haugen

BY Stewart Haugen

1. PROGRESS SCHEDULE / LOOK AHEAD:

- a. Unit C - prepping for and pouring concrete Slab on Grade; underground plumbing being installed; second floor slab to be poured next week.
- b. Unit D - concrete Slab on Grade completed; second floor slab to be poured next week; mech equipment being installed in penthouse; first floor walls being laid out
- c. Unit G - existing air shafts infilled; footings poured this week
- d. Unit B - mech rough ins mostly complete; mezzanine mech units onsite; finish work beginning; chimney demo to begin soon; hole patching in ceilings and walls continues; casework has been delivered (stored in Unit A); reroofing continues (including parapet remediation)

2. **SUBMITTALS:**
 - a. Approximately 6 items to be submitted/ reviewed
3. **REQUEST FOR INFORMATION (RFI):**
 - a. 1-200 issued to date.
4. **CHANGES IN THE WORK (ASI, RFCOP):**
 - a. RFCOPs: 1-70 issued to date.
 - b. ASIs: 1-21 issued to date.
 - c. CORs: 1- 57 issued to date.
5. **BUILDING ACCESS:**
 - a. No issues.
6. **OLD BUSINESS:**

(New Business from 04.12.18 mtg)

 - a. CO #4 will be sent to KR Miller's Chicago office for Friday 04.06 arrival.
 - b. District to confirm camera locations.
 - c. ATS&R to review on-site painting next week.
 - d. Existing doors may need to be upgraded..
 - e. District to see if ROE can assist regarding interpretation of plumbing requirements.
 - f. The district and the city are each considering hiring a plumbing consultant.
 - g. On-site meeting w/ masonry contractor will be Thursday, 04.12.
 - h. Installation of the mixing valves, for the eyewash stations, has been determined.
 - i. Installation of the 4" floor drains, going under the emergency showers, has been determined.
 - j. ATS&R to provide document approving T&M work scope for insulating existing Rain Water Leader's.
 - k. Civil Engineer to attend construction meetings, either in person or by phone.
7. **NEW BUSINESS:**
 - a. The district appreciates KR Miller efforts in keeping the jobsite quite in the earliest work hours of the day.
 - b. ATS&R to research a visual annunciation strategy, linked to the intercom system, for the band, choir and orchestra rooms.
 - c. No Fire Exits shall exit, from any portion of the building, into the courtyard.
 - d. The state plumbing inspector's involvement in this project was discussed. The district, in conjunction with the city, KR Miller and ATS&R is continuing to look at options. A new strategy, involving a consultant retained by the city, is being pursued. The goal of these pursuits is to come to an acceptable resolution on a few issues. These issues have had, thus far, requirements stated by the inspector that ATS&R doesn't completely agree with; and, is unable to find the statutory explanation(s) for the stated requirements.
 - e. The athletic fields slot drains where discussed.
 1. If artificial turf is installed now, the drains will be eliminated.

2. If natural turf is installed now the drains will remain in the work scope.
3. If natural turf goes in now, but artificial turf is planned for the near or distant future, the district will decide about keeping the drains in the work scope.

8. The next Construction Meeting is on Thursday, April 19, 2018 at 11:00 AM in Conference Room A120.

These notes represent the author's understanding of items discussed and decisions made at this meeting. Any comments or corrections should be forwarded to ATS&R within seven (7) days.

OSH:se

Cc: Project Contacts

Encl: KR Miller -Three Week Look Ahead calendar, 04.12.18

PROJECT CONTACTS

Name	Company	Cell	Email
Stewart Haugen	ATS&R	612-599-8517	shaugen@atsr.com
Mark Hayes	ATS&R	612-325-3577	mhayes@atsr.com
Tony Walz	Clark Engineering	765-595-3127	twalz@clark-eng.com
Mike Helmrick	Rettler Corp.	715-347-2314	mhelmrick@rettler.com
Jason Pearson	CUSD 303		Jason.pearson@d303.org
Craig Lamp	CUSD 303	312-975-7253	Craig.lamp@d303.org
Seth Chapman	CUSD 303	847-527-9255	Seth.chapman@d303.org
John Baird	CUSD 303	630-957-8434	John.baird@d303.org
Steve Morrill	CUSD 303		Stephen.morrill@d303.org
Keith Miller	KR Miller	312-504-2475	keith.miller@krmiller.com
Michael Cwienkala	KR Miller	847-561-4966	Michael.Cwienkala@krmiller.com
Cody LaBeck	KR Miller	847-809-1990	Cody.LaBeck@krmiller.com
Paul Ingraham	KR Miller	847-417-9069	Paul.ingraham@krmiller.com
Robert Richards	KR Miller	847-561-5775	Robert.richards@krmiller.com
Jeff Stengler	City of St. Charles		jstengler@stcharlesil.gov
Rainier Galliano	City of St. Charles	PH 630-377-4457	rgalliano@stcharlesil.gov
Mike Neumair	City of St. Charles		mneumaier@stcharlesil.gov



K.R. Miller Contractors, Inc.

Three Week Look Ahead Schedule


Project: Thompson Middle School Additionals and Alterations
705 West Main Street
St. Charles, IL 60174


Contractor: K.R. Miller Contractors, Inc.
1624 Colonial Parkway
Inverness, IL 60067

Architect: ATS&R
8501 Golden Valley Road, Suite 300
Minneapolis, MN 55427
AOR Project No. 16045

Submitted: April 19, 2018

Last Week							Subcontractor	Activity	Current Week							Week 2							Week 3						
Week Ending 04/14/18									Week Ending 04/21/18							Week Ending 04/28/18							Week Ending 05/05/18						
M	T	W	Th	F	Sa	Su			M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su
4/9	4/10	4/11	4/12	4/13	4/14	4/15			4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6
X	X	X	X	X			Construction Junction	Earthwork (Weather Dependant)						X	X	X	X	X					X	X	X	X	X		
X	X						Construction Junction	Excavation for Foundations (Bldg G)																					
							Construction Junction	Backfill for Foundations (Bldg G)									X	X	X										
							Construction Junction	Excavation for Foundations (Bldg H)															X	X	X	X	X	X	
		X	X	X			K.R. Miller	Concrete Footings and Foundations (Bldg G)						X	X	X	X												
X	X	X	X	X			K.R. Miller	Concrete Slab on Deck/Grade (Bldg D)						X	X	X													
X	X	X	X	X			K.R. Miller	Concrete Slab on Deck/Grade (Bldg C)						X	X	X	X	X											
X	X	X	X	X			Iwanski Masonry	Air and Vapor Barrier (Bldg C)						X	X	X	X	X											
X	X	X	X	X			Iwanski Masonry	Brick Veneer (Bldg C)						X	X	X	X	X											
							Iwanski Masonry	CMU Masonry Walls (Bldg G)						X	X	X	X	X				X	X	X	X	X			
							Mark Industries	Aluminum Windows (Bldg B)						X	X	X	X	X				X	X	X	X	X			
							Mark Industries	Aluminum Windows (Bldg C & D)						X	X	X	X	X				X	X	X	X	X			
X	X	X	X	X			Iwanski Masonry	Interior CMU Partitions (Bldg D)						X	X	X	X	X				X	X	X	X	X			
							Iwanski Masonry	Interior CMU Partitions (Bldg C)													X	X	X	X	X				
							K.R. Miller	Exterior Sheathing & Insulation (Bldg D)						X	X	X	X	X											
							L.J. Morse	Partition Walls - Framing (Bldg C&D)												X	X	X	X	X					
X	X	X	X	X			L.J. Morse	Partition Walls - Taping (Bldg A&B)																					
X	X	X	X	X			Waukeegan Roofing	Roofing (Bldg B)															X	X	X	X	X		

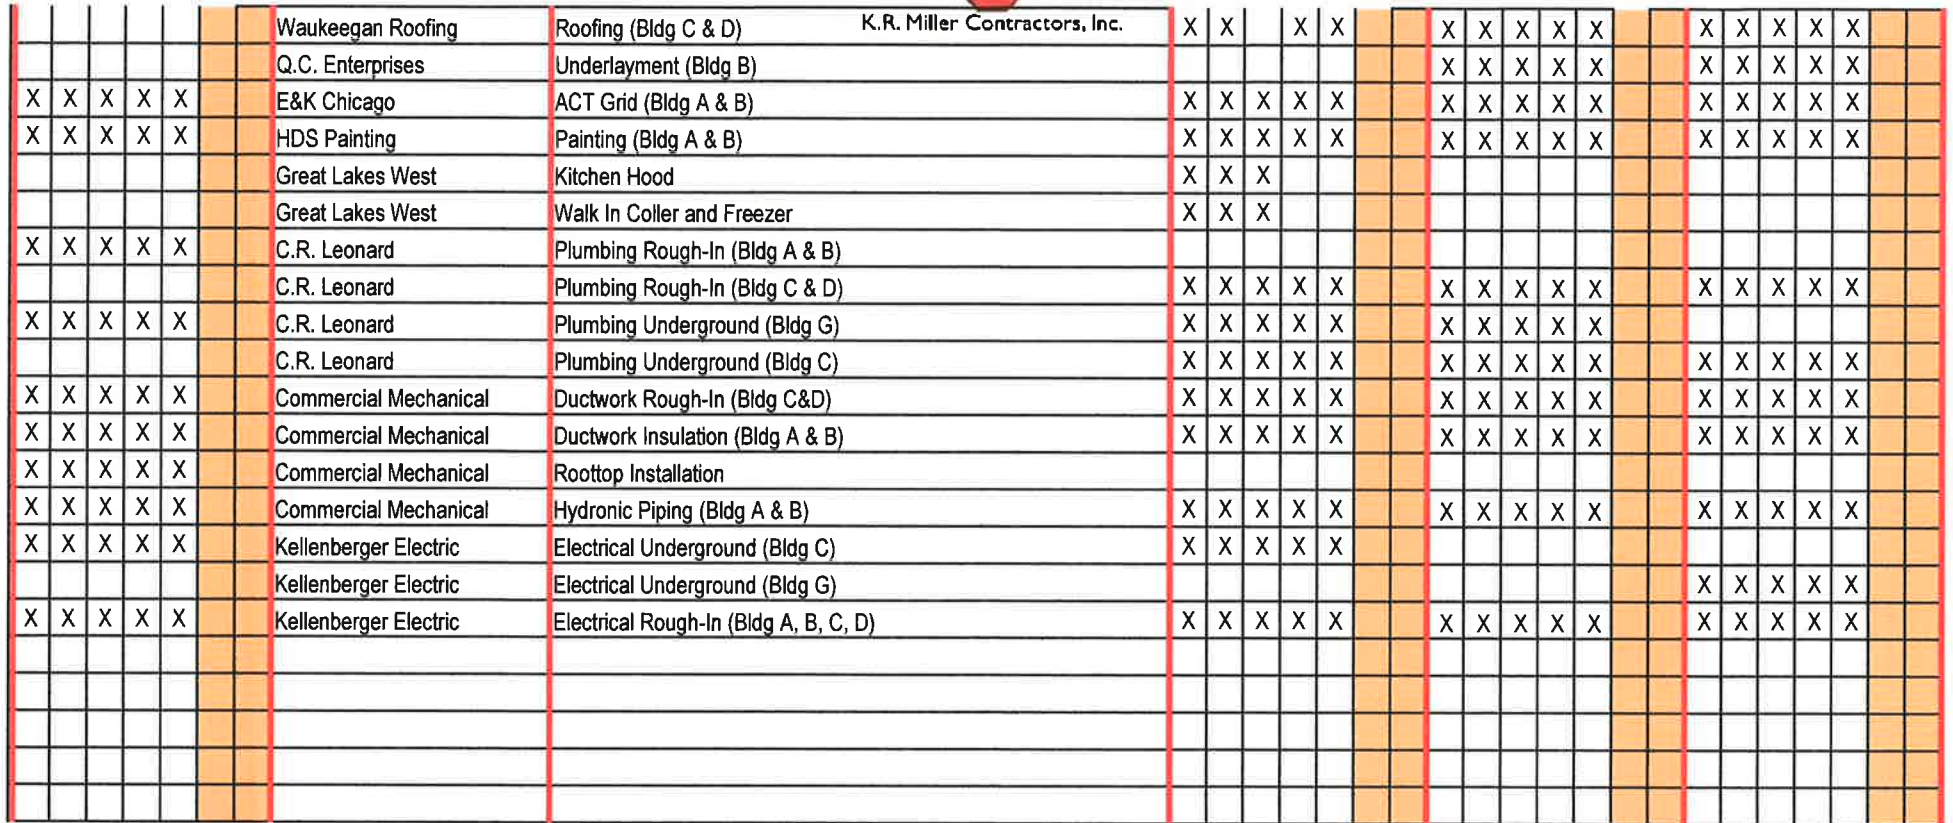

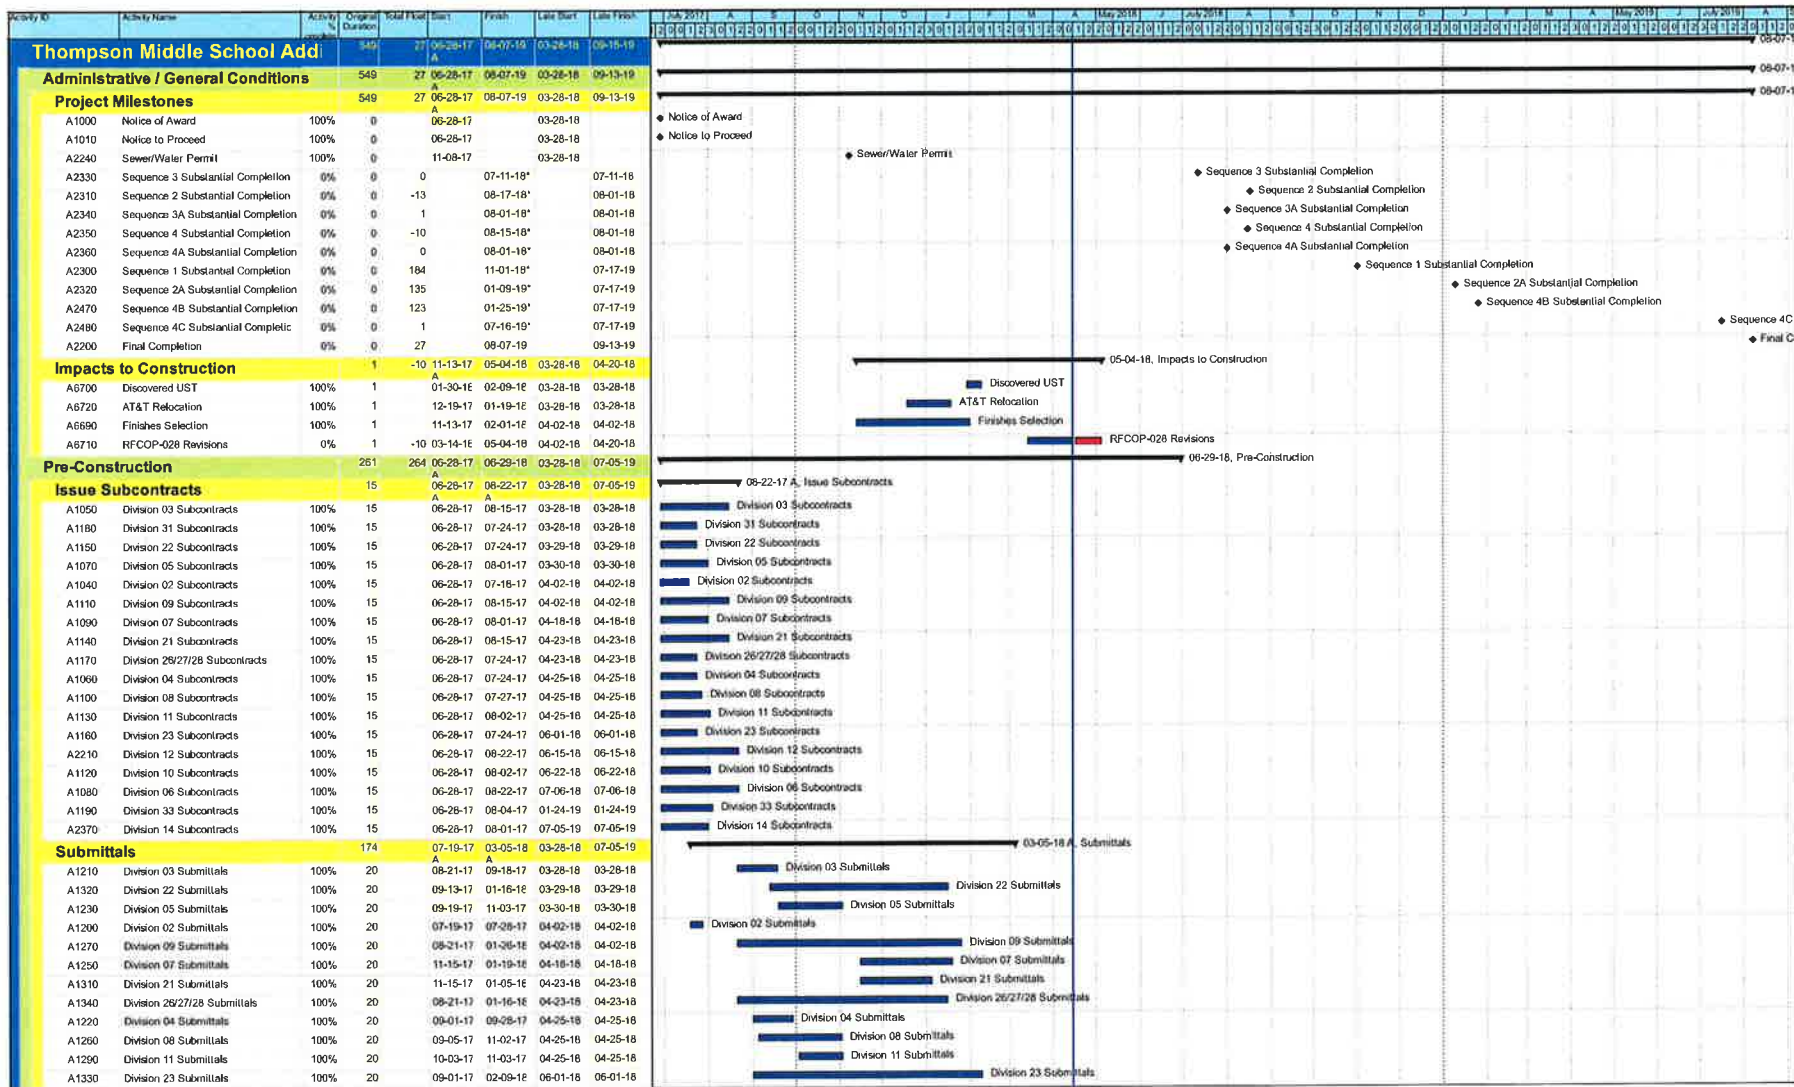


Run Date 04-19-18

Data Date 04-15-18

Page 1 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



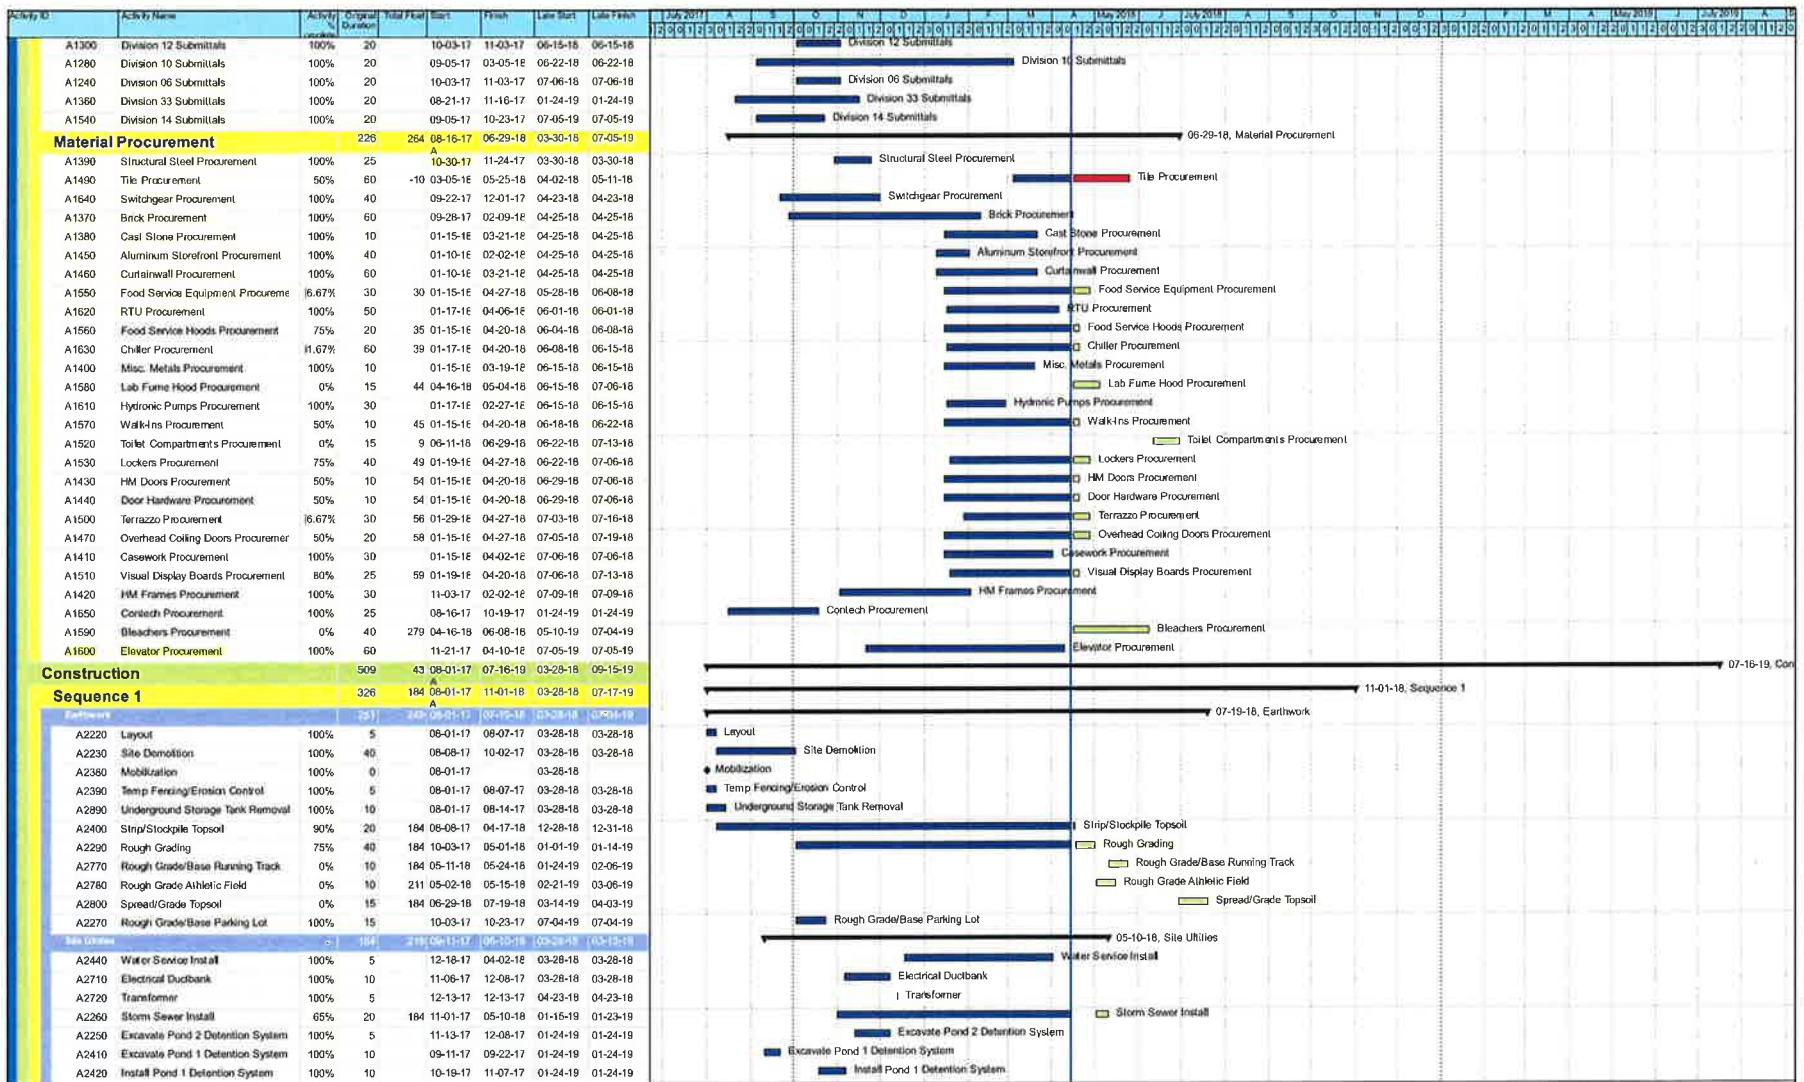


Run Date 04-19-18

Data Date 04-15-18

Page 2 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



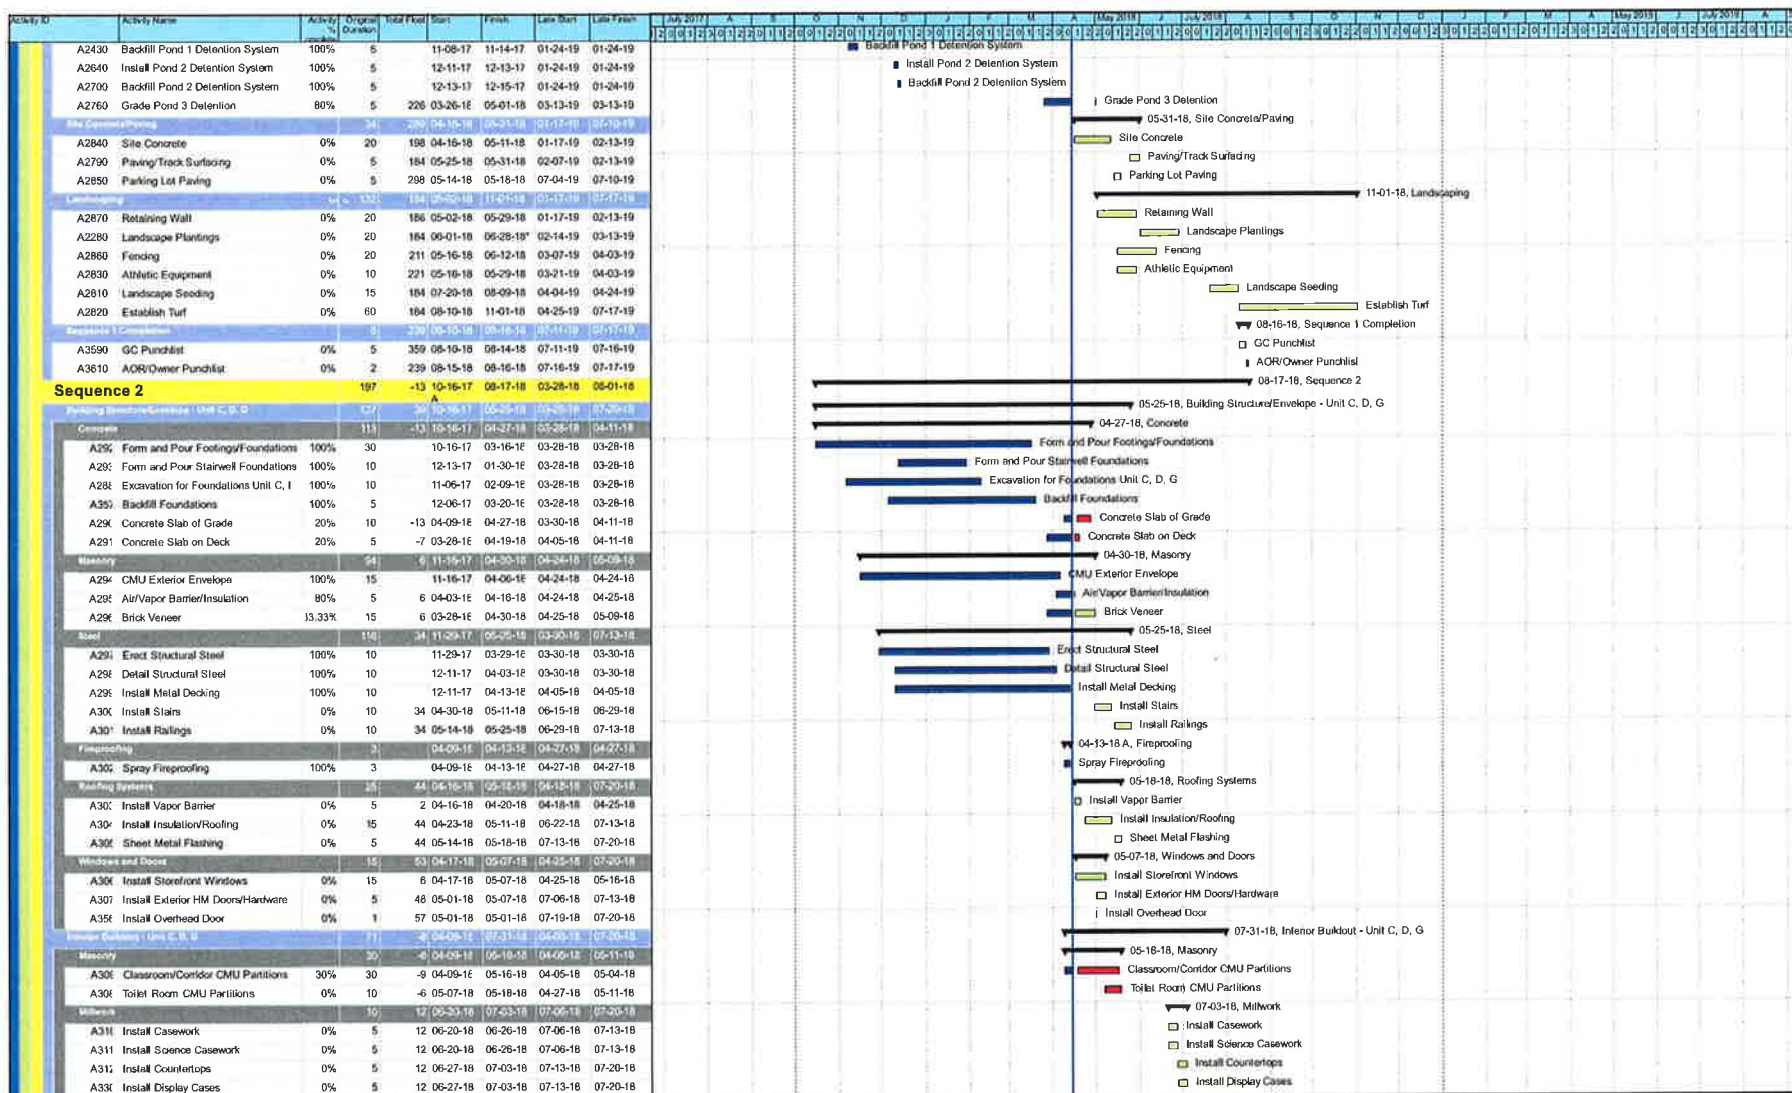


Run Date 04-19-18

Data Date 04-15-18

Page 3 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



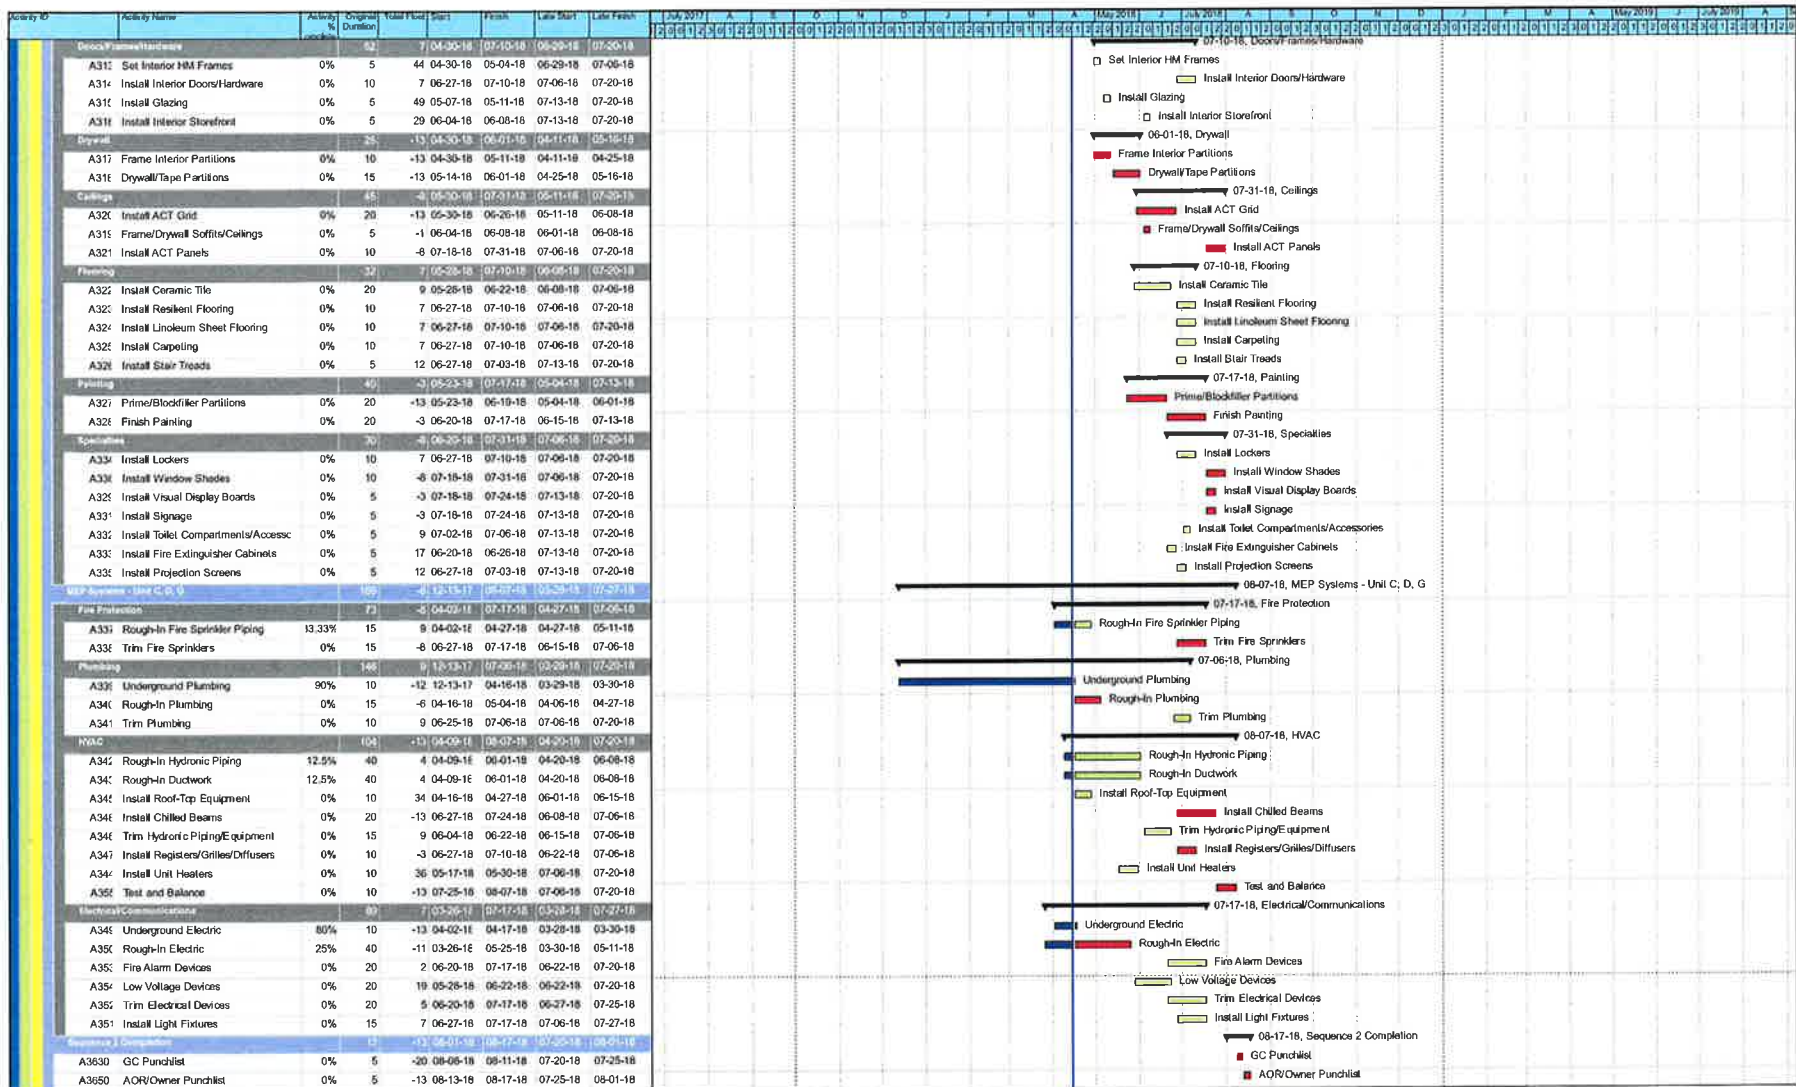


Run Date 04-19-18

Data Date 04-15-18

Page 4 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



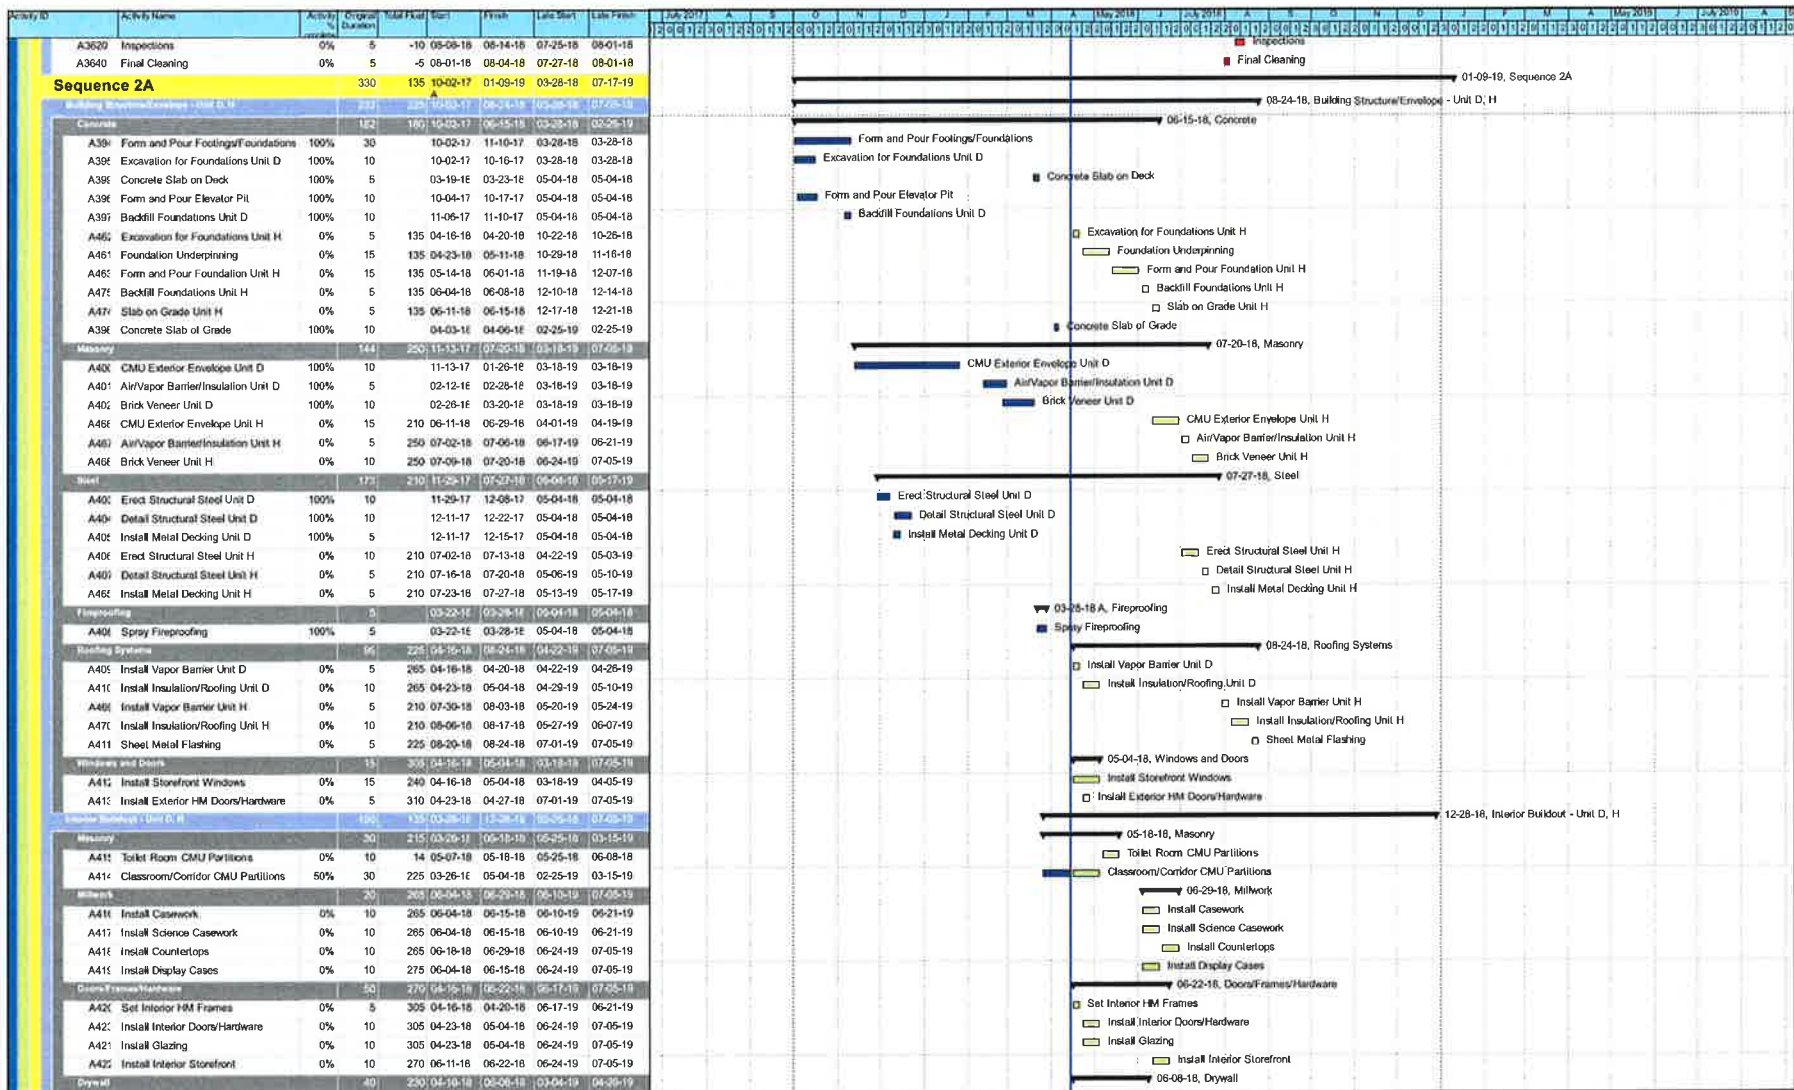


Run Date 04-19-18

Data Date 04-15-18

Page 5 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



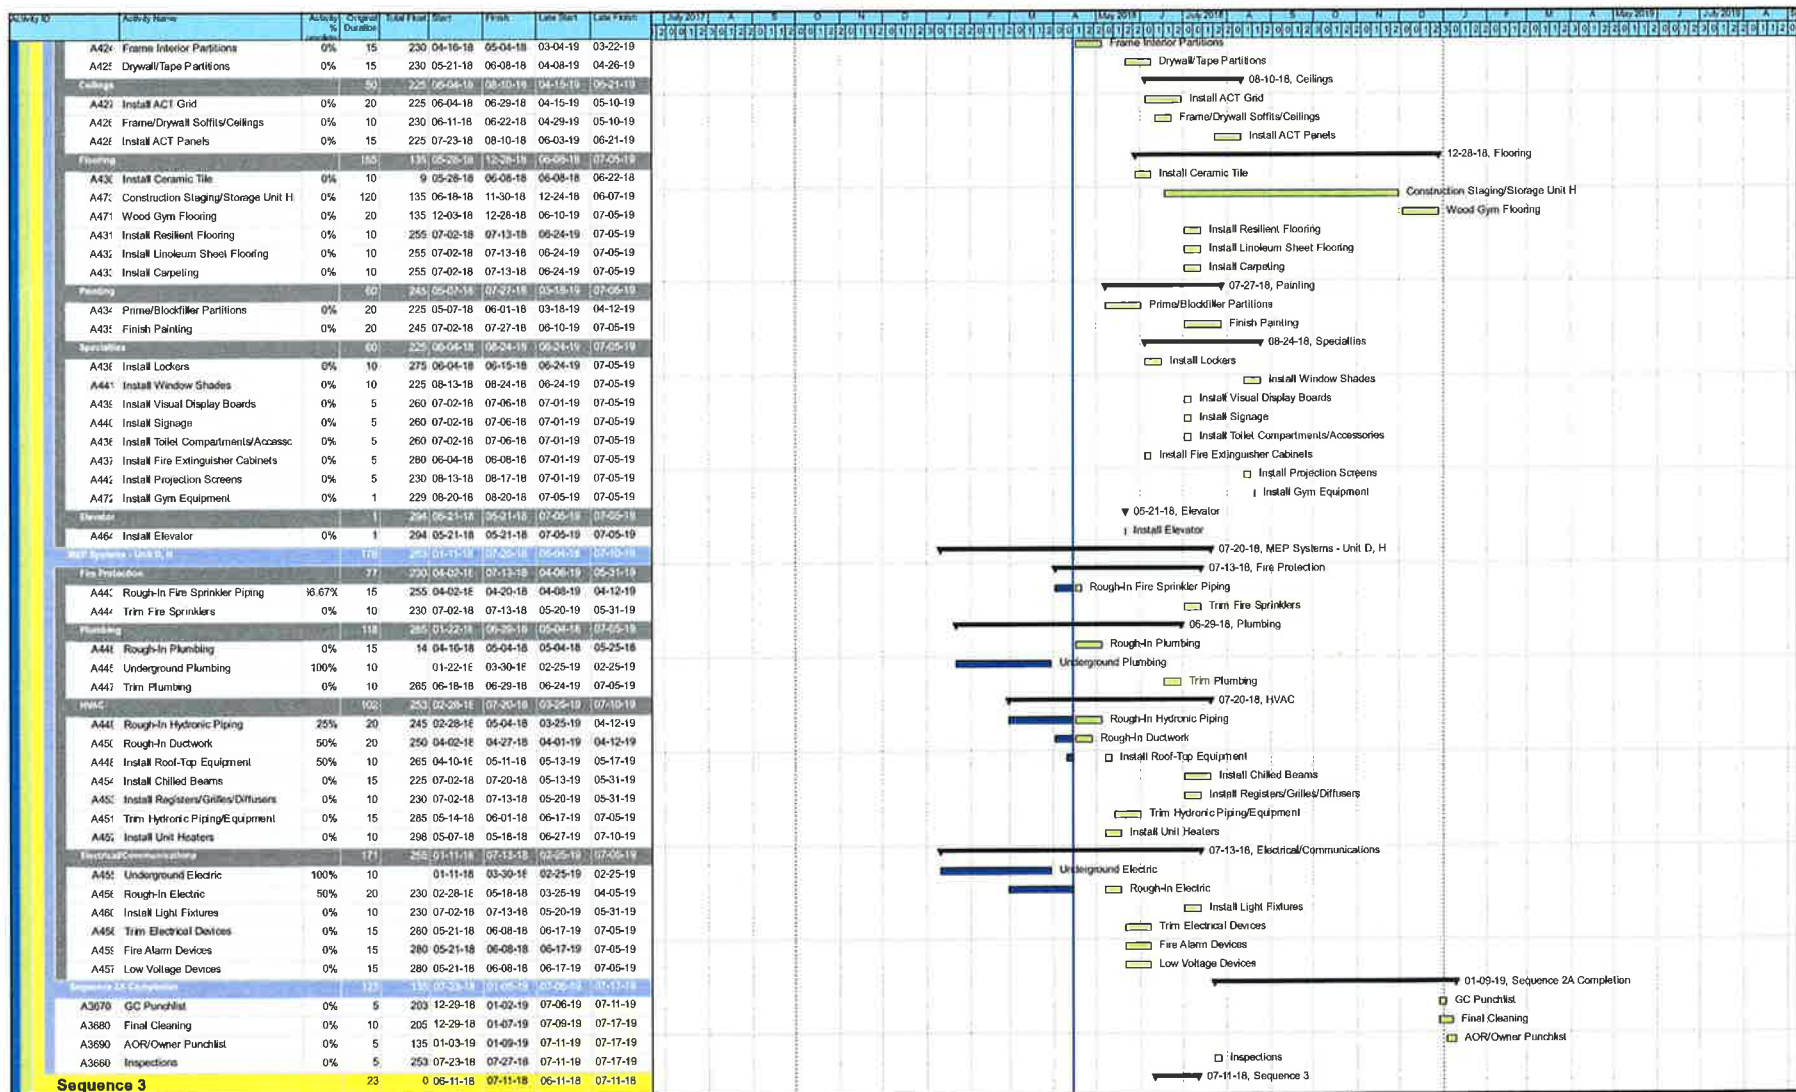


Run Date 04-19-18

Data Date 04-15-18

Page 6 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



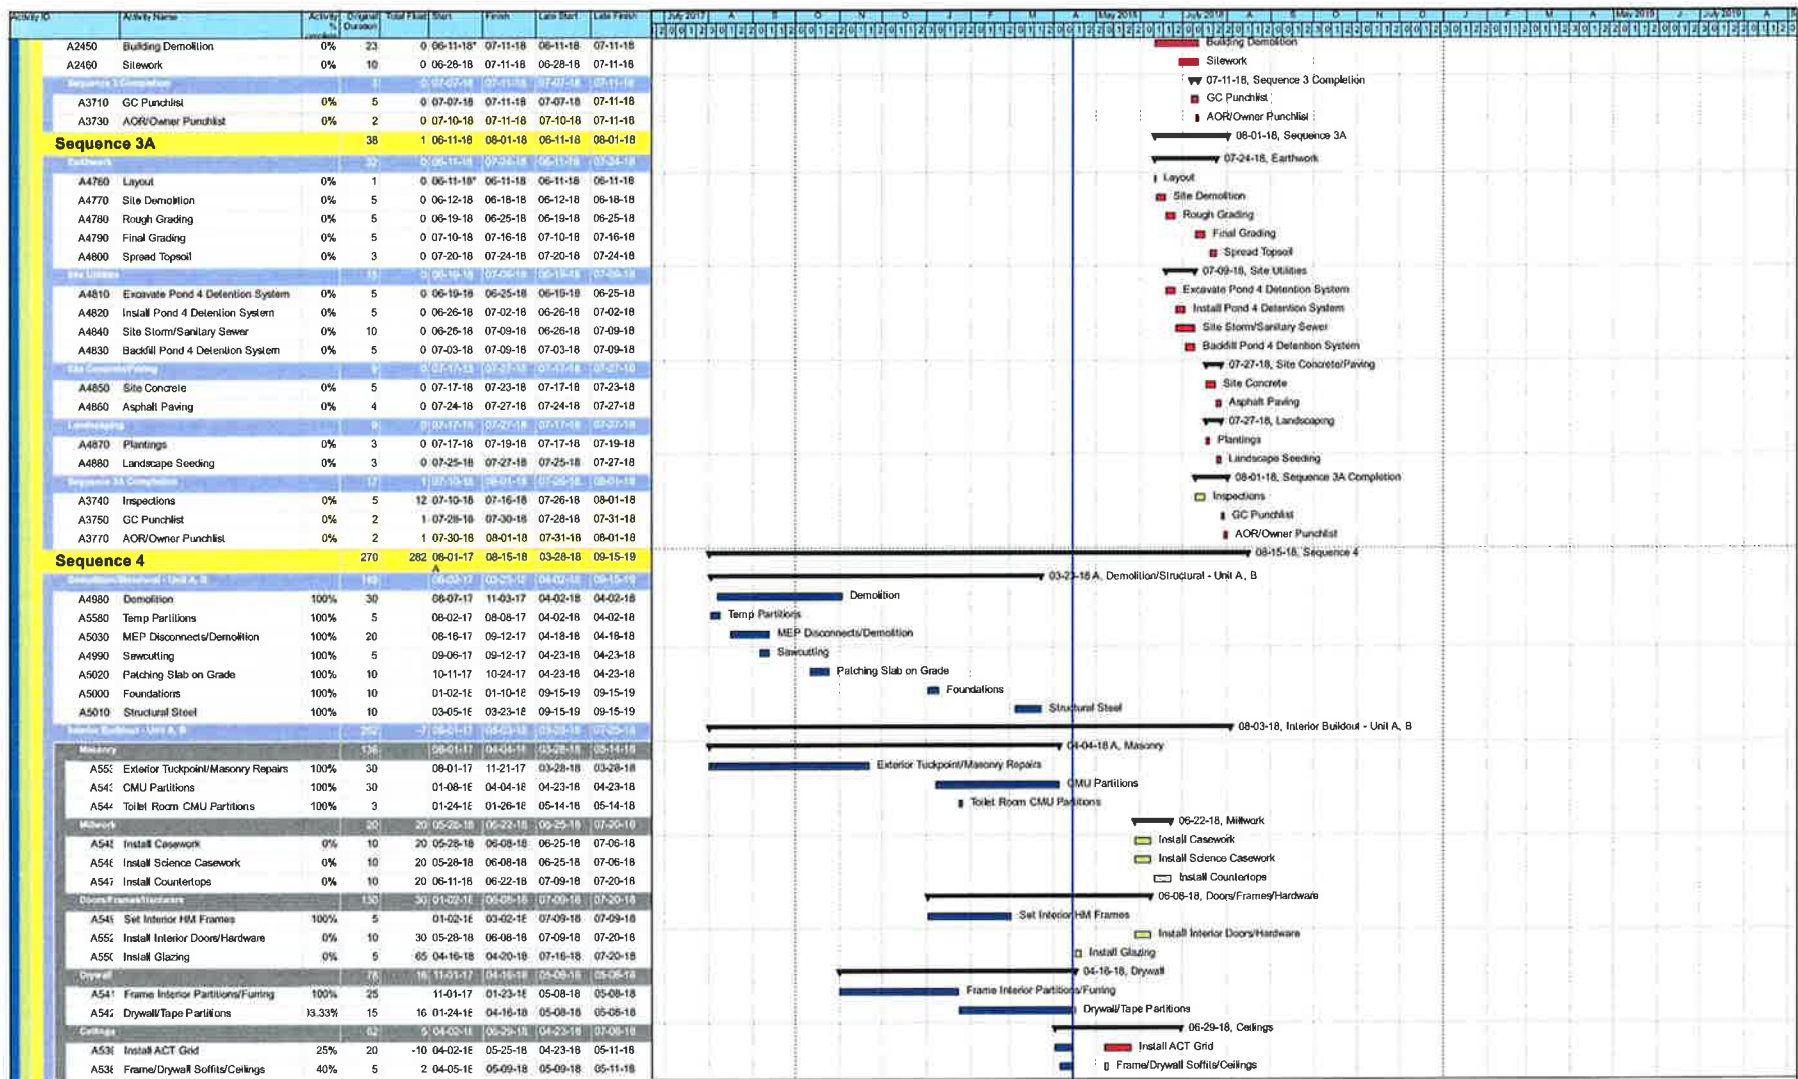


Run Date 04-19-18

Data Date 04-15-18

Page 7 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



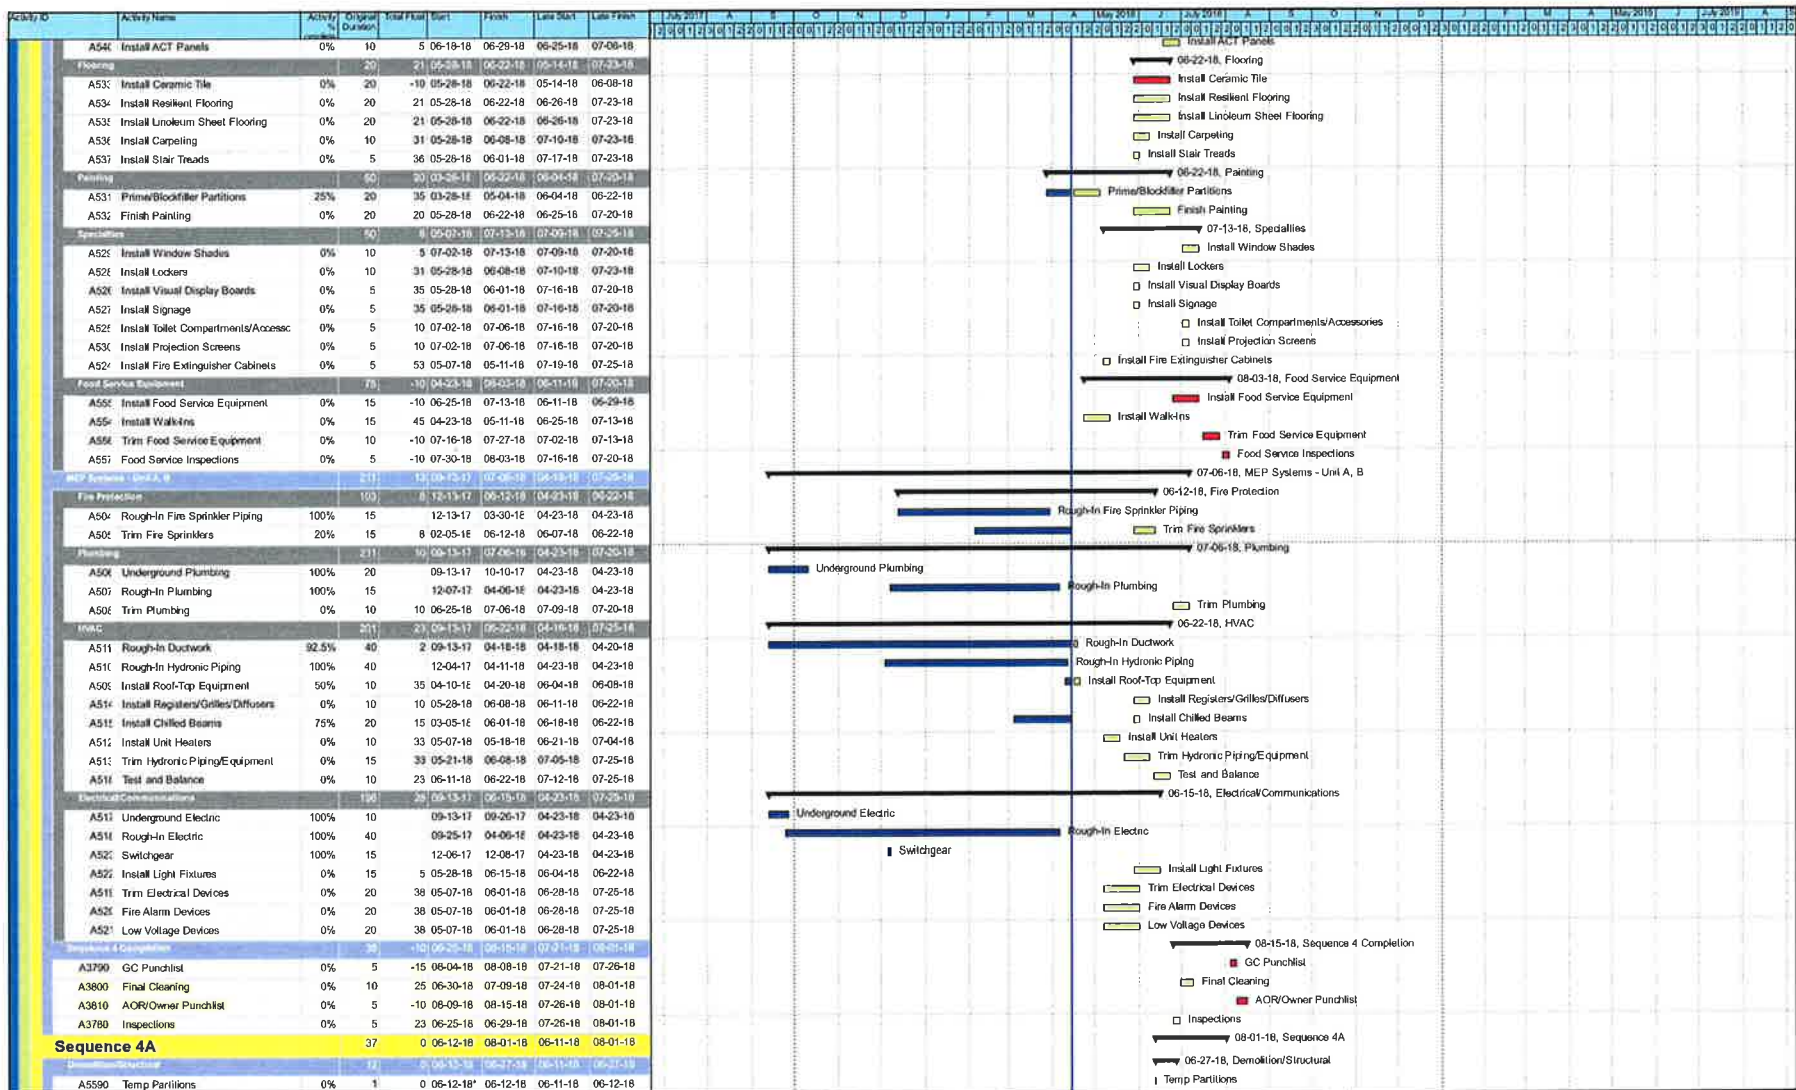


Run Date 04-19-18


Data Date 04-15-18

Page 8 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



Run Date 04-19-18	<p align="center">Thompson Middle School Additions and Alterations</p> <p align="center">Schedule Update</p> <p align="center">Submitted April 19, 2018</p>	 <p align="center">K.R. Miller Contractors, Inc.</p>
Data Date 04-15-18		
Page 9 of 11		

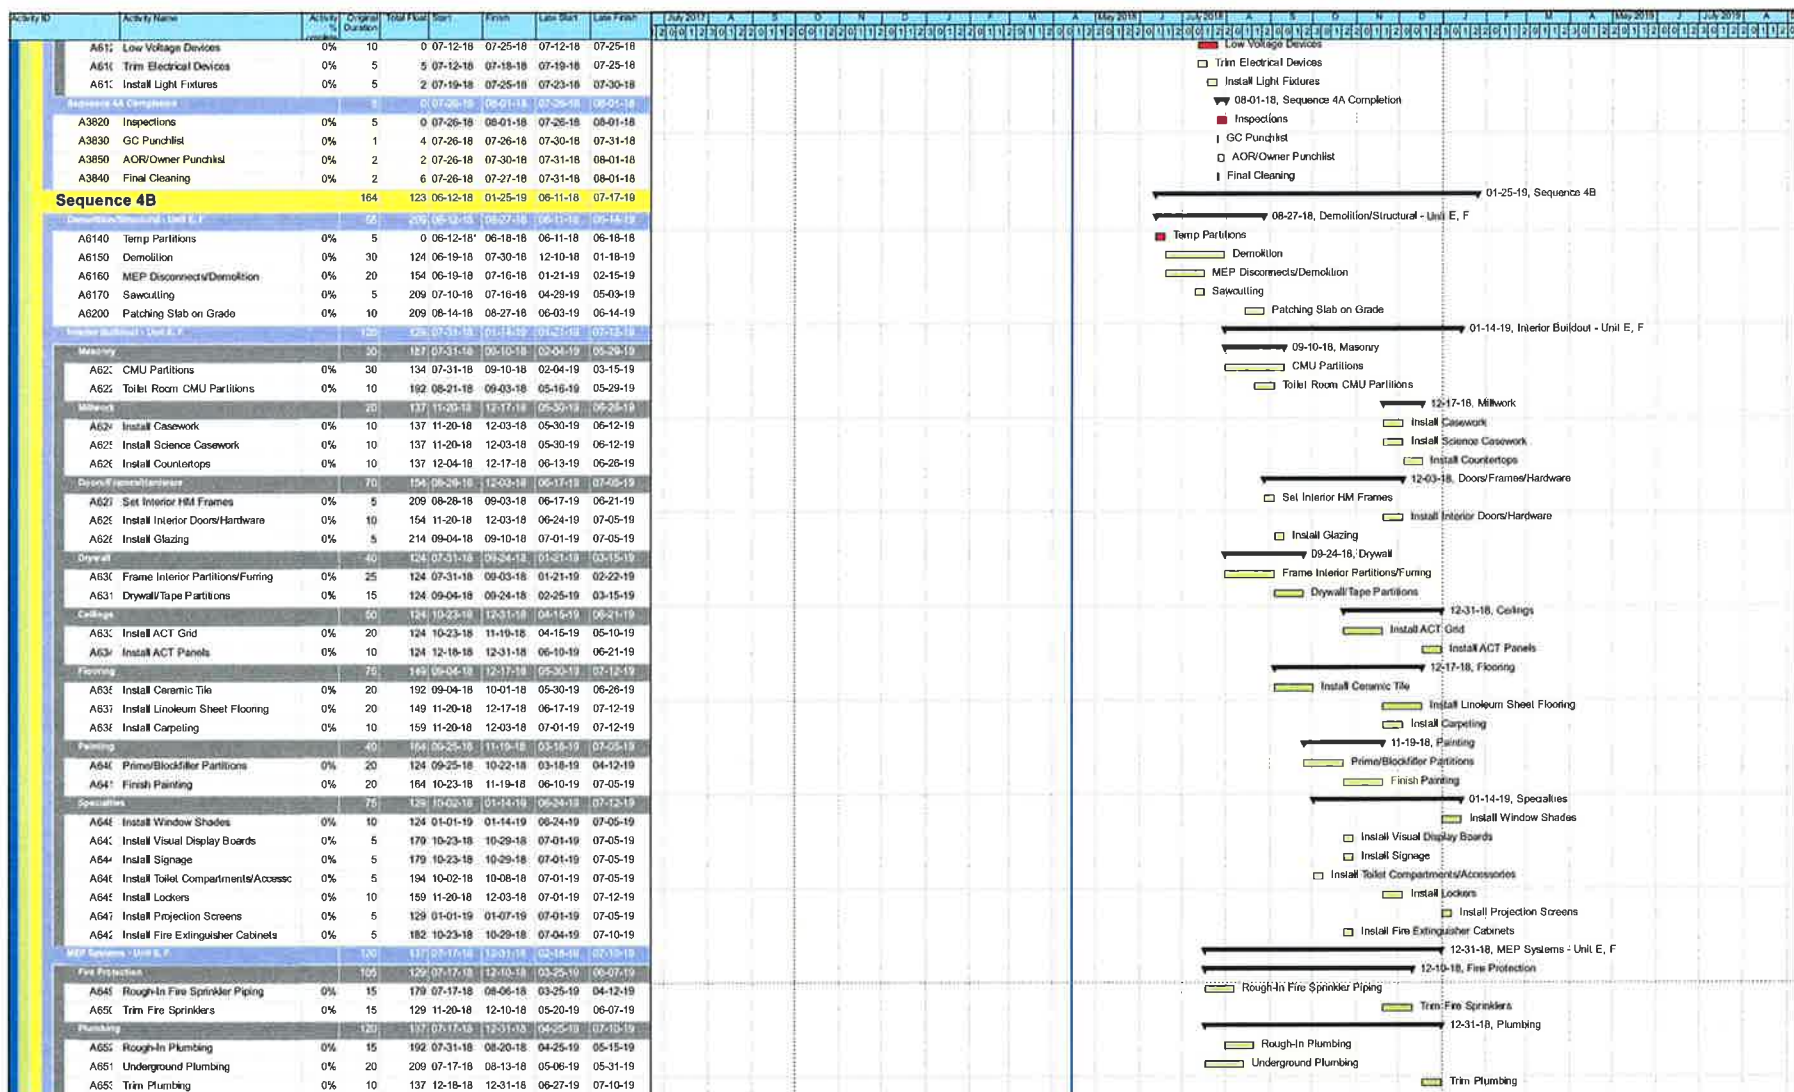


Run Date 04-19-18

Data Date 04-15-18

Page 10 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018



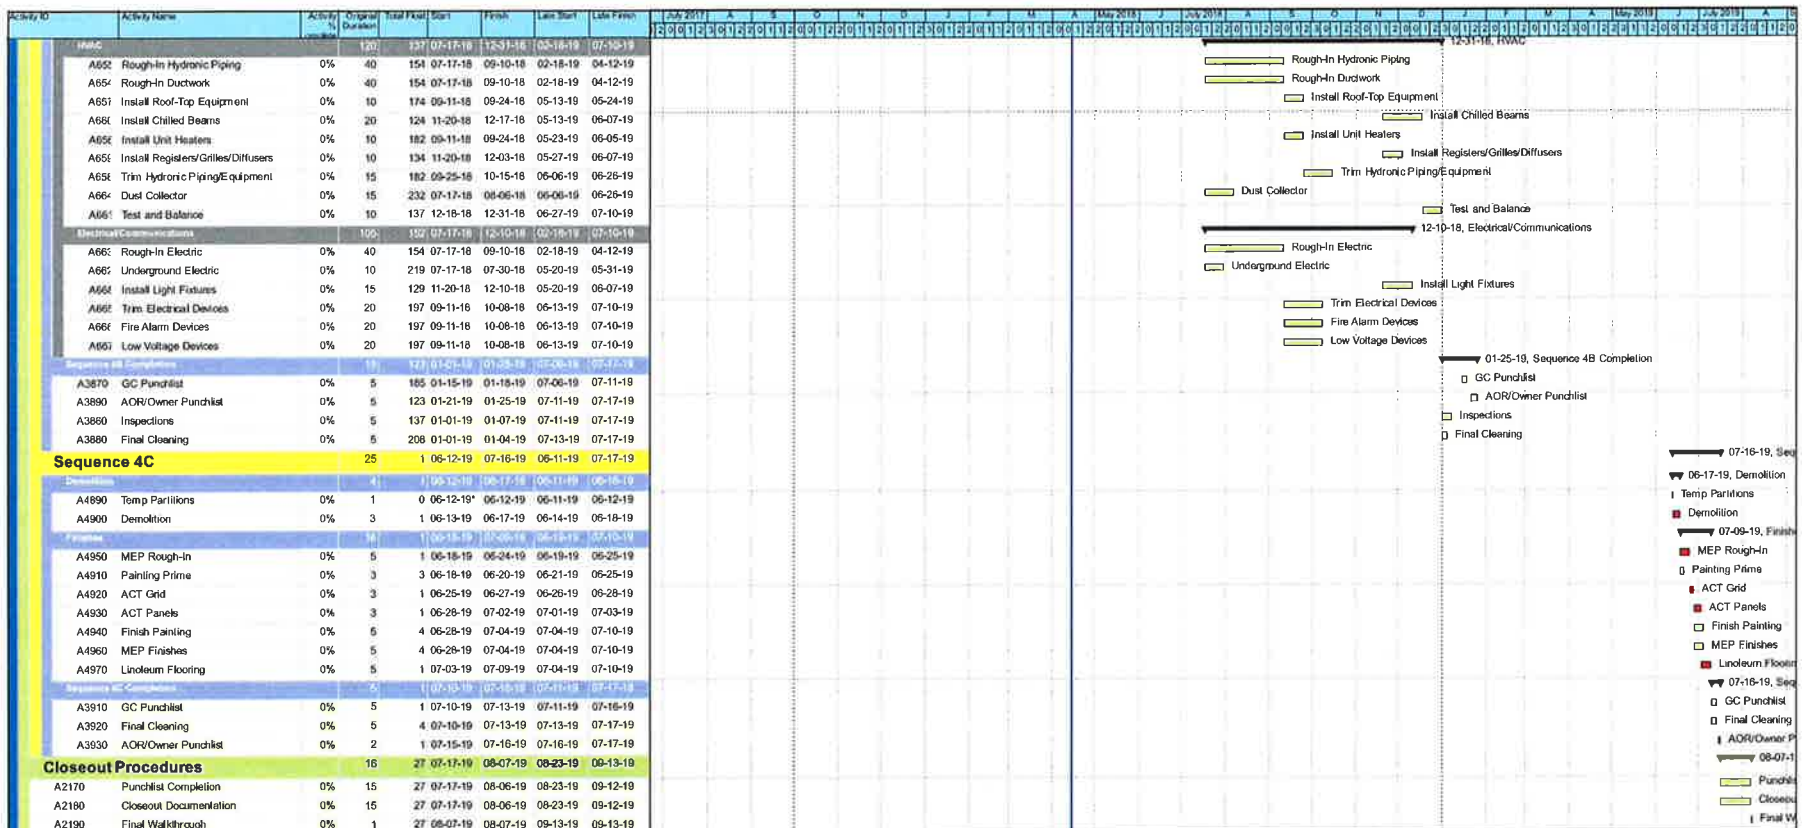

Run Date 04-19-18

Data Date 04-15-18

Page 11 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted April 19, 2018

