

Construction Status Update Report

March 2018

Thompson Middle School

Project Manager – Craig Lamp

Contractor – K.R. Miller Contractors, Inc.

Accomplishments

- Interior structural steel
- Taping of drywall has begun
- Air barrier, insulation and brick work
- Plumbing, HVAC, electrical and fire protection rough-ins ongoing
- Underground plumbing & electric in addition
- Kitchen masonry & wall framing installed
- Interior plaster patching @ kitchen & cafeteria
- Classroom addition foundation complete
- Loading dock foundation footings
- Cafeteria exterior windows installed

Schedule

Project on schedule

- Upcoming Milestones
 - Foundation work for locker room addition
 - Rework steel for kitchen/serving/cafeteria area
 - Structural steel @ north classroom addition
 - New water line into building over spring break
 - Begin interior painting
- Anticipated Completion Date: 8/15/19
- Status Meetings: Thursdays at 11:00 am in Thompson LRC Conference Room

Budget

Total Project Budget = \$47,100,000 (pre-bid) \$44,496,000 (post bid)

Contract to K.R. Miller \$36,724,550 + \$710,902 = \$37,435,452

KR Miller paid as of 3/1/18 = \$7,647,922.71

Change Orders

- Fully Executed
 - Change Order #1 \$400,013
 - Change Order #2 \$62,384
 - Change Order #3 \$248,505
- Approved in Process (Change Order #4)
 - Cafeteria ceiling revisions \$12,638
 - MCT flooring patterns \$0
 - Remove additional underground tank \$13,352
 - Revise steel 2nd floor cafeteria \$15,822
 - Remove buried concrete pad \$3,928
- Pending
 - Site work & parking revisions \$36,550
 - Chilled water piping \$13,894
 - Cafeteria/Kitchen modifications \$80,338
 - Additional windows @ west & north elevations \$66,365
 - Backflow preventer B141 \$8,720
 - Additional exterior windows \$66,365
 - Power/IT requirements \$23,431
 - Replace 2 existing columns @ cafeteria \$15,667
 - Add fritz tile in hall outside cafeteria \$31,425
 - Add fire pump \$67,510
 - Added safety goggle cabinets \$3,849
 - Parapet wall replacement \$51,178
 - Infill openings at duct \$9,262
 - Furring @ existing exterior walls T&M \$49,632
 - Infill opening 107 \$5,143
 - Retaining wall demo \$5,916
 - CUH-B2 RFI #86 \$7,745
 - RTU-4 rework per ASI #3 \$9,278
 - Chilled beams added after bid \$6,684
 - Fire sprinkler plan review \$788
 - Revised hardware finish \$11,025
 - Remove CMU between windows 1st & 2nd floor \$18,025
 - Outlet for water cooler B126 \$315
- Rejected
 - Sound door alternate manufacturer (\$31,300)

Progress Photos -

Removal of discovered unknown underground storage tank



Kitchen/Serving area wall framing



Wall framing & wood blocking @ Science and Prep Room




Abuse resistant drywall installation in classroom



Underground plumbing in addition



Air barrier, insulation, brick approved sample corner

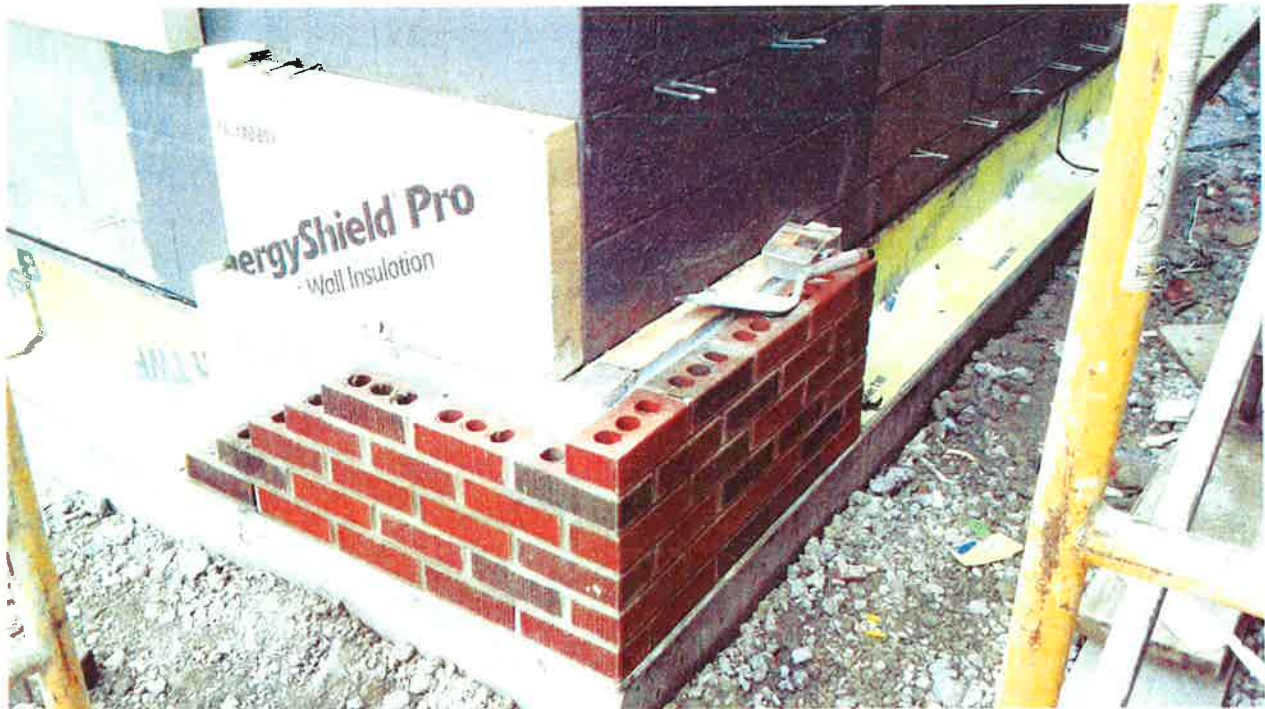

Kitchen area soffit framing



Air barrier installed, ready for insulation & brick 2/27/18



Last interior courtyard foundation wall forming



Start of brick installation



Brick work progress, south wall 3/5/18



Loading dock retaining wall framing



Final footing for addition poured



Interior steel installed to support Kitchen area



Drywall taping



Brick installation progress 3/13/18



Thompson Middle School
Change Order Summary Sheet

Total Projected Budget = \$44,496,000

#	Date Issued	Description	Status	Generated By (A,O,GC)	Cost	Final Determination
RFCOP #1	8/1/2017	Acoustic Windows @ Music Area	Rejected	Owner	\$18,900	Void
RFCOP #1(a)	8/1/2017	Acoustic Windows @ Music Area (Alt)	Approved	Owner	\$10,835	Change Order #1
RFCOP #2	8/25/2017	Replace Existing Hall Lockers	Rejected	Owner	\$23,063	Void
RFCOP #3	8/25/2017	Glass Marker Boards @ Science Rooms	Rejected	Owner	\$53,490	Void
RFCOP #4	9/6/2017	Extra Cabinetry Demolition	Approved	Architect	\$1,357	Change Order #1
RFCOP #5	9/15/2017	Sitework/Parking Lot Revisions	Approved	Architect	\$55,612	Change Order #1
RFCOP #6	9/20/2017	Revise Feeder to RTU 3	Approved	Architect	\$0	Change Order #1
RFCOP #7	10/2/2017	Existing Door 17 to Remain	Approved	Architect	(\$2,099)	Change Order #1
RFCOP #8	10/10/2017	Replace hall lockers E&F	Rejected	Owner	\$41,727	Void
RFCOP #9	10/10/2017	Site changes Bulletin #2	Approved	Architect	\$68,907	Change Order #2
RFCOP #10	10/10/2017	Site changes Bulletin #3	Pending	Architect	\$36,550	Repricing
RFCOP #11	10/24/2017	ERU VFD's	Approved	Architect	\$0	Change Order #2
RFCOP #12	10/26/2017	Chilled water piping	Pending	Architect	\$13,894	
RFCOP #13	11/6/2017	Revise wall tile	Approved	Architect	(\$4,050)	Change Order #3
RFCOP #14	11/8/2017	Renumber existing lockers	Approved	Owner	\$2,082	Change Order #2
RFCOP #15	11/8/2017	Revisions to FACS area	Approved	Architect	\$51,206	Change Order #2
RFCOP #16	11/10/2017	Band & Choir revisions	Approved	Architect/Owner	\$14,650	Change Order #2
RFCOP #17	11/9/2017	Cafeteria ceiling	Approved	Architect	\$12,638	Approved
RFCOP #18	11/8/2017	Added steel at front entry	Approved	Architect	\$7,079	Change Order #2
RFCOP #19	11/16/2017	VCT in Cafeteria	Approved	Architect/Owner	(\$35,216)	Change Order #2
RFCOP #20.1	11/16/2017	Marmoleum tile in Classrooms	Approved	Architect/Owner	(\$145,254)	Change Order #2
RFCOP #20.2	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$81,848)	Void
RFCOP #20.3	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$28,199)	Void
RFCOP #21	11/16/2017	Marmoleum tile in Corridors	Approved	Architect/Owner	(\$54,514)	Change Order #2
RFCOP #22	11/16/2017	VT in Cafeteria	Void	Architect/Owner	(\$6,000)	Void
RFCOP #23	11/16/2017	VT in Classrooms	Void	Architect/Owner	Void	Void
RFCOP #24	11/20/2017	Modify running track	Void	Architect/Owner	\$132,825	Void
RFCOP #24A	11/20/2017	Modify running track Alternate	Rejected	Architect/Owner	\$193,515	Void
RFCOP #25	11/20/2017	Prep field for turf	Approved	Architect/Owner	\$28,712	Change Order #2
RFCOP #26	11/20/2017	Toilet room B130 revision	Approved	Architect	28,534	Change Order #3

RFCOP #27	11/20/2017	Skylight shaft	Approved	Architect	\$9,175	Change Order #2
RFCOP #28	11/22/2017	Cafeteria/Kitchen modifications	Pending	Architect	\$80,338	
RFCOP #29	11/22/2017	Area B,C,D sanitary	Approved	Architect	\$15,854	Change Order #3
RFCOP #30	11/22/2017	Area B sanitary	Approved	Architect	\$9,455	Change Order #3
RFCOP #31	11/27/2017	Electric water cooler A108	Approved	Architect	\$8,801	Change Order #3
RFCOP #32	11/28/2017	Casework changes A114	Void	Architect	Void	Void
RFCOP #33	12/12/2017	Sensory room relocation	Approved	Architect/Owner	\$21,127	Change Order #2
RFCOP #34	12/7/2017	Delete sanitary to west addition	Approved	Architect	\$536	Change Order #2
RFCOP #35	12/15/2017	Additional exterior windows	Pending	Owner	\$66,365	
RFCOP #36	12/8/2017	Classroom mobile casework	Approved	Architect/Owner	\$33,643	Change Order #3
RFCOP #37	12/14/2017	Backflow preventer B141	Pending	Architect	\$8,720	
RFCOP #38	12/14/2017	New radiation room A112	Approved	Architect	\$7,809	Change Order #2
RFCOP #39	12/14/2017	Water cooler B205	Approved	Architect	\$4,850	Change Order #3
RFCOP #40	12/14/2017	New door to conf. rm. B	Approved	Owner	\$10,163	Change Order #3
RFCOP #41	1/8/2018	Power & IT requirements	Pending	Architect	\$23,431	
RFCOP #42	1/10/2018	Storefront finish	Approved	Architect	(\$4,037)	Change Order #2
RFCOP #43	1/12/2018	Reroute stormwater	Approved	Architect	\$3,439	Change Order #3
RFCOP #44	1/12/2018	Replace 2 existing columns	Pending	Architect	\$15,667	
RFCOP #45	1/12/2018	City water main revisions	Approved	City	\$6,441	Change Order #2
RFCOP #46	2/27/2018	Gym floor striping				
RFCOP #47	1/29/2018	Fritz tile	Pending	Owner/Architect	\$31,425	
RFCOP #48	1/30/2018	Subfloor patching/prep				T&M
RFCOP #49	1/30/2018	Fire pump	Pending	Architect	\$67,510	
RFCOP #50	Void	Void	Void	Void	Void	Void
RFCOP #51	Void	Void	Void	Void	Void	Void
RFCOP #52	2/12/2018	MCT floor patterns	Approved	Architect	\$0	Approved
RFCOP #53	2/19/2018	Emergency shower floor drains		Architect		
RFCOP #54	2/16/2018	Revise tempered water		Architect		
RFCOP #55	2/14/2018	Frosted glass @ Science rooms	Approved	Architect	\$657	Change Order #3
RFCOP #56	2/14/2018	Water cooler A106 & A127		Architect		
RFCOP #57	2/15/2018	Ceiling modifications B140 & B141	Approved	Architect	\$4,088	Change Order #3
RFCOP #58	2/15/2018	Modify existing light wells		Architect		
RFCOP #59	2/16/2018	Safety goggle cabinets	Pending	Architect	\$3,849	
RFCOP #60	2/21/2018	B213 mechanical chase		Architect		

RFCOP #61	2/21/2018	Sensory room/tech room revisions		Architect		
RFCOP #62	2/21/2018	Band/Orchestra exterior windows		Architect		
RFCOP #63	2/21/2018	Science B213 wall modification		Architect		
RFCOP #64	2/27/2018	Locker revision		Architect		
RFCOP #65	2/27/2018	Marker board modifications		Architect		
RFCOP #66	3/6/2018	Cafeteria ceiling tile revision		Architect		
COR #1	9/20/2017	Remove & Replace 2 Existing Manholes	Approved	Katco/RFI	\$15,462	Change Order #1
COR #2	9/27/2017	Remove & Replace Water Lines Corr 108	Approved	Owner	\$28,175	Change Order #1
COR #3	10/4/2017	Lintel Replacement	Approved	Iwanski/Architect	\$97,818	Change Order #1
COR #4	10/4/2017	Parapet Wall Replacement	Pending	Iwanski/Architect	\$51,178	\$258,021 T&M NTE
COR #5	11/6/2017	Mezzanine demolition RFI #47	Approved	Miller/RFI	\$7,482	Change Order #2
COR #6		New chase walls RFI #5	Void	Void	Void	Void
COR #7	11/4/2017	Barrier curb removal RFI #7&8	Approved	Miller/RFI	\$9,075	Change Order #1
COR #8	11/1/2017	Remove floor substrate RFI #19	Approved	Miller/RFI	\$6,795	Change Order #1
COR #9	11/4/2017	Revised ramp curb detail RFI #20	Approved	Miller/RFI	\$427	Change Order #1
COR #10	11/4/2017	Revised foundation wall detail RFI #21	Approved	Miller/RFI	\$1,573	Change Order #1
COR #11	2/23/2018	Infill openings @ duct RFI #27	Pending	Miller/RFI	\$9,262	
COR #12	11/4/2017	Concrete infills RFI #30&73	Approved	Miller/RFI	\$5,008	Change Order #1
COR #13	11/28/2017	Demolition of LBP RFI #35	Approved	Miller/RFI	(\$5,432)	Change Order #2
COR #14	1/3/2018	Remove blower motor	Approved	Miller/RFI	\$3,584	Change Order #2
COR #15	11/28/2017	Furring @ exterior walls RFI #45,46&70	Pending	Miller/RFI	\$49,634	T&M
COR #16		Sump pit @ elevator RFI #52	Void	Void	Void	Void
COR #17		Revise mezz wall construction RFI #53	Void	Void	Void	Void
COR #18	11/3/2017	Brick ledge @ retaining wall RFI #54&57	Approved	Miller/RFI	\$1,879	Change Order #1
COR #19	2/22/2018	Demo conc. wall in lieu of mas. RFI #55	Approved	Miller/RFI	\$2,986	Change Order #3
COR #20		Chilled water piping RFI #58	Void	Void	Void	Void
COR #21		Floor underlayment RFI #64	Void	Void	Void	Void
COR #22		Undercuts per Oz Engineering				
A	11/3/2017	Pond #1 9/15 - 9/17	Approved	Oz Engineering	\$66,776	Change Order #1
B	11/3/2017	Report #24 & #28	Approved	Oz Engineering	\$36,924	Change Order #1
C	11/3/2017	Report #38, #40 & #44	Approved	Oz Engineering	\$16,932	Change Order #1

D	11/3/2017	Report #48, #52 & #58	Approved	Oz Engineering	\$44,880	Change Order #1
E	11/3/2017	Report #73 & #81	Approved	Oz Engineering	\$2,584	Change Order #1
F	11/21/2017	Report 11/1/17, 11/2/17	Approved	Oz Engineering	\$11,900	Change Order #2
G	11/21/2017	Report 11/6/17 - 11/11/17	Approved	Oz Engineering	\$53,924	Change Order #2
H	12/18/2017	Report 11/13/17 - 11/25/17	Approved	Oz Engineering	\$6,392	Change Order #3
I	12/18/2017	Report 11/27/17 - 12/2/17	Approved	Oz Engineering	\$62,356	Change Order #3
J						
K						
COR #23	11/3/2017	Drain tile @ retaining wall RFI #77	Approved	Miller/RFI	\$8,139	Change Order #2
COR #24		Roof parapet replacement	Void	Void	Void	Void
COR #25	11/28/2017	Electric cost above allowance	Approved	Miller/Allowance	\$1,700	Change Order #2
COR #26	1/3/2018	Manhole 33 to parkway	Approved	Rettler	\$41,447	Change Order #3
COR #27		Hot and chilled water ERU-6	Void	Void	Void	Void
COR #28		Piping to VAV	Void	Void	Void	Void
COR #29	2/2/2018	Kitchen piping revisions	Approved	Miller/RFI	\$2,768	Change Order #3
COR #30	2/22/2018	Coal shoot infill @ courtyard	Approved	Miller/RFI	\$2,082	Change Order #3
COR #31	2/23/2018	Deadwall revisions	Approved	Miller/RFI	\$693	Change Order #3
COR #32	2/23/2018	Infill opening 107	Pending	Miller/RFI	\$5,143	
COR #33	2/23/2018	Retaining wall demo	Pending	Miller/RFI	\$5,916	
COR #34	2/2/2018	CR Leonard RFI #109	Approved	Miller/RFI	\$6,450	Change Order #3
COR #35	2/2/2018	Additional piping RFI #115	Approved	Miller/RFI	\$1,680	Change Order #3
COR #36	12/22/2017	Remove T&G flooring room 107A	Approved	Miller/RFI	\$2,602	Change Order #2
COR #37		Waterline revision per City	Void	Void	Void	Void
COR #38		Void	Void	Void	Void	Void
COR #39	2/22/2018	ASI #10	Approved	Architect	\$2,,300	Change Order #3
COR #40	1/31/2018	Sound door & frames to match window	Rejected	Miller	(\$31,300)	Rejected
COR #41	2/23/2018	CUH-B2 RFI #86	Pending	Miller/RFI	\$7,745	
COR #42	2/2/2018	ASI #9 ductwork B212	Approved	Architect	\$3,918	Change Order #3
COR #43	2/2/2018	ASI #3 RTU-4	Pending	Architect	\$9,278	
COR #44	2/23/2018	Chilled beams added after bid	Pending	Miller/RFI	\$6,684	
COR #45	2/21/2018	Fire sprinkler plan review	Pending	Miller	\$788	
COR #46	3/6/2018	Hardware finish	Pending	Miller/RFI	\$11,025	
COR #47	3/8/2018	Remove additional UG tank	Approved	Miller	\$13,352	Approved
COR #48	3/8/2018	Remove CMU @ windows	Pending	Architect	\$18,025	ATS&R to reimburse

COR #49	3/8/2018	Revise steel 2nd floor cafeteria	Approved	Architect	\$15,822	Approved
COR #50	3/8/2018	Outlet for water cooler B126	Pending	Architect	\$315	
COR #51	3/8/2018	Remove burried conc pad water line	Approved	Miller	\$3,928	Approved
			Change Order #1		\$400,013	
			Change Order #2		\$62,384	
			Change Order #3		\$248,505	
			Approved Changes		\$45,740	
			Pending Changes		\$522,742	
			Total Changes		\$1,279,384	
			Rejected Changes		\$299,395	

Thompson Middle School					%
K.R. Miller Contract				\$36,724,550.00	
		Change Order #1		\$400,013.00	
		Change Order #2		\$62,384.00	
		Change Order #3		\$248,505.00	
	Paid to Date	Pay App 1		-670,788.90	
		Pay App 2		-691,703.10	
		Pay App 3		-1,251,562.50	
		Pay App 4		-1,696,042.75	
		Pay App 5		-2,269,936.97	
		Pay App 6		-1,067,888.49	
		Balance Due		\$29,787,529.29	80%
	Contingency Allocation			\$ 2,500,000.00	
	Signed Change Orders				
		Change Order #1		\$ 400,013.00	
		Change Order #2		\$62,384	
		Change Order #3		\$248,505	
	Pending Change Orders			\$ 568,482.00	
	Remaining Contingency			\$ 1,220,616.00	49%

DATE March 8, 2018

PROJECT Thompson Middle School Additions and Alterations

SUBJECT Construction Meeting

PRESENT School District #303
Craig Lamp
Seth Chapman

K.R. Miller
Robert Richards
Michael Cwienkala
Paul Ingraham
Cody LaBeck

City of St. Charles
Rainier Galliano
Jeff Stengler

ATS&R
Stewart Haugen

BY Stewart Haugen

1. PROGRESS SCHEDULE / LOOK AHEAD:

- a. Site work proceeding more quickly, weather more cooperative.
- b. Continuation of exterior steel erection to begin week of 03.18.
- c. Phone vendor continues to work on relocating/ replacing land lines.
- d. Unit B basement columns (under first floor kitchen area) being installed.
- e. Unit C loading dock/retaining wall and foundation work continuing. Pier footings completed.
- f. Unit D Concrete Masonry Unit installation continuing.
- g. Unit D plumbing second floor plumbing sleeves being installed.
- h. Unit D first floor bed being prepped for receipt of S.O.G.
- i. Unit D air / moisture barrier and face brick installation continuing.
- j. Unannounced arrival of the gas company to install new service this week.
- k. MEP rough-ins continuing in Units A and B. Insulating ductwork and piping continues.
- l. Drywall installation continuing. Taping and priming to begin next week.
- m. Units A and B existing windows field measuring complete.
- n. Unit B field measuring for science room countertops being completed.

- o. Units A and B existing windows field measured.
- p. Concrete contractor working overtime to make up for delays caused by inclement weather & unforeseen conditions.
- q. Plaster patching continues.
- r. Flooring substrate remedial work continuing.

2. SUBMITTALS:

- a. Shop Drawings - approximately 8 items to be reviewed/ resubmitted.

3. REQUEST FOR INFORMATION (RFI):

- a. 1-170 issued to date.

4. CHANGES IN THE WORK (ASI, RFCOP):

- a. RFCOPs: 1-66 issued to date.
- b. ASIs: 1-16 issued to date.
- c. CORs: 1-51 issued to date.

5. BUILDING ACCESS:

- a. No issues.

6. OLD BUSINESS:

- a. Room B133B will, in addition to storing cafeteria furniture, house an MDF cabinet. ATS&R will investigate the need for anti-static treatment of the finish flooring.
- b. The district expressed interest in having the first floor new light well access panels, which open into the adjacent staircases, be transparent. ATS&R will generate an RFCOP for this item.
- c. Due to different existing conditions becoming apparent, the new chase in the southwest corner of Room B213 will be revised and the goggle cabinet will be located on the south, rather than the west wall. KR Miller will issue an RFI.
- d. ATS&R to follow up on the State Plumbing Inspector's comment regarding bathroom accessibility.
- e. Due to different existing conditions becoming apparent, the partition between rooms B218 and 219 has been constructed in a slightly different configuration than as shown on the floor plan. KR Miller has provided as-built dimensions and ATS&R will both review the seating layout and issue an ASI to reflect the new ceiling plan in each room.

7. NEW BUSINESS:

- a. Room B133B will, in addition to storing cafeteria furniture, house an MDF cabinet. KR Miller will research costs for anti-static treatment of the finish flooring.
- b. The District expressed interest in having the first floor new light well access panels, which open into the adjacent staircases, be transparent. ATS&R will provide a list of assemblies and materials to KR Miller for cost research.
- c. Electrician to investigate rerouting of power for locker room addition. ATS&R to assist/ review as requested.
- d. ATS&R will explore an option to have the new fire pump placed on an exterior concrete slab adjacent to the west wall of Unit A. This may become a more cost effective option than placing the pump in existing Mechanical Room A124, on the east side of Unit A.
- e. Both Change Order #3 and Pay Application #7 have been approved.

8. The next Construction Meeting is on Thursday, March 15, 2018 at 11:00 AM in Conference Room A120.

These notes represent the author's understanding of items discussed and decisions made at this meeting. Any comments or corrections should be forwarded to ATS&R within seven (7) days.

OSH:af

cc: All Present, CUSD #303 – Dr. Pearson

Encl: KR Miller - Three Week Look Ahead Schedule (03.01.2018).



Three Week Look Ahead Schedule

Project: Thompson Middle School Additional and Alterations
705 West Main Street
St. Charles, IL 60174

Architect: ATS&R
8501 Golden Valley Road, Suite 300
Minneapolis, MN 55427
AOR Project No. 16045

Contractor: K.R. Miller Contractors, Inc.
1624 Colonial Parkway
Inverness, IL 60067

Submitted: March 1st, 2018

Last Week							Subcontractor	Activity	Current Week							Week 2							Week 3										
Week Ending 03/04/18									Week Ending 03/11/18							Week Ending 03/18/18							Week Ending 03/25/18										
M	T	W	Th	F	Sa	Su			M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su				
2/27	2/28	3/1	3/2	3/3	3/4	3/5			3/6	3/7	3/8	3/9	3/10	3/11	3/12	3/13	3/14	3/15	3/16	3/17	3/18	3/19	3/20	3/21	3/22	3/23	3/24	3/25	3/26				
							Construction Junction	Earthwork (Weather Dependant)																									
x	x	x	x	x			Construction Junction	Excavation for Foundations (Bldg C & D, Weather Dependant)							x	x	x			x	x	x	x	x			x	x	x	x	x		
							Construction Junction	Excavation for Foundations (Bldg G, Weather Dependant)												x	x	x	x	x			x	x	x	x	x		
x	x	x	x	x	x		K.R. Miller	Concrete Footings and Foundations (Bldg C & G)							x	x	x	x	x			x	x	x	x	x			x	x	x		
							Iwanski Masonry	Exterior CMU Walls (Bldg D)							x	x	x	x	x			x	x	x	x	x			x	x	x		
x	x	x	x	x	x		Iwanski Masonry	Air and Vapor Barrier							x	x				x	x	x	x	x			x	x	x	x	x		
x	x	x	x	x	x		Iwanski Masonry	Exterior Cavity Walls (Bldg C & D)							x	x				x	x	x	x	x			x	x	x	x	x		
							Synergy Steel	Structural Steel (Bldg B)										x	x														
							Synergy Steel	Structural Steel (Bldg D)																									
							Synergy Steel	Structural Steel (Bldg C)												x	x	x	x	x			x	x	x	x	x		
x	x	x	x	x			C.R. Leonard	Plumbing Underground (Bldg D)							x	x	x	x	x														
x	x	x	x	x			Kalco Development	Site Storm Sewer, Water Main (Weather Dependant)							x	x	x	x	x			x	x	x	x	x			x	x	x		
x	x	x	x	x			Iwanski Masonry	Interior CMU Partitions (Bldg A & B)																									
x	x	x	x	x			L.J. Morse	Partition Walls - Framing (As Needed in Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x		
x	x	x	x	x			C.R. Leonard	Plumbing Rough-In (Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x		
x	x	x	x	x			L.J. Morse	Partition Walls - Drywall (As Needed in Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x		
							L.J. Morse	Taping Partition Walls (Bldg A + B)												x	x	x	x	x			x	x	x	x	x		
							Q.C. Enterprises	Underlayment (Bldg B)																					x	x	x	x	x
x	x	x	x	x			Commercial Mechanical	Ductwork Rough-In (Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x	x	x
x	x	x	x	x			Commercial Mechanical	Ductwork Insulation (Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x	x	x
x	x	x	x	x			Commercial Mechanical	Hydronic Piping (Bldg A & B)							x	x	x	x	x			x	x	x	x	x			x	x	x	x	x
x	x	x	x	x			Kellenberger Electric	Electrical Rough-In (Bldg A&B)							x	x	x	x	x			x	x	x	x	x			x	x	x	x	x
x	x	x	x	x			Skyline Plaster	Plaster Repair (Bldg B)																				x	x	x	x	x	
							HDS	Painting																				x	x	x	x	x	



Three Week Look Ahead Schedule


Project: Thompson Middle School Additional and Alterations
705 West Main Street
St. Charles, IL 60174

Contractor: K.R. Miller Contractors, Inc.
1624 Colonial Parkway
Inverness, IL 60067

Architect: ATS&R
8501 Golden Valley Road, Suite 300
Minneapolis, MN 55427
AOR Project No. 16045

Submitted: March 15th, 2018

Last Week								Subcontractor	Activity	Current Week								Week 2						Week 3													
Week Ending 03/11/18										Week Ending 03/18/18								Week Ending 03/25/18						Week Ending 04/01/18													
M	T	W	Th	F	Sa	Su				M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su
3/6	3/7	3/8	3/9	3/10	3/11	3/12									3/13	3/14	3/15	3/16	3/17	3/18	3/19			3/20	3/21	3/22	3/23	3/24	3/25	3/26	3/27	3/28	3/29	3/30	3/31	4/1	4/2
								Construction Junction	Earthwork (Weather Dependant)															x	x	x	x	x			x	x	x	x	x		
x	X	x	X	X				Construction Junction	Excavation for Foundations (Bldg C & D, Weather Dependant)		x	x	x										x	x	x	x	x			x	x	x	x	x			
				x				Construction Junction	Excavation for Foundations (Bldg G, Weather Dependant)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
x	X	x	X	X				K.R. Miller	Concrete Footings and Foundations (Bldg C & G)		x	x	x	x	x																						
								K.R. Miller	Concrete Slabs (C+D)					x									x	x	x	x	x			x	x	x	x	x			
								Iwanski Masonry	Exterior CMU Walls (Bldg D)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
x	x	x	x	x				Iwanski Masonry	Air and Vapor Barrier														x	x	x	x	x			x	x	x	x	x			
x	x	x	x	x				Iwanski Masonry	Exterior Cavity Walls (Bldg C &D)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
				x				Synergy Steel	Structural Steel (Bldg B)		x	x	x	x	x								x	x													
								Synergy Steel	Structural Steel (Bldg D)																												
								Synergy Steel	Structural Steel (Bldg C)														x	x	x	x	x			x	x	x	x	x			
x	x	x	x	x				C.R. Leonard	Plumbing Underground (Bldg D)		x	x	x	x	x																						
X	X	X	X	X				Katco Development	Site Storm Sewer, Water Main (Weather Dependant)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				Iwanski Masonry	Interior CMU Partitions (Bldg A & B)																												
X	X	X	X	X				L.J. Morse	Partition Walls - Framing (As Needed in Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				C.R. Leonard	Plumbing Rough-In (Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				L.J. Morse	Partition Walls - Drywall (As Needed in Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
								L.J. Morse	Taping Partition Walls (Bldg A + B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
								Q.C. Enterprises	Underlayment (Bldg B)																					x	x	x	x	x			
X	X	X	X	X				Commercial Mechanical	Ductwork Rough-In (Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				Commercial Mechanical	Ductwork Insulation (Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				Commercial Mechanical	Hydronic Piping (Bldg A & B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
X	X	X	X	X				Kellenberger Electric	Electrical Rough-In (Bldg A&B)		x	x	x	x	x								x	x	x	x	x			x	x	x	x	x			
x	x	x	x	x				Skyline Plaster	Plaster Repair (Bldg B)																					x	x	x	x	x			
								HDS	Painting																					x	x	x	x	x			

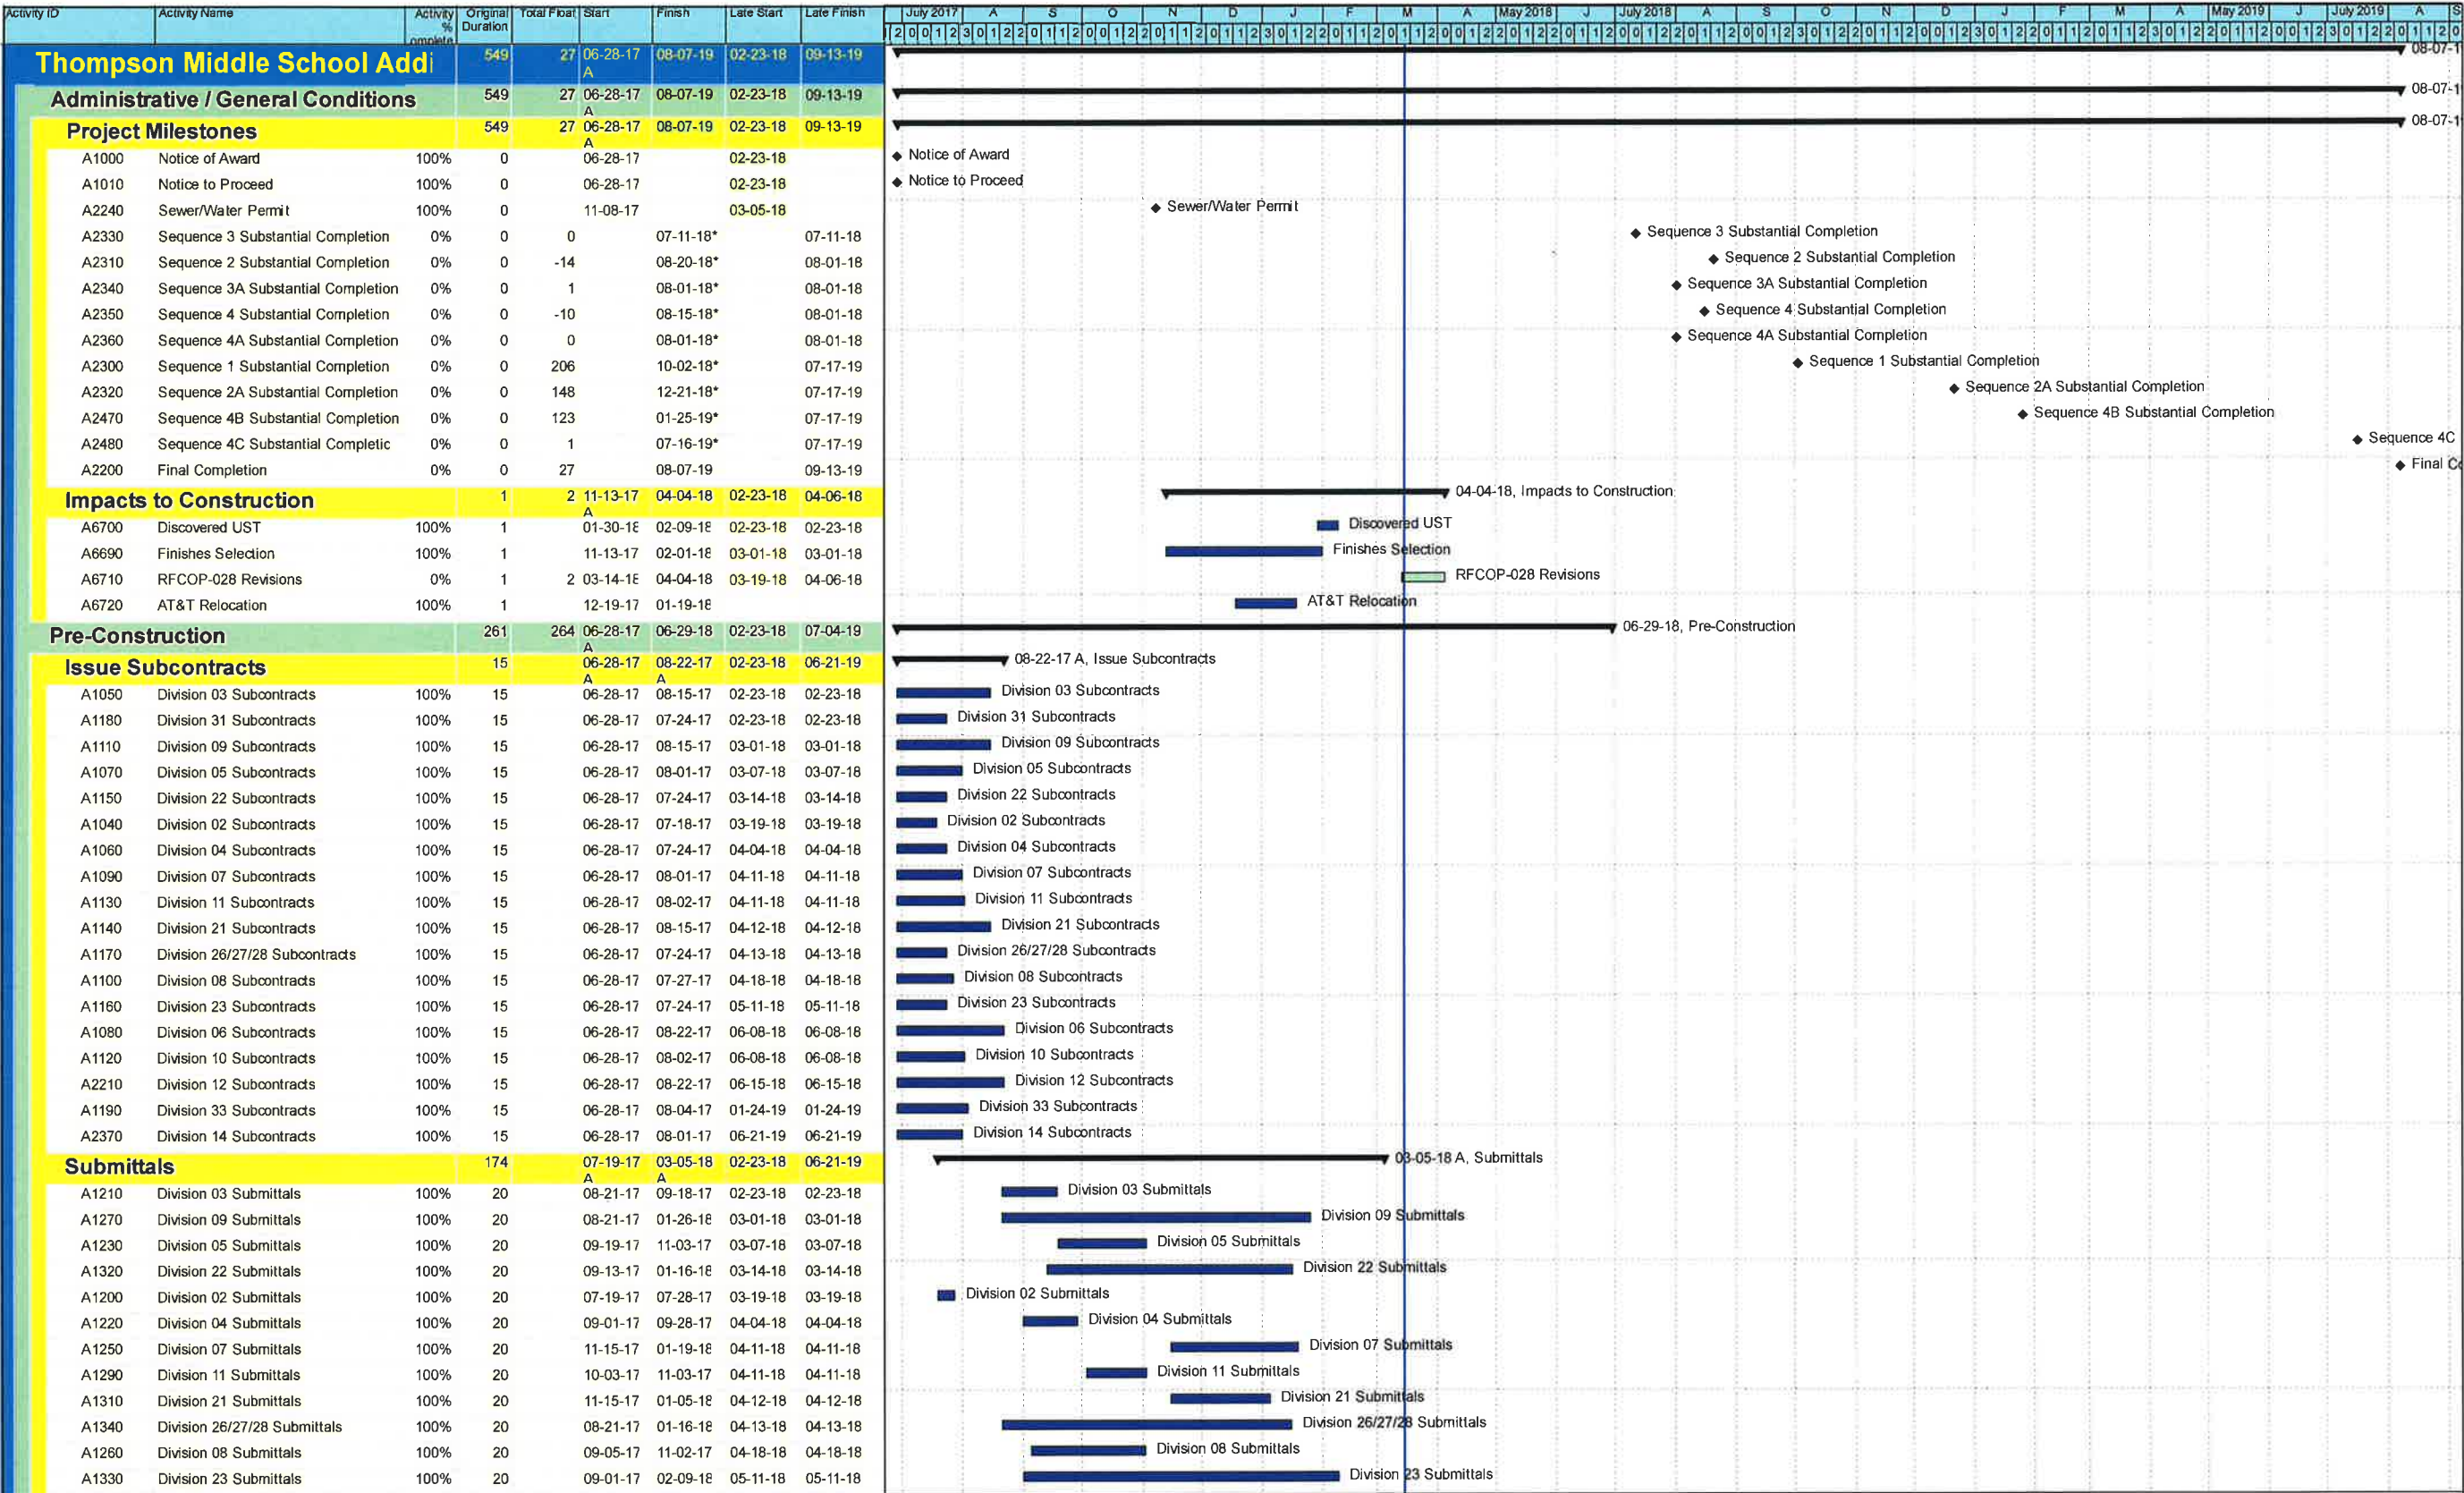


Run Date 03-14-18

Data Date 03-15-18

Page 1 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



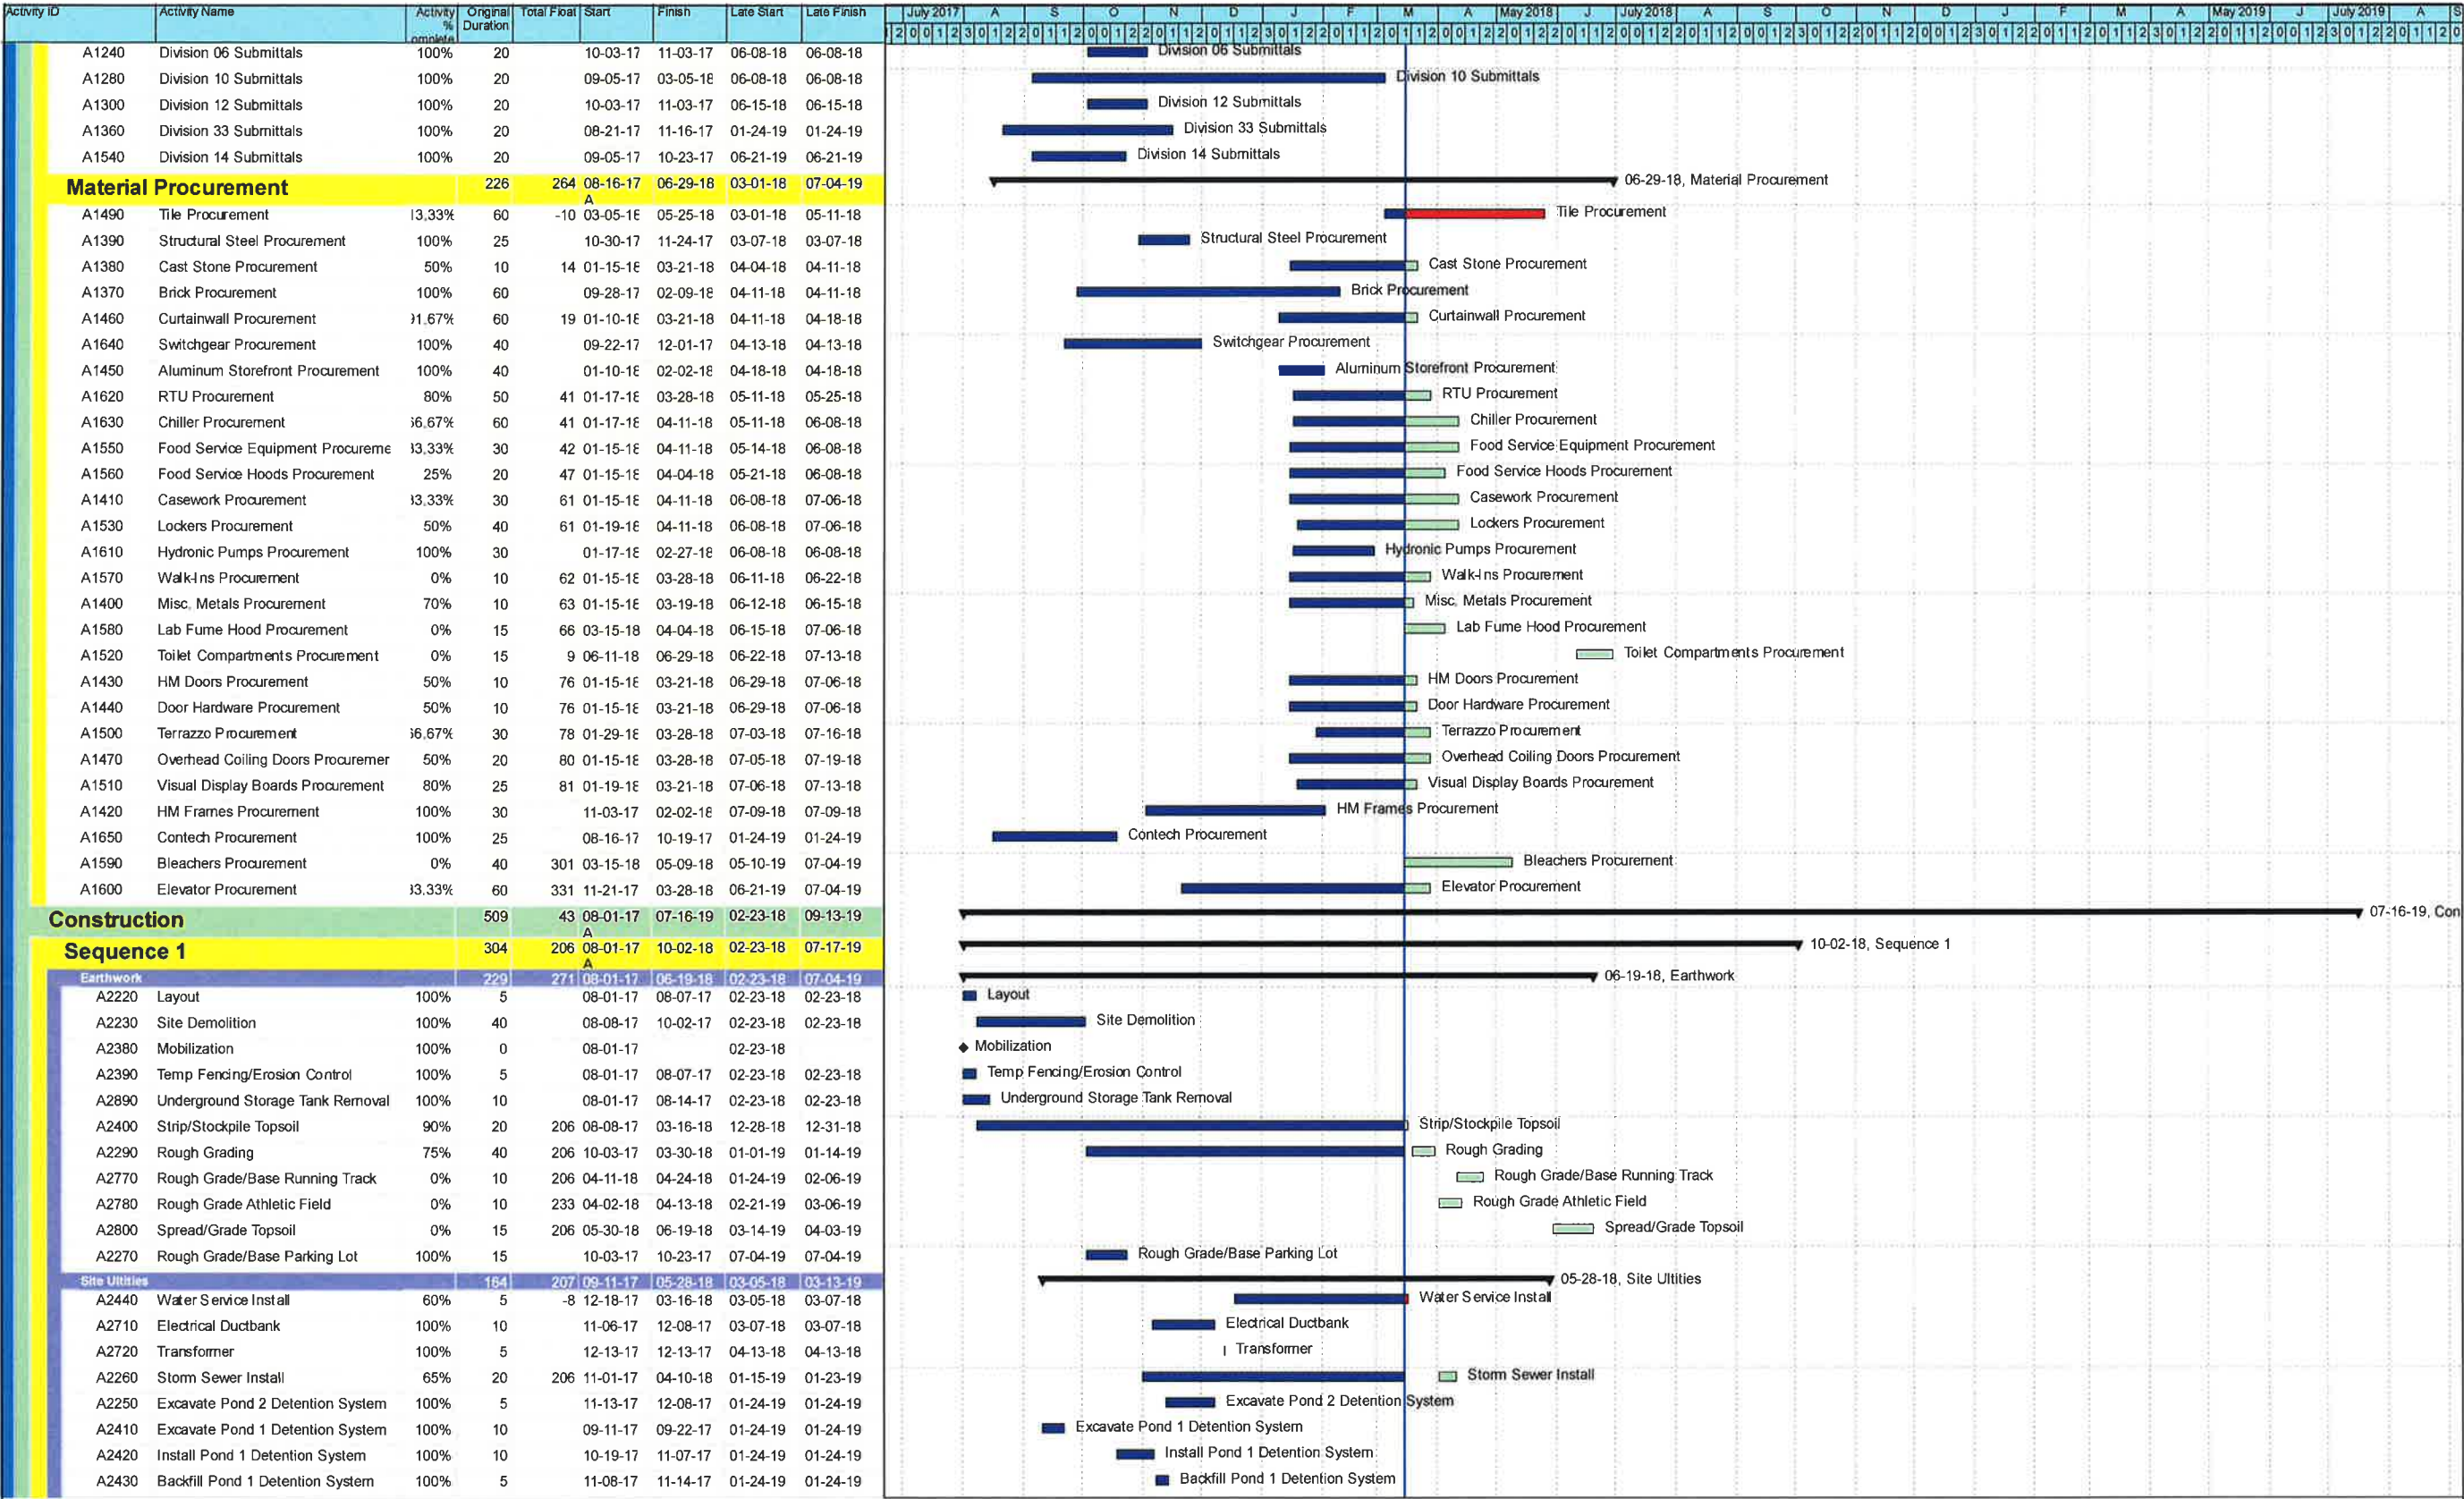


Run Date 03-14-18

Data Date 03-15-18

Page 2 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



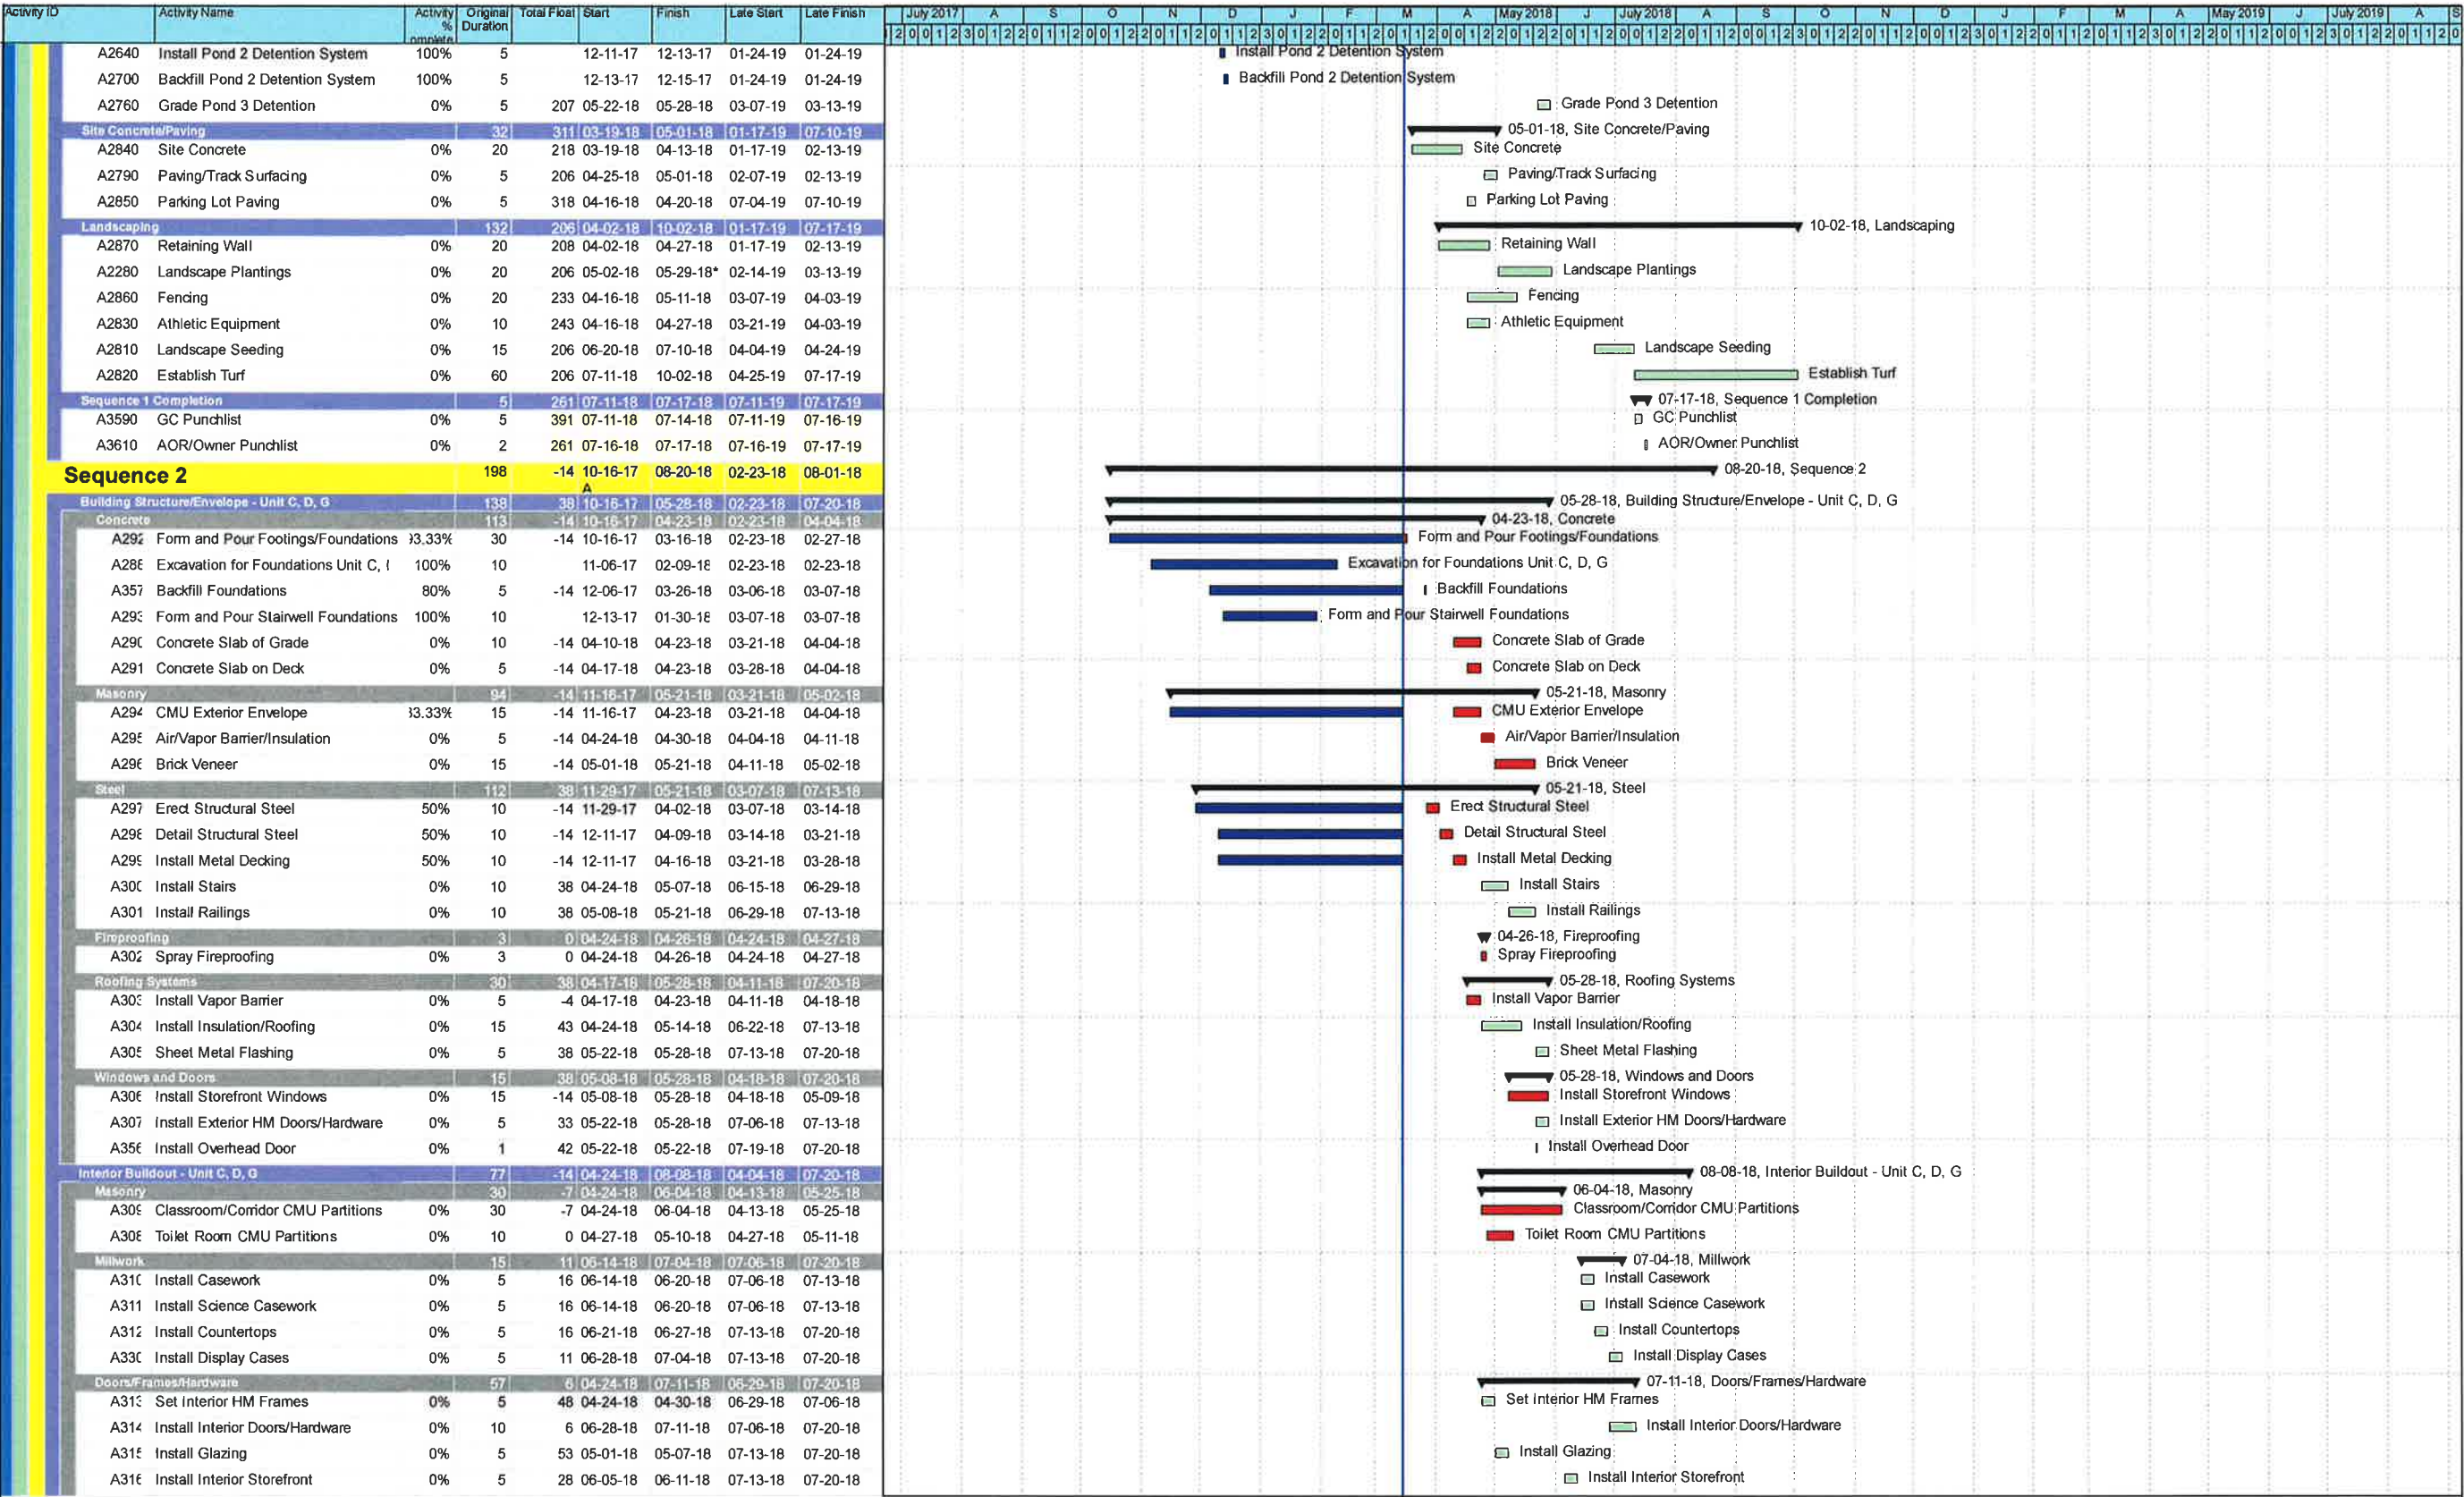


Run Date 03-14-18

Data Date 03-15-18

Page 3 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



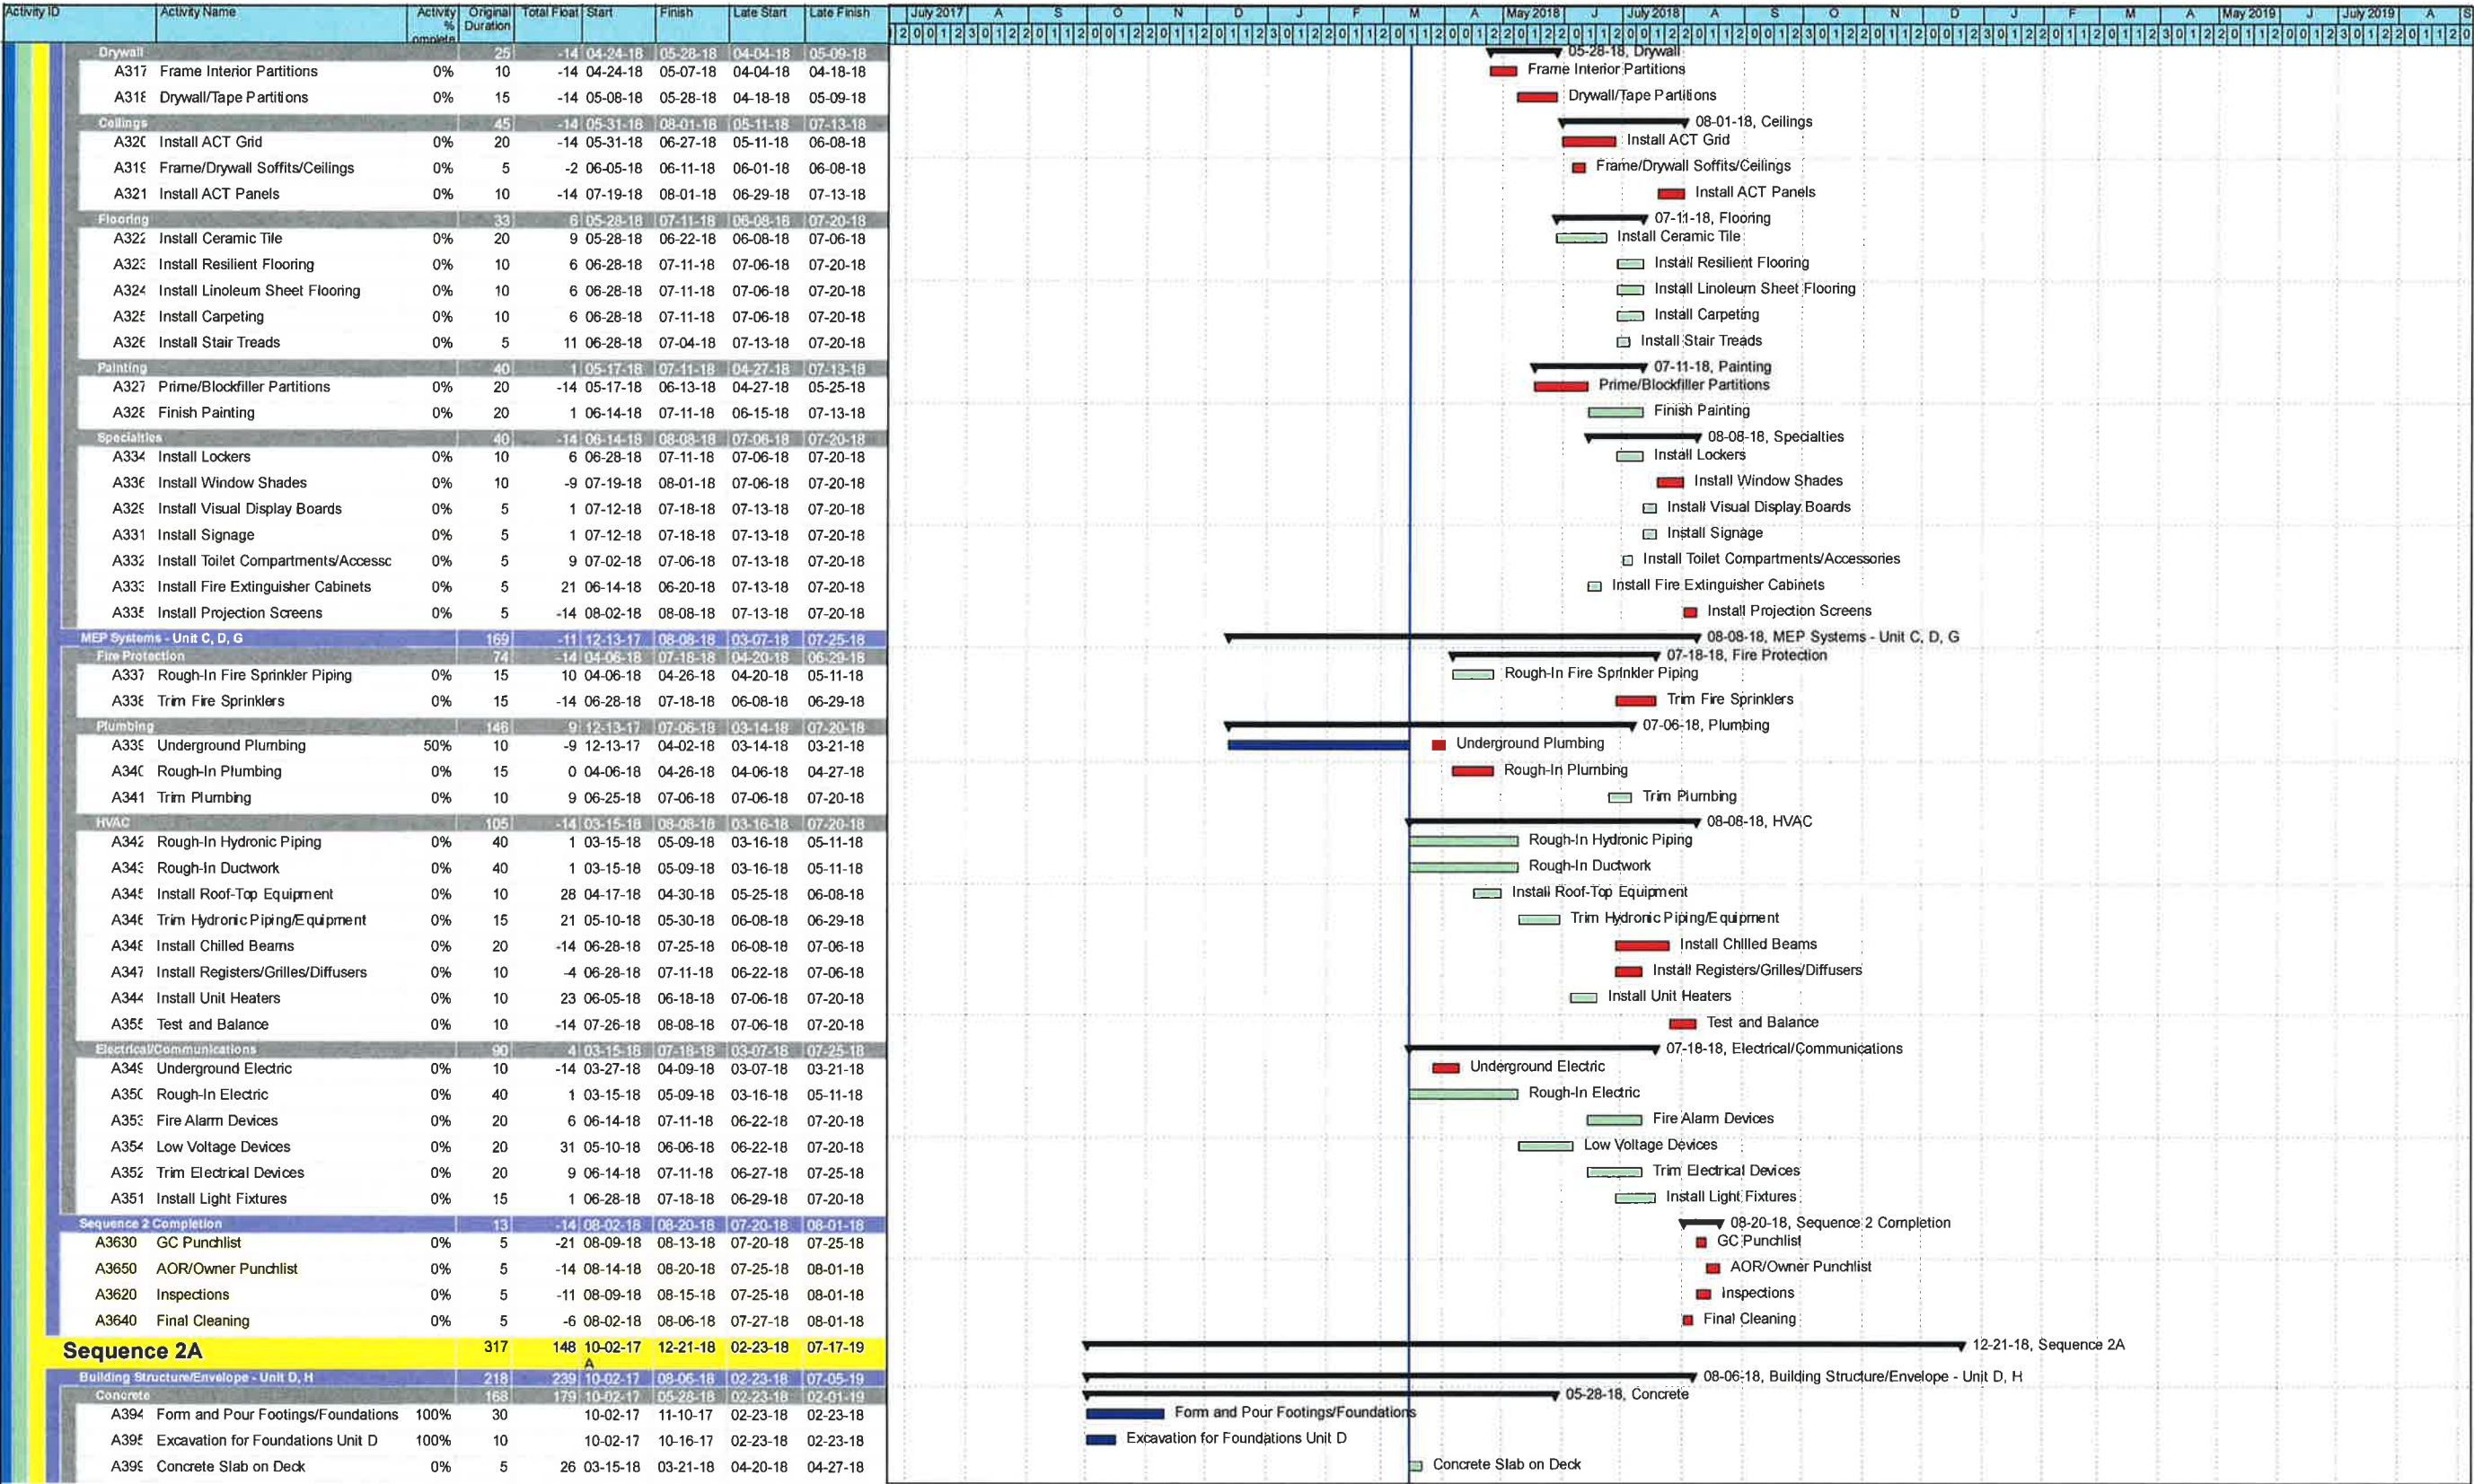


Run Date 03-14-18

Data Date 03-15-18

Page 4 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



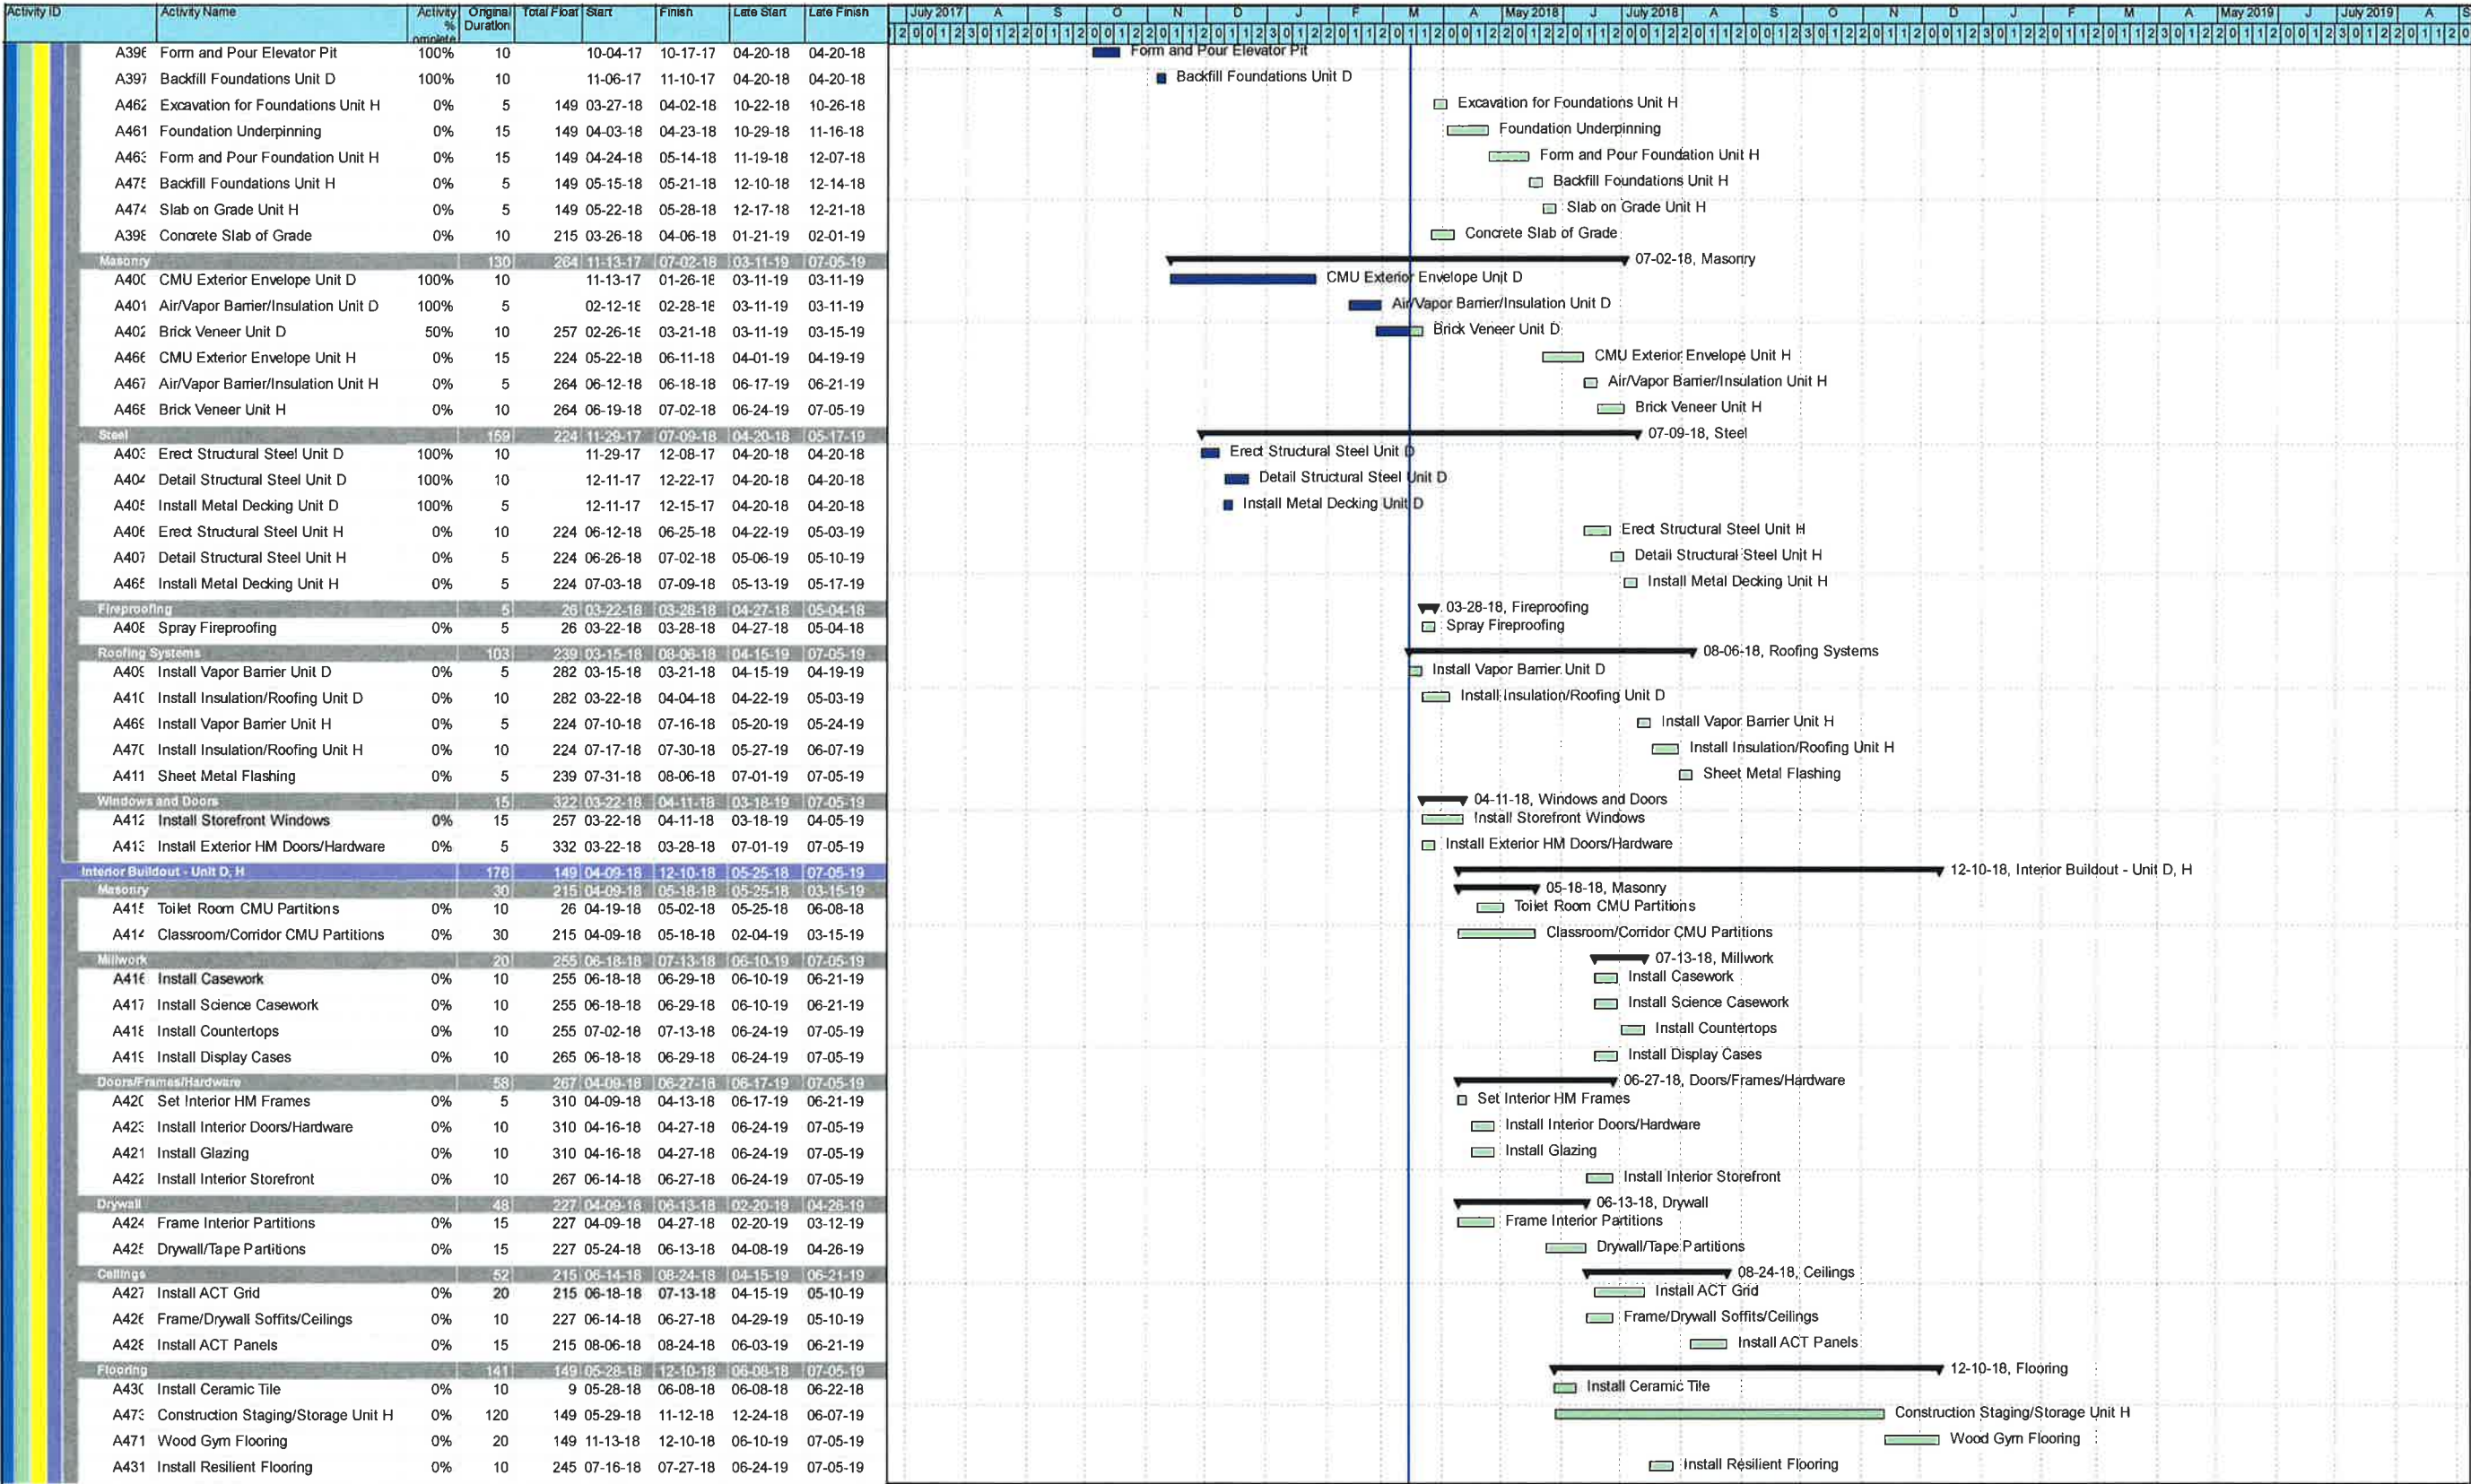


Run Date 03-14-18

Data Date 03-15-18

Page 5 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



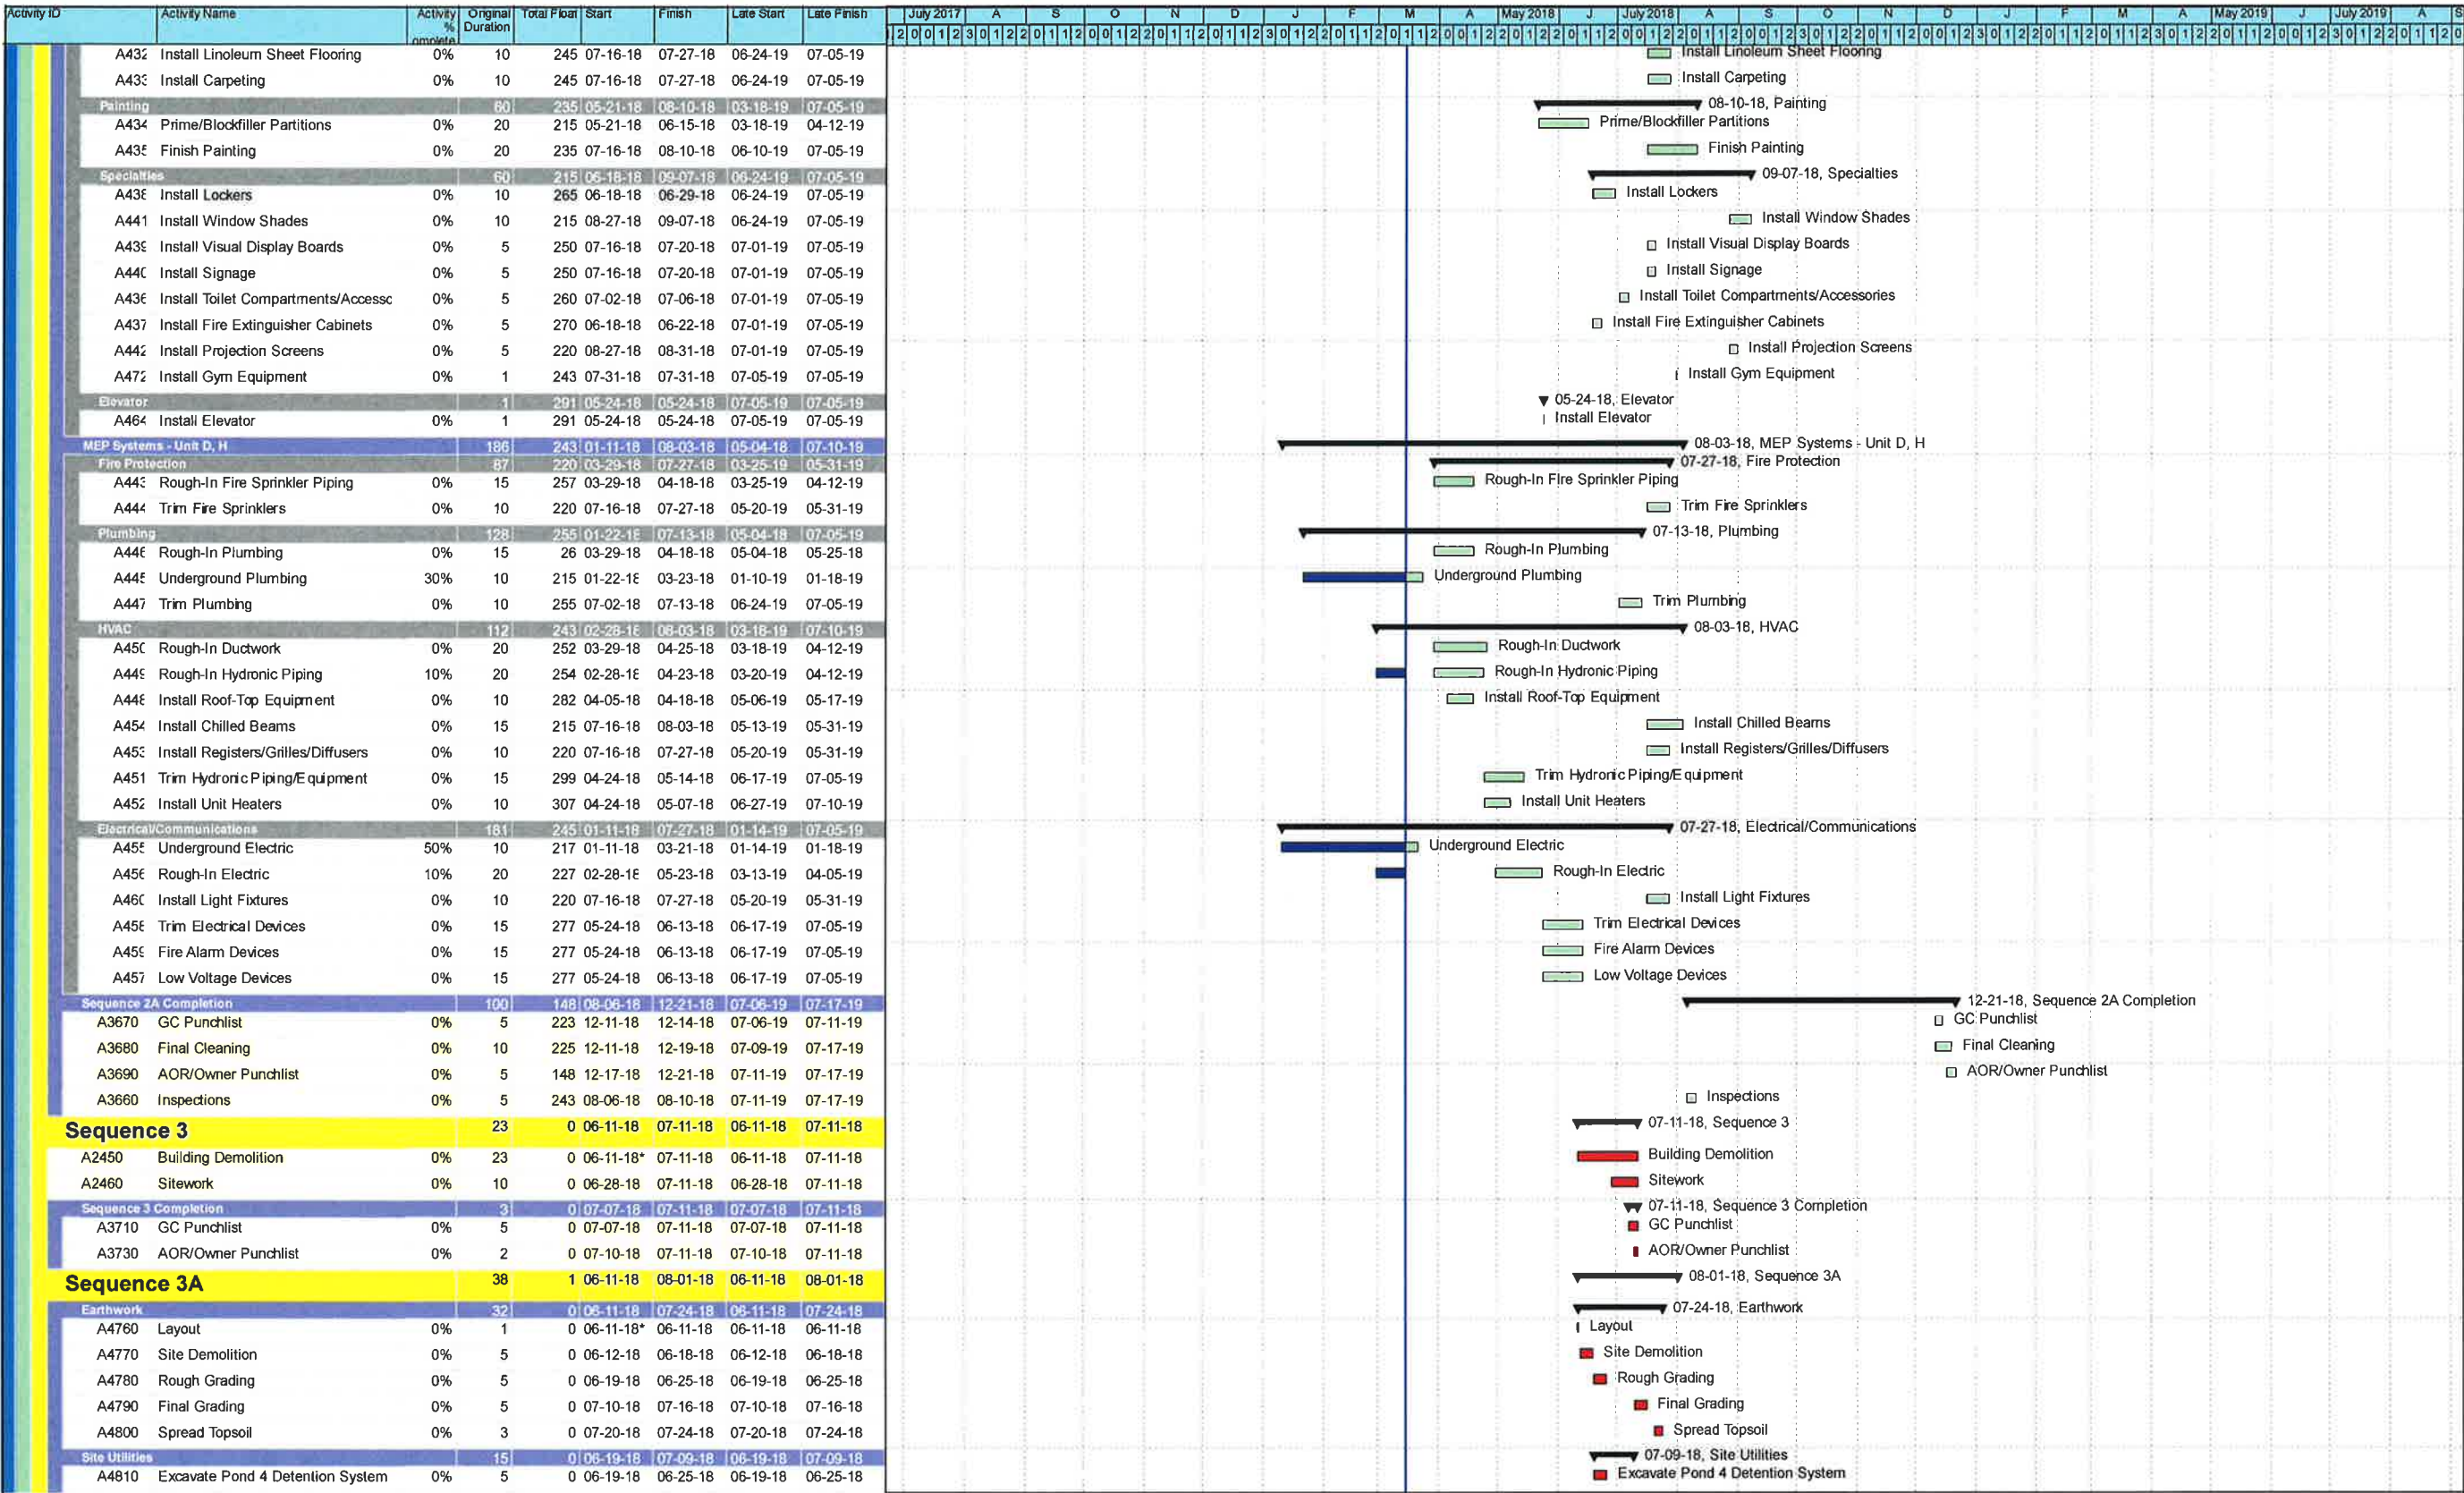

Run Date 03-14-18


Data Date 03-15-18

Page 6 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



K.R. Miller Contractors, Inc.

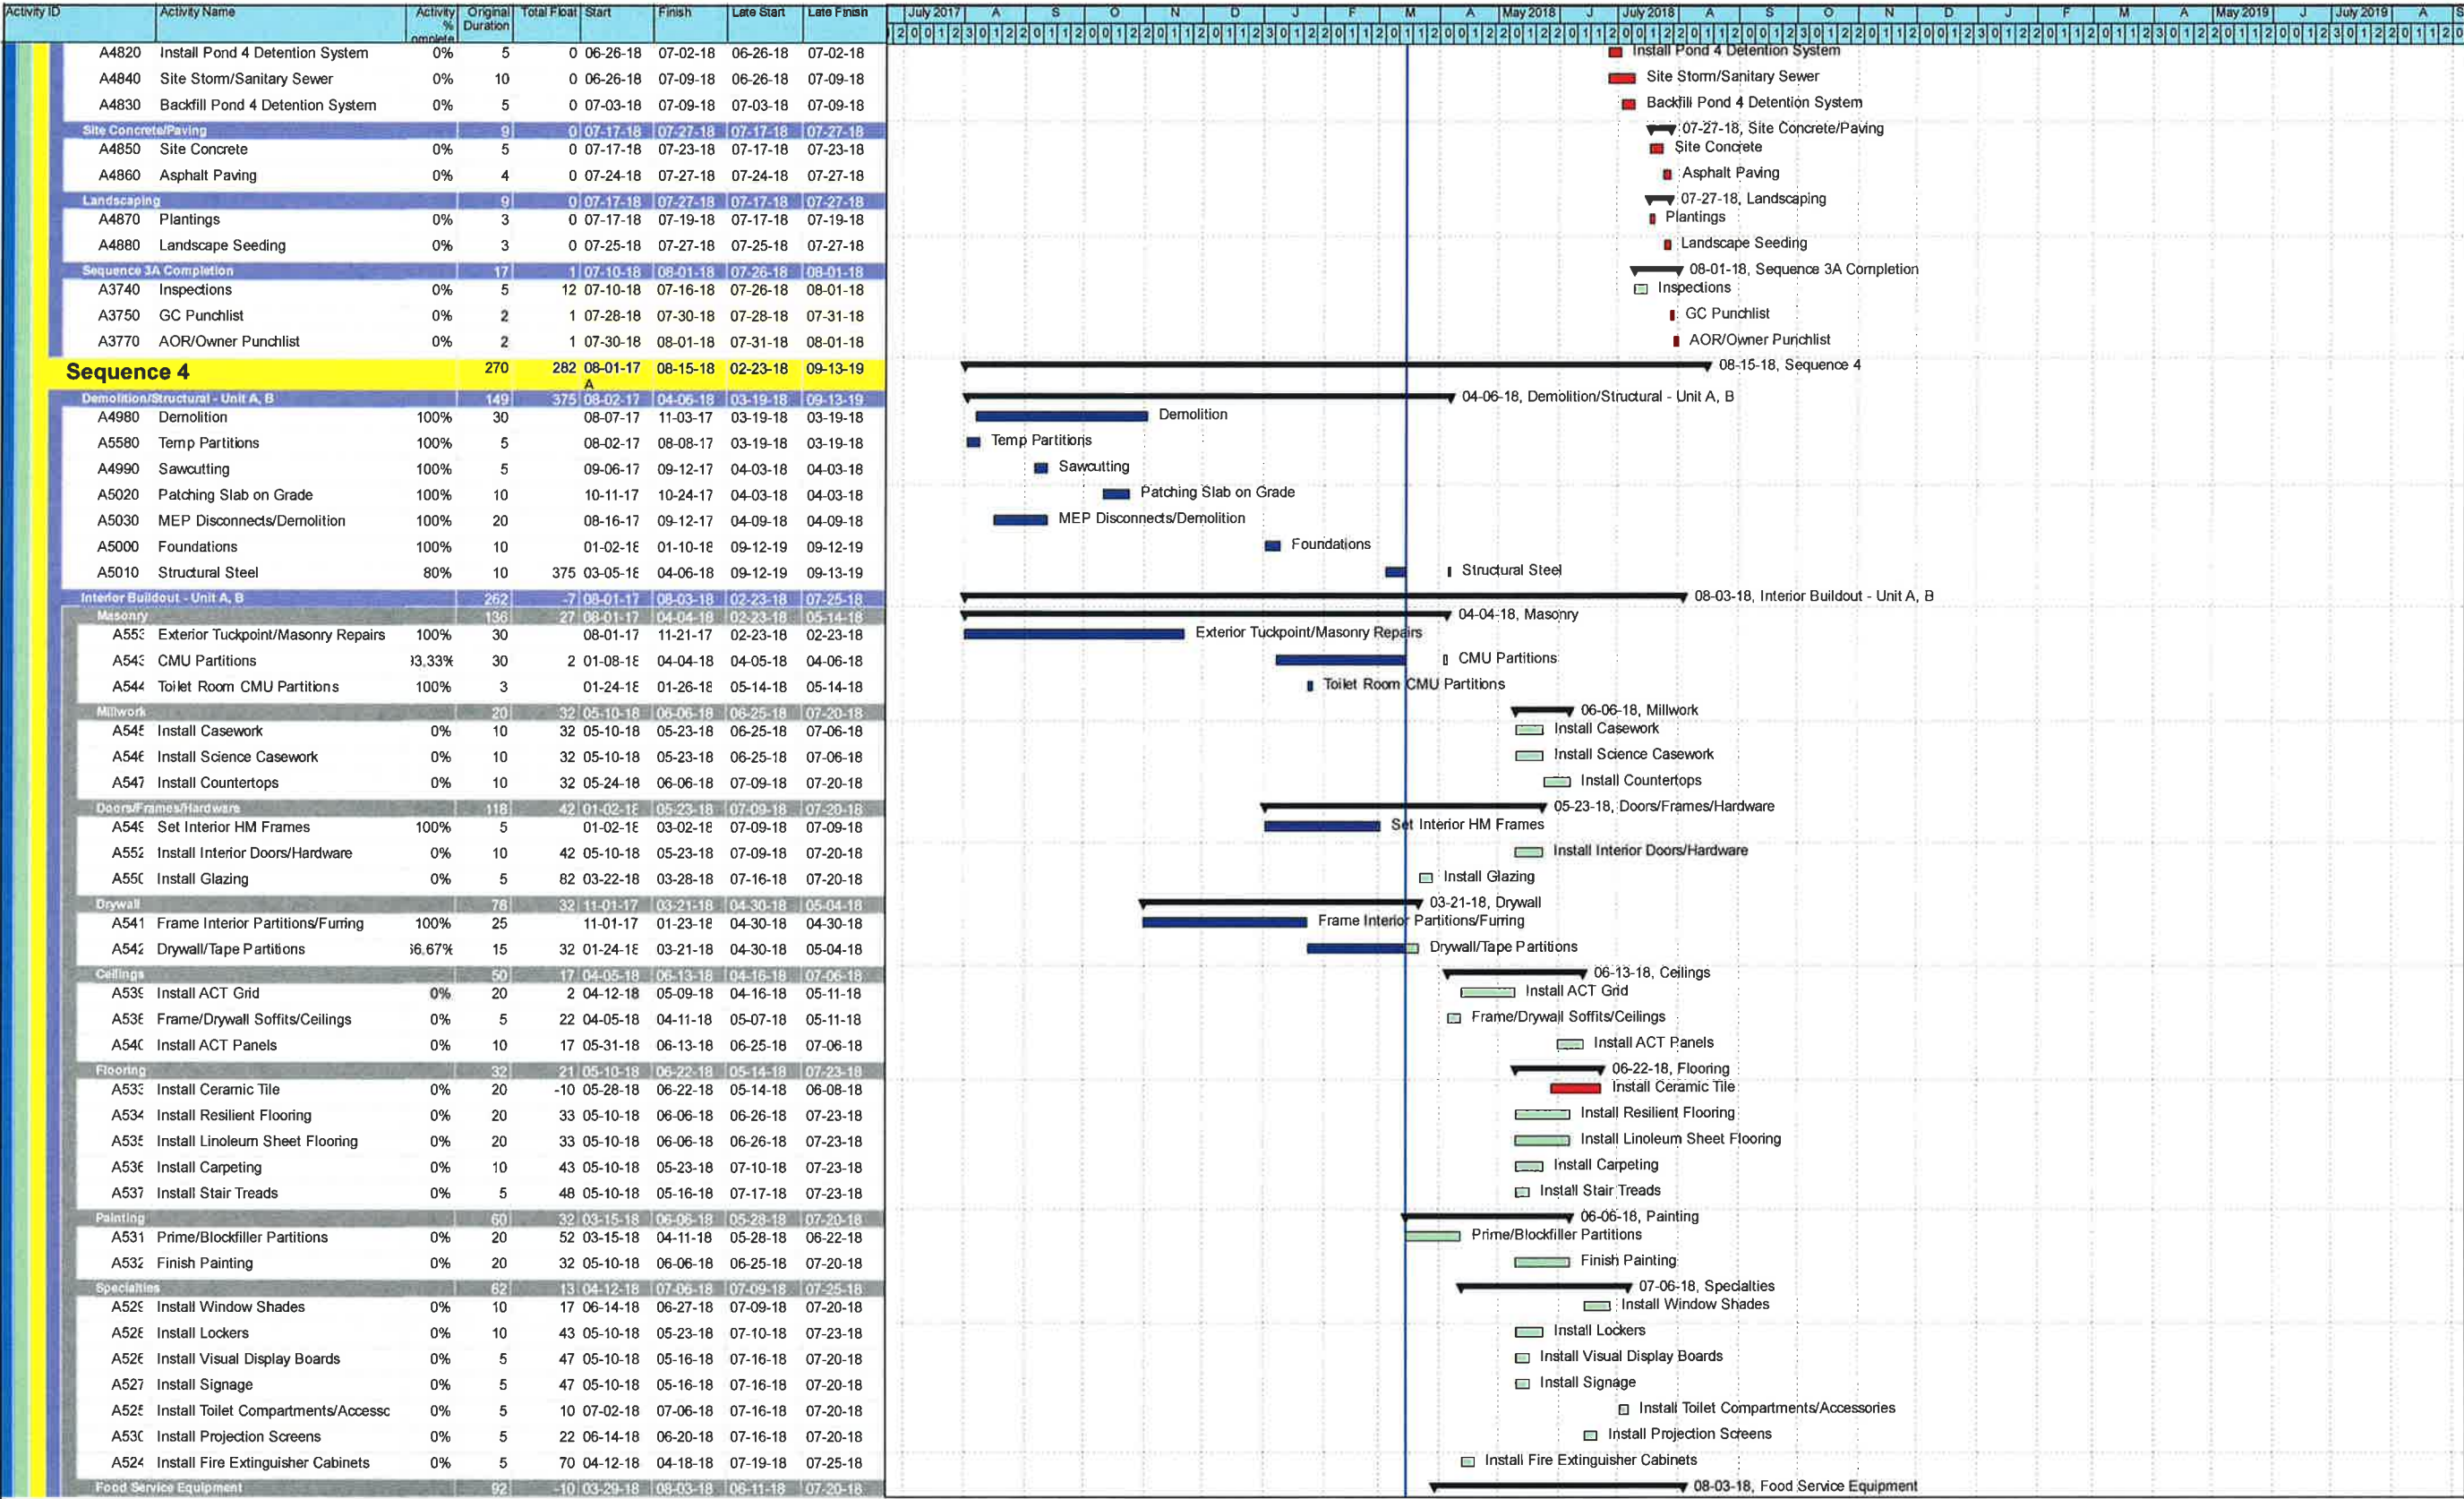


Run Date 03-14-18

Data Date 03-15-18

Page 7 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



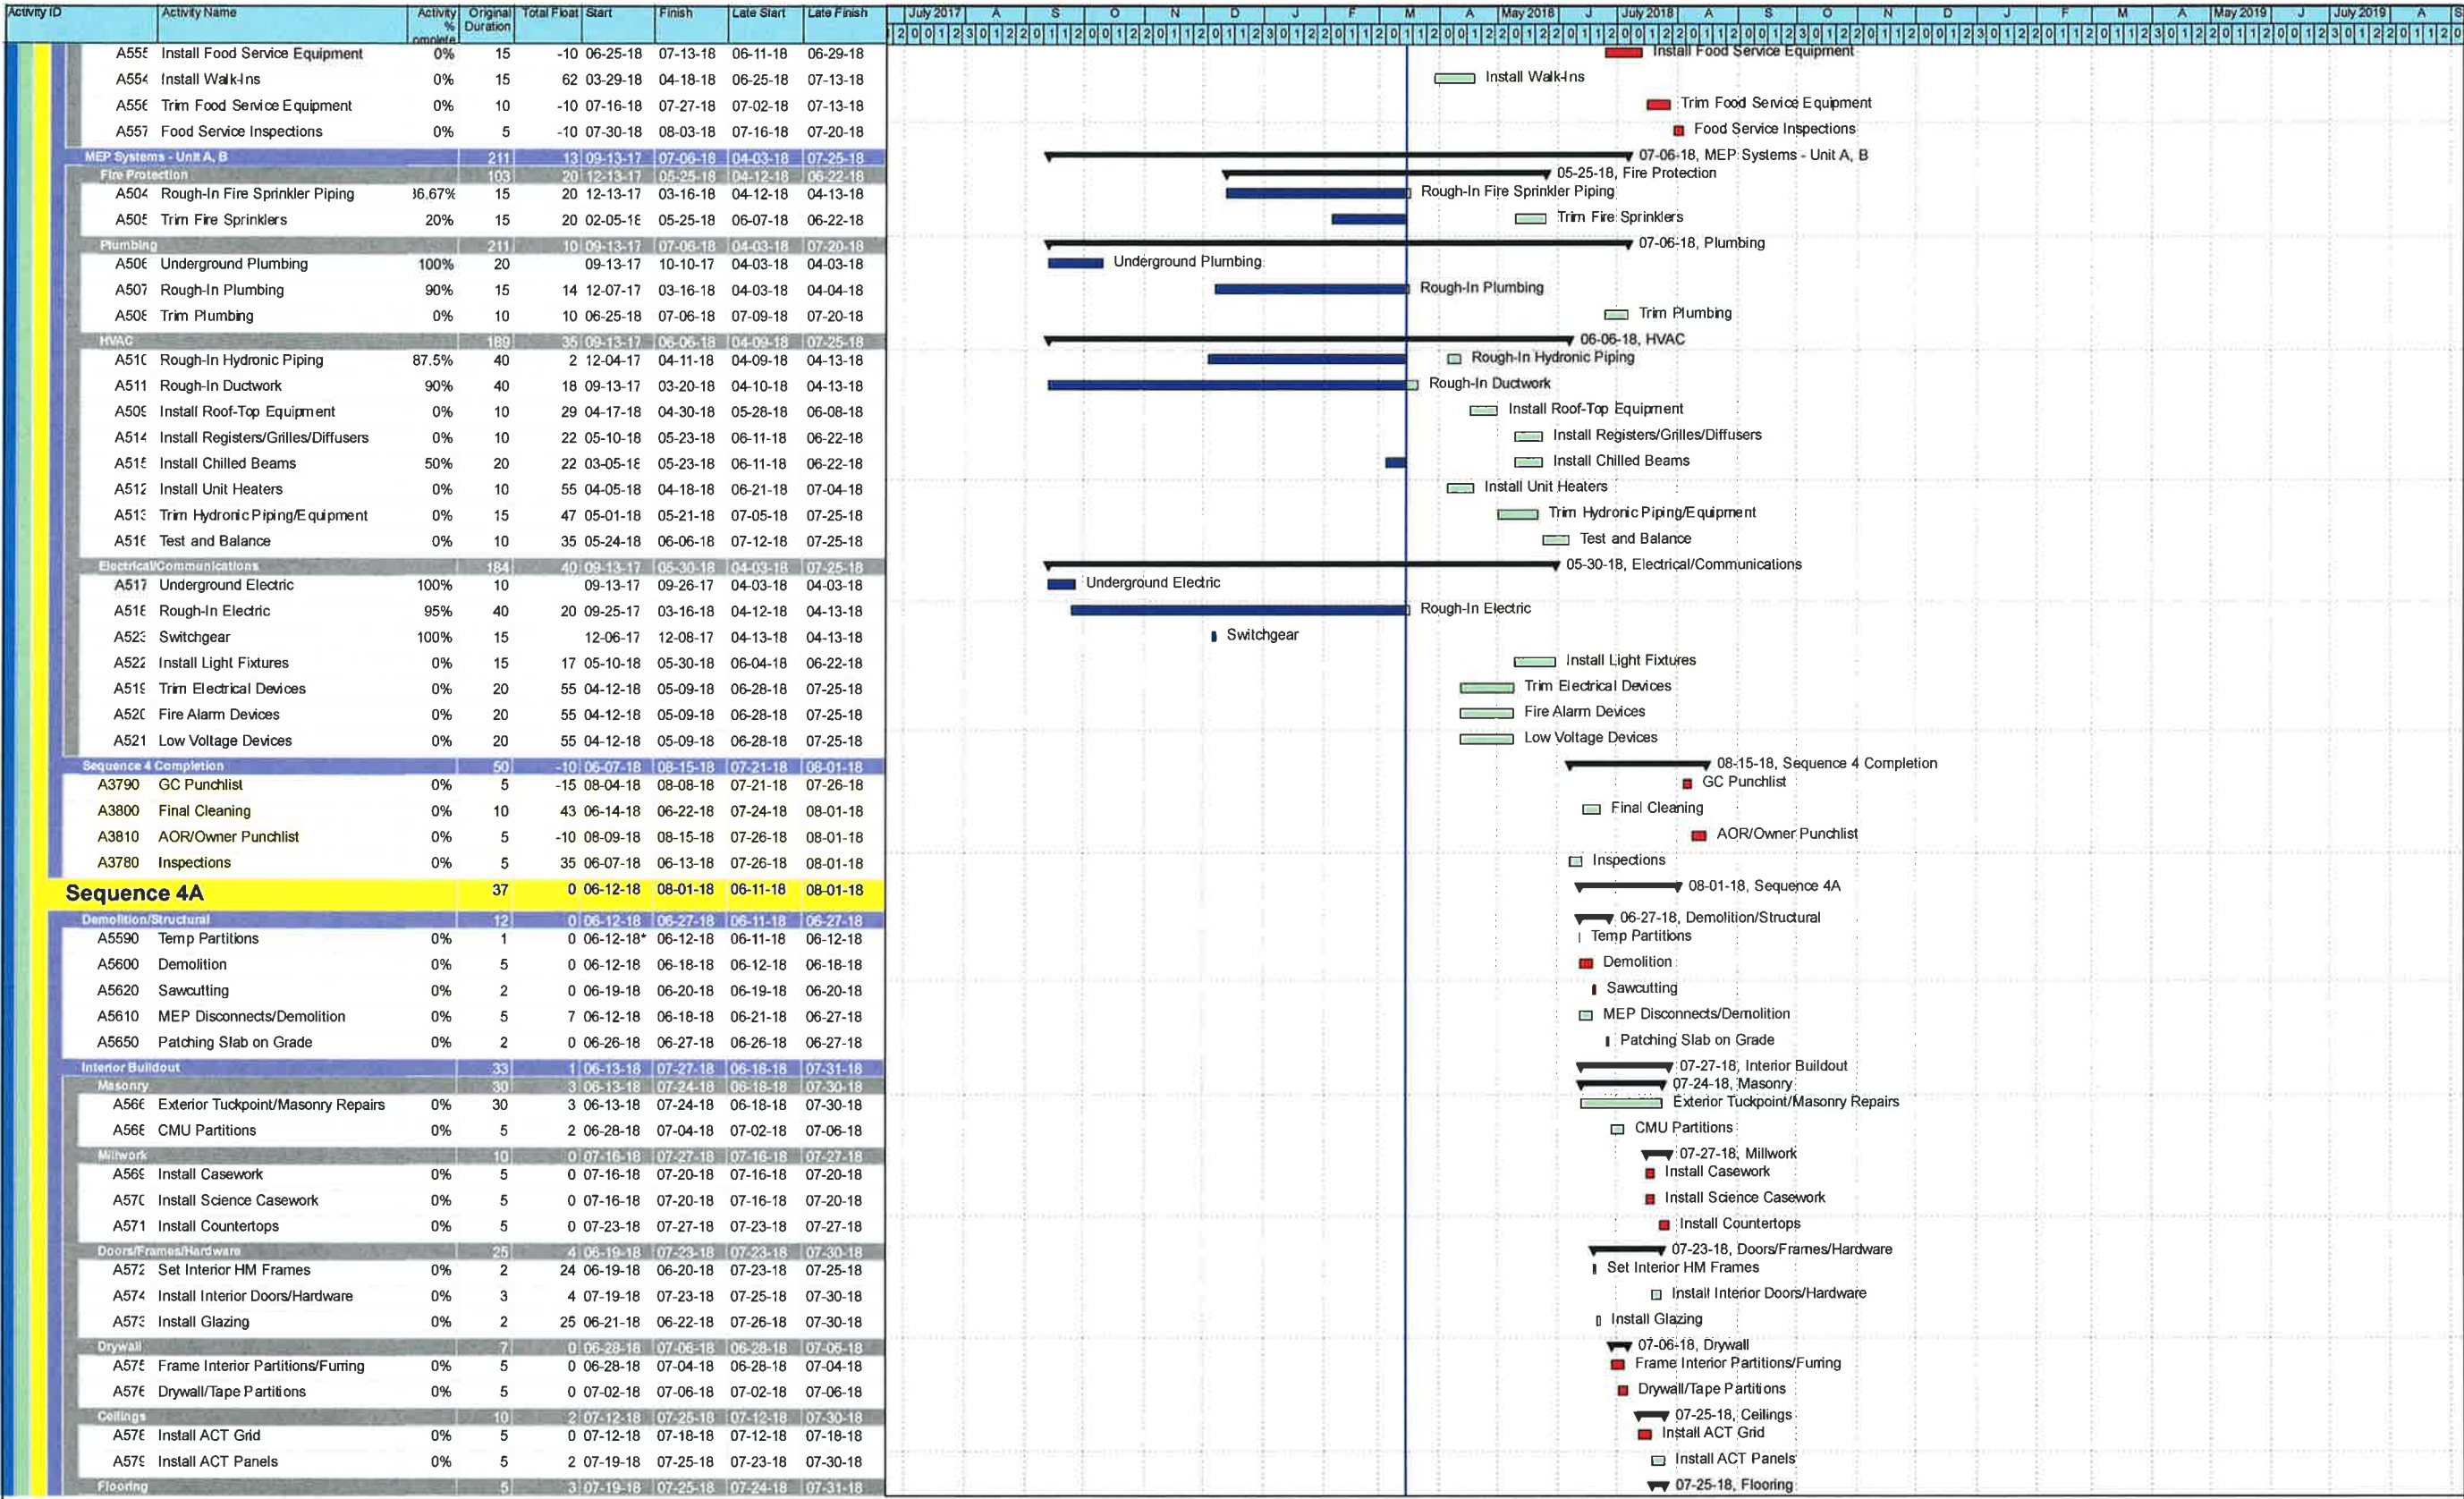

Run Date 03-14-18


Data Date 03-15-18

Page 8 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



K.R. Miller Contractors, Inc.

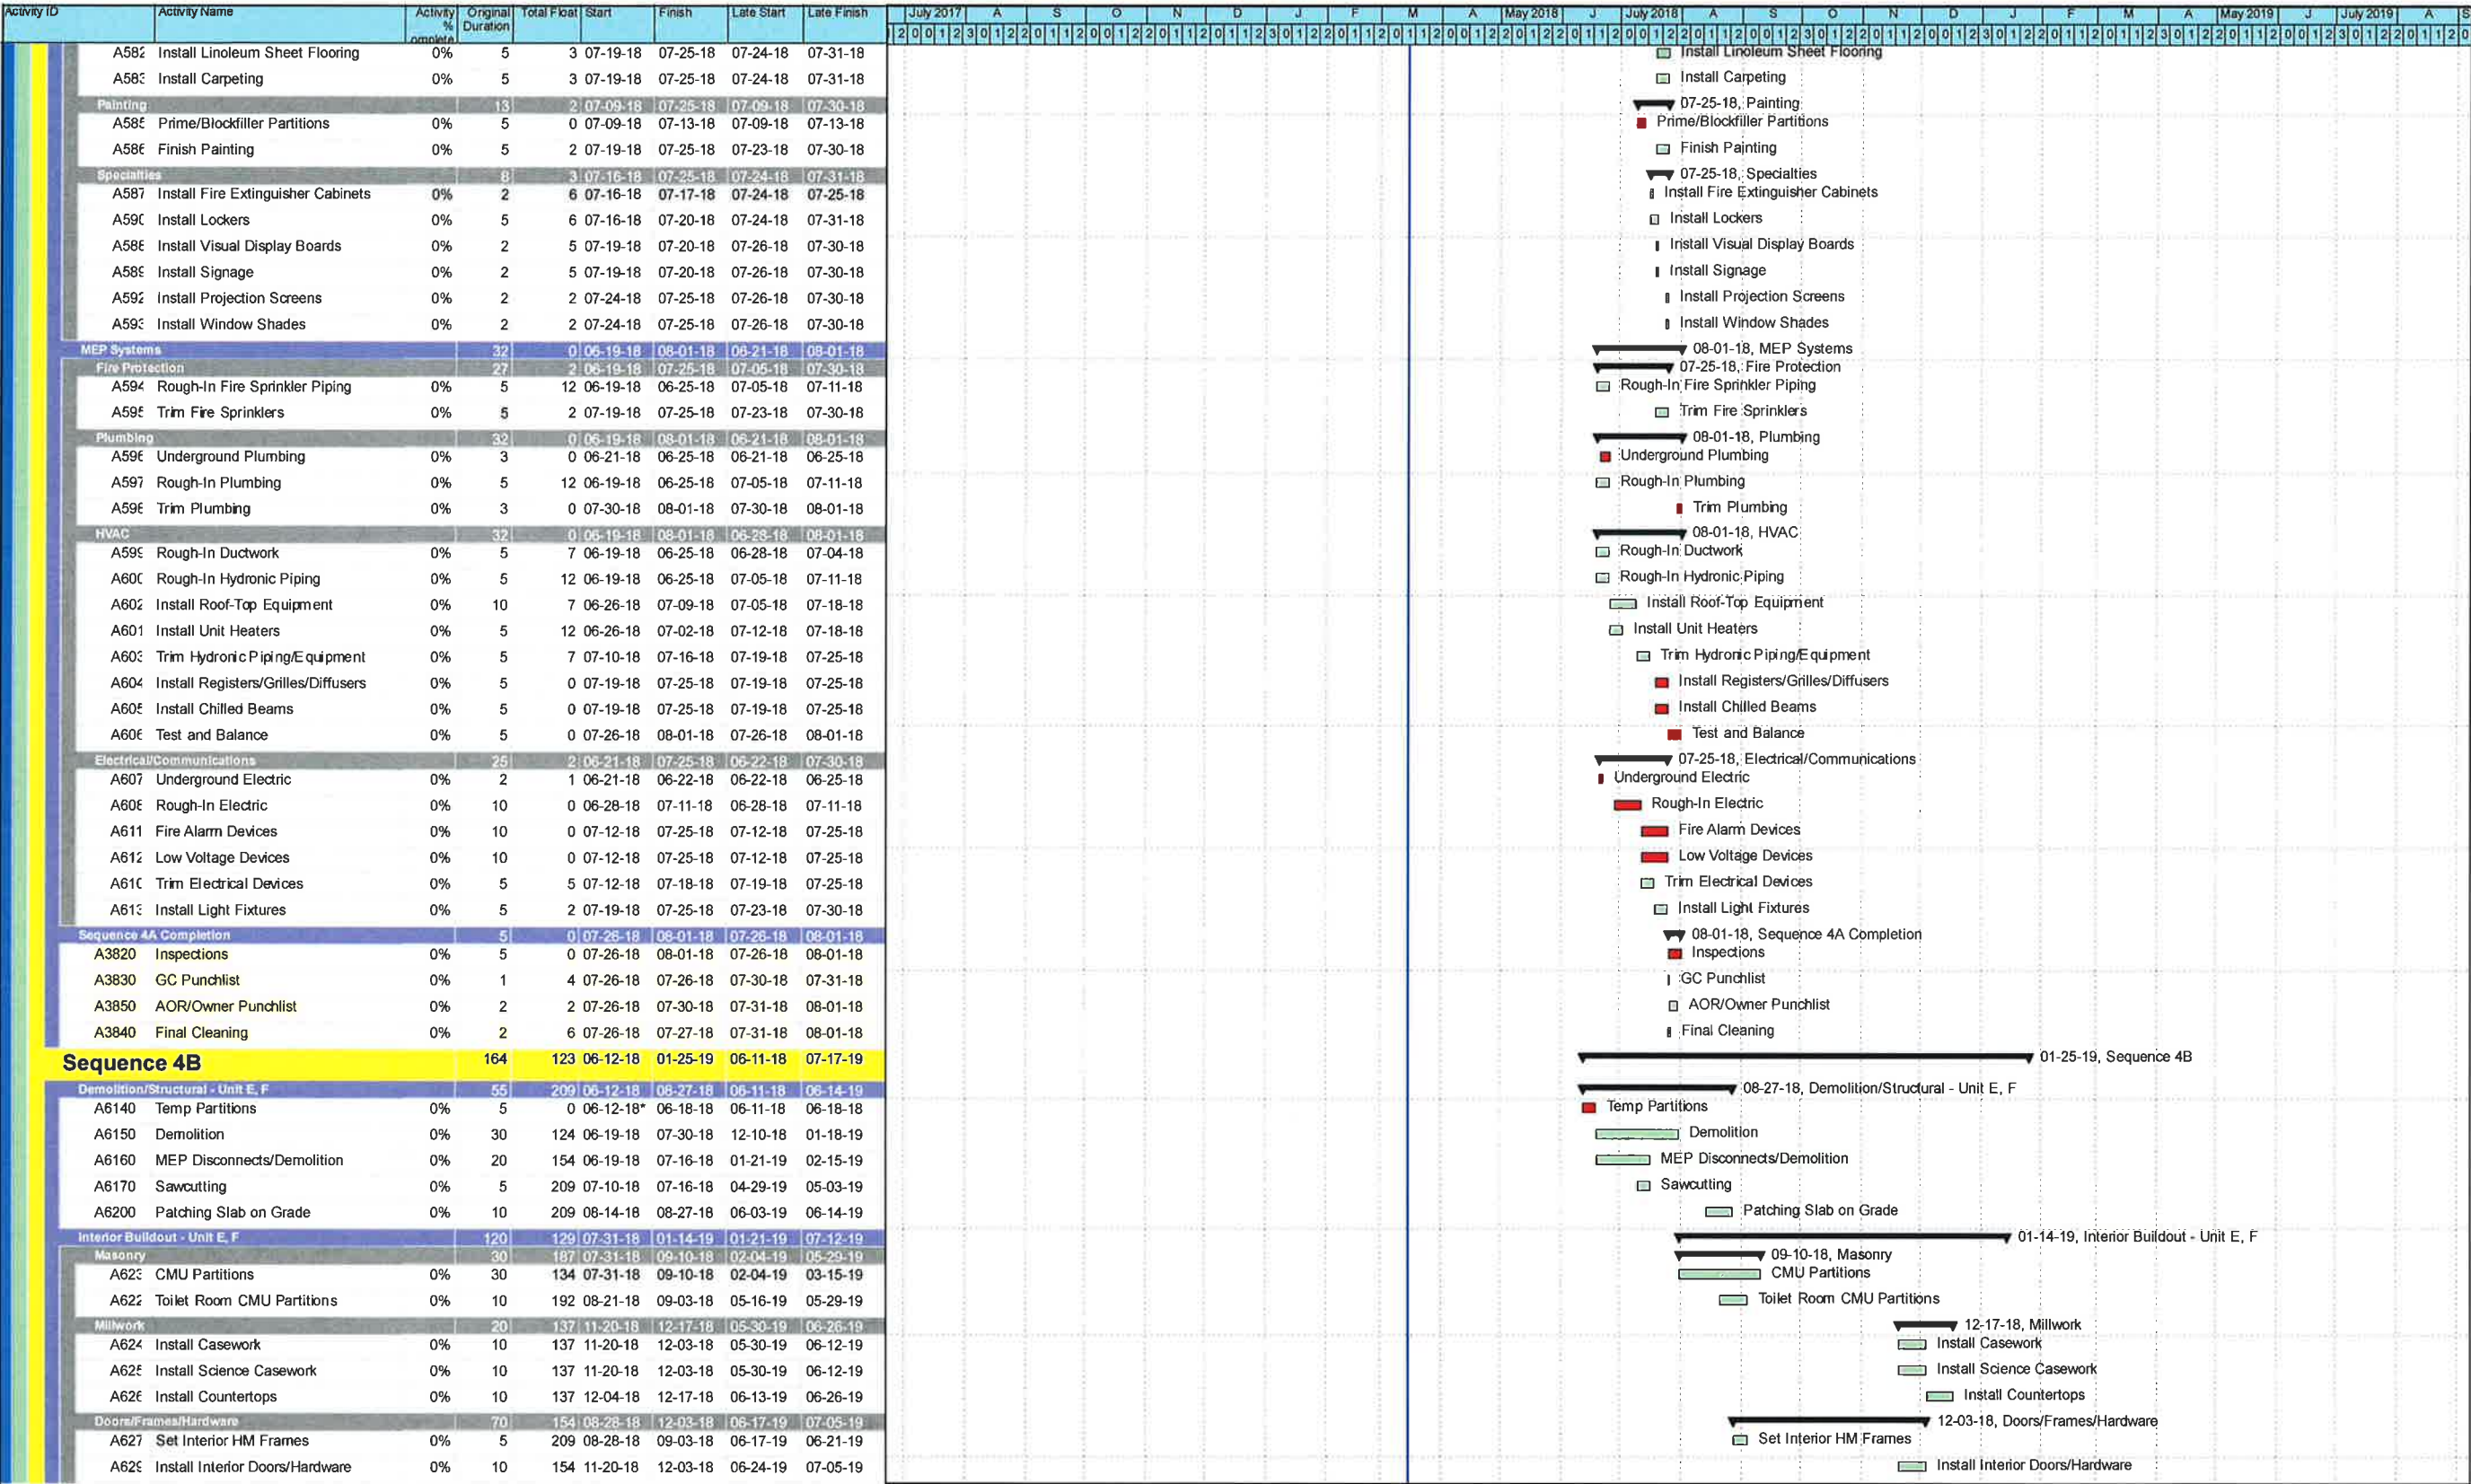


Run Date 03-14-18

Data Date 03-15-18

Page 9 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



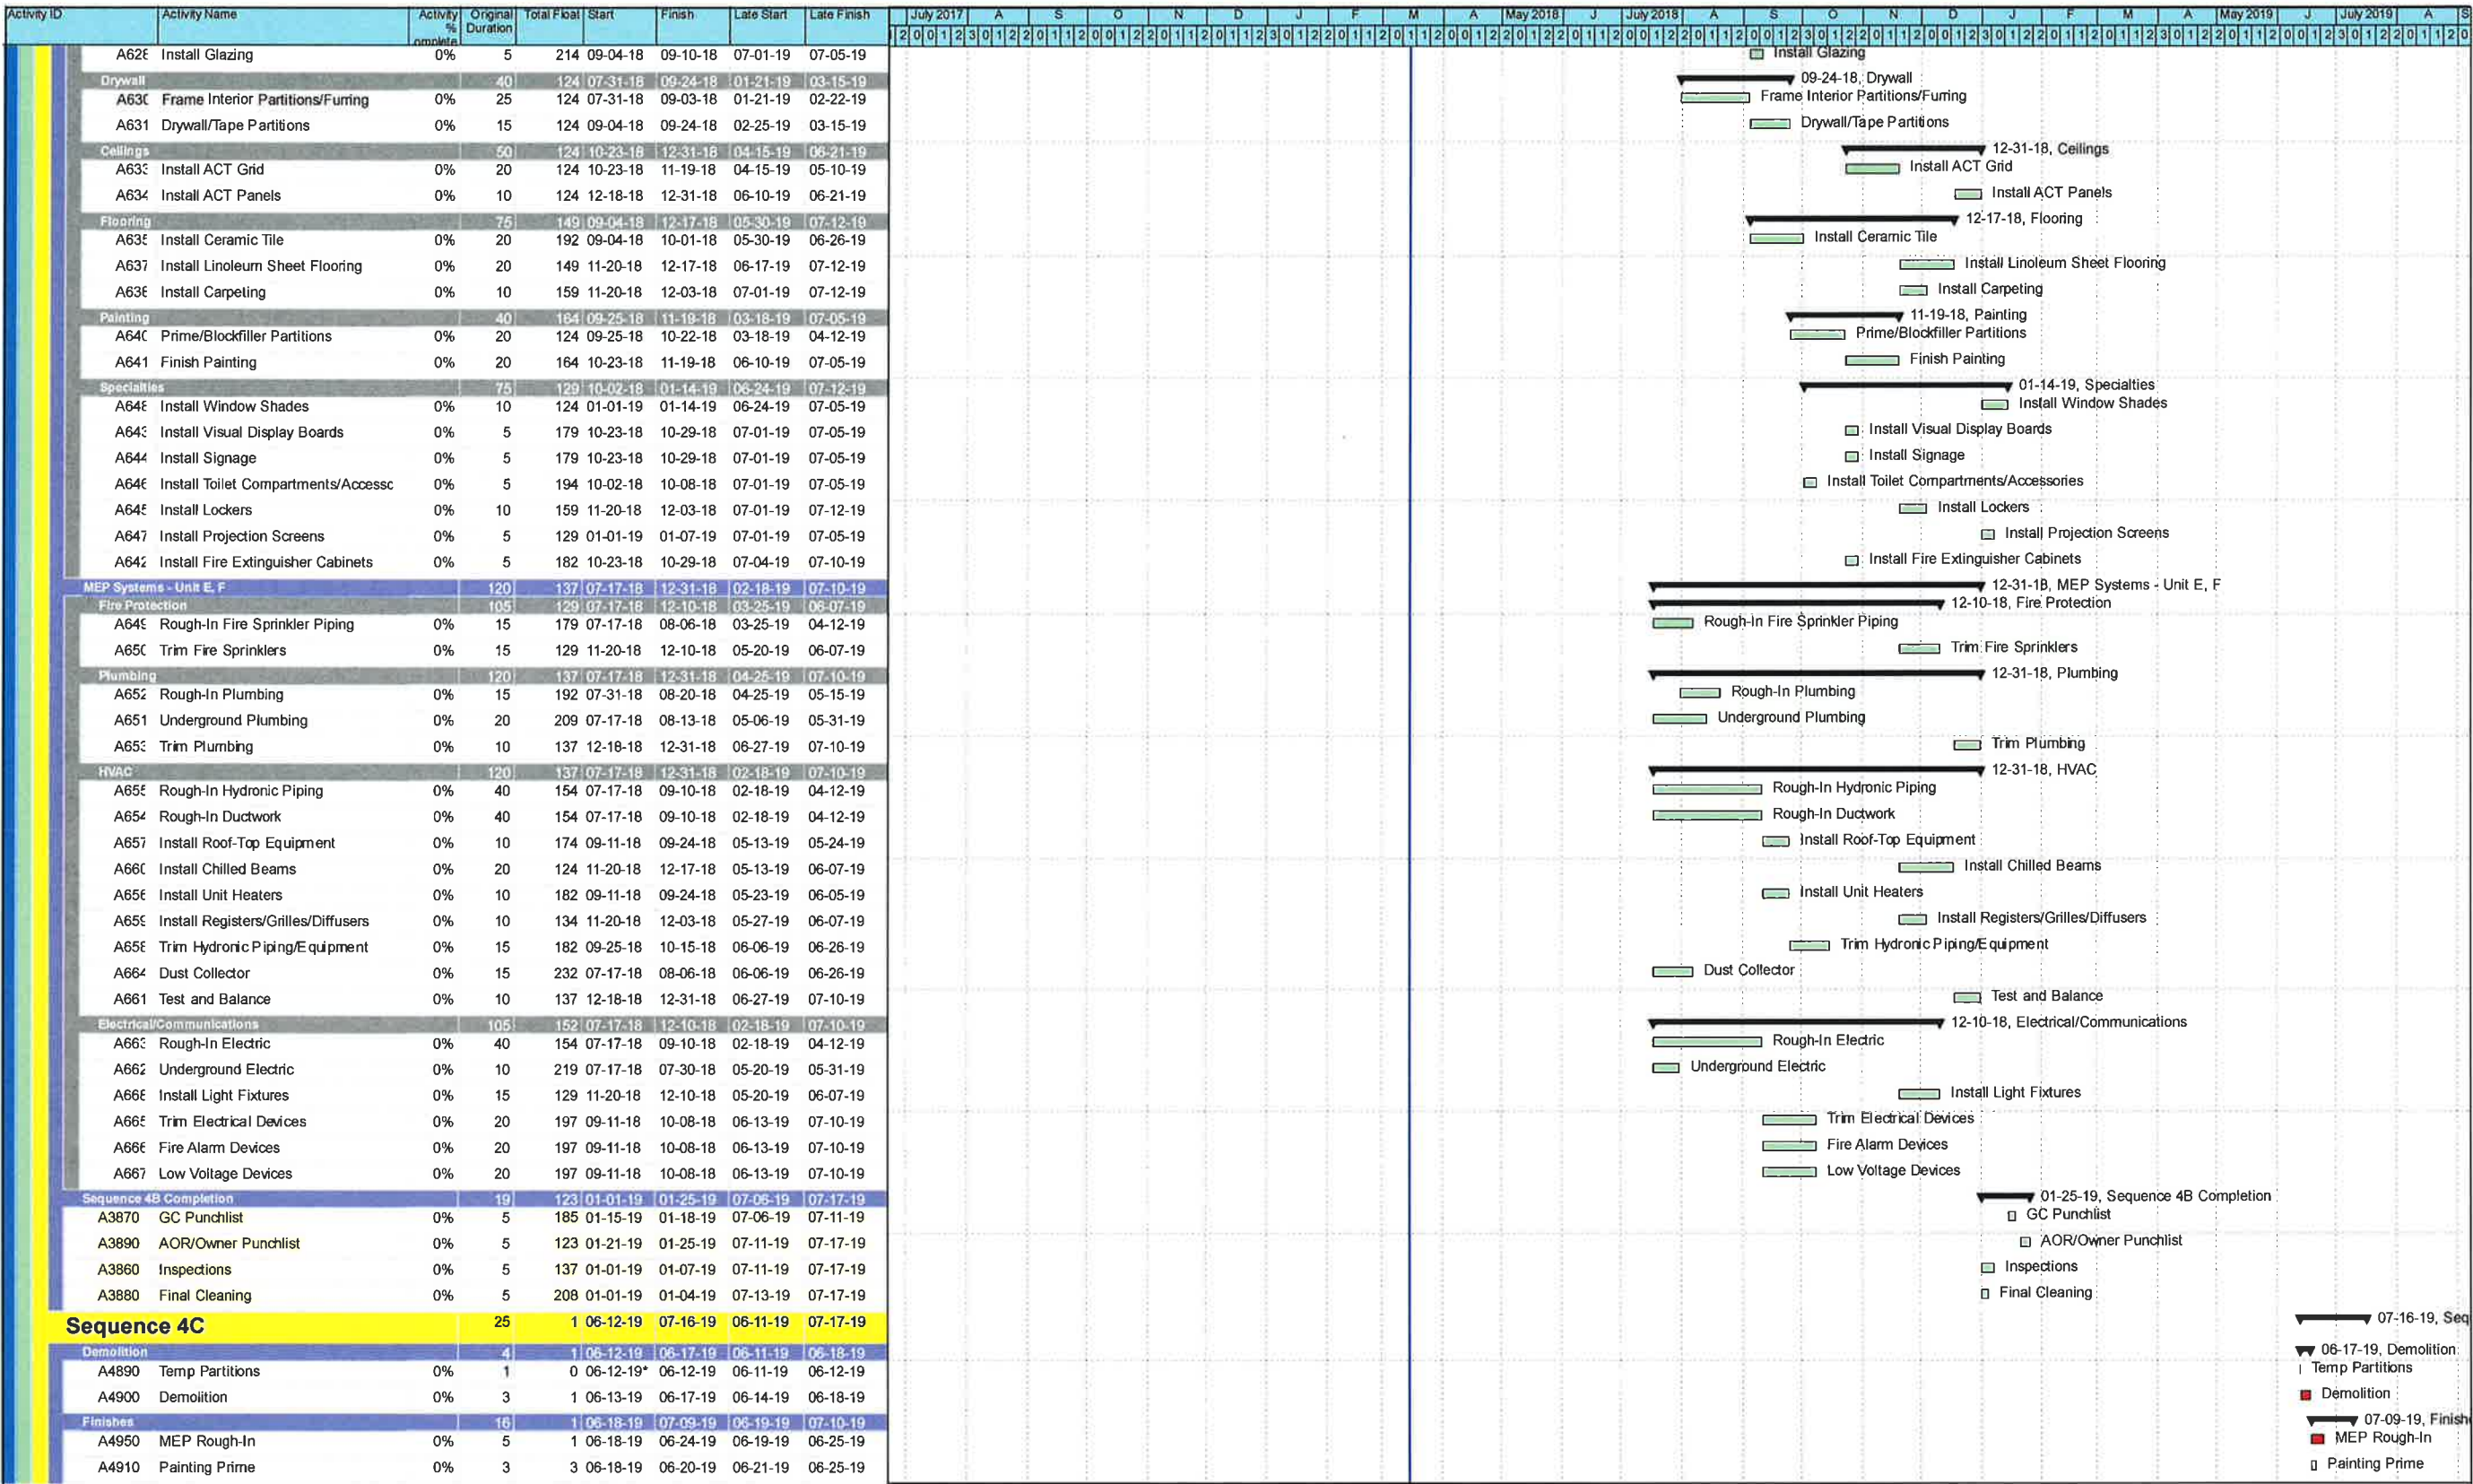

Run Date 03-14-18

Data Date 03-15-18

Page 10 of 11

Thompson Middle School Additions and Alterations
Schedule Update
Submitted March 15, 2018



