

## Construction Status Update Report

*July 2018*

### **Thompson Middle School**

*Project Manager – Craig Lamp*

*Contractor – K.R. Miller Contractors, Inc.*

#### Accomplishments

- Demolition of East wing complete
- Kitchen equipment being installed
- Bathroom floor & wall tile
- Painting in addition
- Ceiling grid & border tile in addition
- Roof tear off and replacement on going
- Interior demolition of existing building
- Underground plumbing installed in renovation area
- Setting casework & tops in addition
- Painting in cafeteria & remodeled areas
- Toilet partitions being installed
- Gym foundation has started
- Site work grading & site concrete
- East side underground storm water retention installed
- Courtyard turf installed
- Brick installed at locker room addition
- Locker bases installed
- Classroom floor tile has started

#### Schedule

Project on schedule

- Upcoming Milestones
  - Asphalt paving
  - Classroom and hallway floor tile
  - Corridor wall tile
  - Carpeting
  - Lockers
- Anticipated Completion Date: 8/1/19
- Status Meetings: Thursdays at 11:00 am in Thompson Office Conference Room

### Budget

Total Project Budget = \$47,100,000 (pre-bid) \$44,496,000 (post bid)

Contract to K.R. Miller \$36,724,550 + \$1,735,793 = \$38,460,343

KR Miller paid as of 7/1/18 = \$16,236,433.03

### Change Orders

- Fully Executed
  - Change Order #1 \$400,013
  - Change Order #2 \$62,384
  - Change Order #3 \$248,505
  - Change Order #4 \$283,910
  - Change Order #5 \$143,501
  - Change Order #6 \$206,746
  - Change Order #7 \$396,446
- Approved in process (Change Order #8)
  - Site Changes \$36,550
  - Modify running track \$132,825
  - Elevator circuits \$1,386
  - Electric for overhead doors \$2,594
  - Lighting for weight rooms \$16,517
- Pending
  - Subfloor patching/prep T&M
  - Connect existing roof drains \$14,232
  - Synthetic turf \$842,791
  - Cafeteria ceiling modifications \$18,141
  - Fill in pond #3 \$35,028
  - Additional tuck pointing \$11,620
  - Additional tuck pointing \$7,200
  - Water tie in for hose bibs \$4,784
  - Replace existing Allerton controllers \$7,809
  - Proscenium opening, color change \$1,948

## Progress Photos

Demolition of east wing 6/22/18



East wing foundation removal 6/28 /18





Cafeteria ceiling grid 6/25/18



Bleacher demolition 6/26/18



Demolition of existing locker rooms 6/26/18



Courtyard turf 6/29/18





Classroom painting & ceiling grid 7/2/18



Gym foundation 7/3/18





East side underground storm detention 7/9/18



Collaboration space 7/9/18





FACS lab 7/9/18



Forming curb east side 7/10/18





Bathroom wall tile & sinks 7/10/18



Pouring curb 7/11/18



Prep to re-pour concrete slab @ UG plumbing 7/12/18



Reroofing work 7/13/18





Filling in of existing ramp 7/16/18



Toilet partitions 7/16/18



East wing demolition 6/15/18



Classroom flooring, cabinets & ceiling 7/17/18





Thompson Middle School  
Change Order Summary Sheet

Total Projected Budget = \$44,496,000

#	Date Issued	Description	Status	Generated By (A,O,GC)	Cost	Final Determination
RFCOP #1	8/1/2017	Acoustic Windows @ Music Area	Rejected	Owner	\$18,900	Void
RFCOP #1(a)	8/1/2017	Acoustic Windows @ Music Area (Alt)	Approved	Owner	\$10,835	Change Order #1
RFCOP #2	8/25/2017	Replace Existing Hall Lockers	Rejected	Owner	\$23,063	Void
RFCOP #3	8/25/2017	Glass Marker Boards @ Science Rooms	Rejected	Owner	\$53,490	Void
RFCOP #4	9/6/2017	Extra Cabinetry Demolition	Approved	Architect	\$1,357	Change Order #1
RFCOP #5	9/15/2017	Sitework/Parking Lot Revisions	Approved	Architect	\$55,612	Change Order #1
RFCOP #6	9/20/2017	Revise Feeder to RTU 3	Approved	Architect	\$0	Change Order #1
RFCOP #7	10/2/2017	Existing Door 17 to Remain	Approved	Architect	(\$2,099)	Change Order #1
RFCOP #8	10/10/2017	Replace hall lockers E&F	Rejected	Owner	\$41,727	Void
RFCOP #9	10/10/2017	Site changes Bulletin #2	Approved	Architect	\$68,907	Change Order #2
RFCOP #10	10/10/2017	Site changes Bulletin #3	Approved	Architect	\$36,550	Approved
RFCOP #11	10/24/2017	ERU VFD's	Approved	Architect	\$0	Change Order #2
RFCOP #12	10/26/2017	Chilled water piping	Approved	Architect	\$13,894	Change Order #4
RFCOP #13	11/6/2017	Revise wall tile	Approved	Architect	(\$4,050)	Change Order #3
RFCOP #14	11/8/2017	Renumber existing lockers	Approved	Owner	\$2,082	Change Order #2
RFCOP #15	11/8/2017	Revisions to FACS area	Approved	Architect	\$51,206	Change Order #2
RFCOP #16	11/10/2017	Band & Choir revisions	Approved	Architect/Owner	\$14,650	Change Order #2
RFCOP #17	11/9/2017	Cafeteria ceiling	Approved	Architect	\$12,638	Change Order #4
RFCOP #18	11/8/2017	Added steel at front entry	Approved	Architect	\$7,079	Change Order #2
RFCOP #19	11/16/2017	VCT in Cafeteria	Approved	Architect/Owner	(\$35,216)	Change Order #2
RFCOP #20.1	11/16/2017	Marmoleum tile in Classrooms	Approved	Architect/Owner	(\$145,254)	Change Order #2
RFCOP #20.2	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$81,848)	Void
RFCOP #20.3	11/16/2017	Marmoleum tile in Classrooms	Void	Architect/Owner	(\$28,199)	Void
RFCOP #21	11/16/2017	Marmoleum tile in Corridors	Approved	Architect/Owner	(\$54,514)	Change Order #2
RFCOP #22	11/16/2017	VT in Cafeteria	Void	Architect/Owner	(\$6,000)	Void
RFCOP #23	11/16/2017	VT in Classrooms	Void	Architect/Owner	Void	Void
RFCOP #24	11/20/2017	Modify running track	Approved	Architect/Owner	\$132,825	Approved
RFCOP #24A	11/20/2017	Modify running track Alternate	Rejected	Architect/Owner	\$193,515	Void
RFCOP #25	11/20/2017	Prep field for turf	Approved	Architect/Owner	\$28,712	Change Order #2
RFCOP #26	11/20/2017	Toilet room B130 revision	Approved	Architect	28,534	Change Order #3

RFCOP #27	11/20/2017	Skylight shaft	Approved	Architect	\$9,175	Change Order #2
RFCOP #28	11/22/2017	Cafeteria/Kitchen modifications	Approved	Architect	\$71,722	Change Order #4
RFCOP #29	11/22/2017	Area B,C,D sanitary	Approved	Architect	\$15,854	Change Order #3
RFCOP #30	11/22/2017	Area B sanitary	Approved	Architect	\$9,455	Change Order #3
RFCOP #31	11/27/2017	Electric water cooler A108	Approved	Architect	\$8,801	Change Order #3
RFCOP #32	11/28/2017	Casework changes A114	Void	Architect	Void	Void
RFCOP #33	12/12/2017	Sensory room relocation	Approved	Architect/Owner	\$21,127	Change Order #2
RFCOP #34	12/7/2017	Delete sanitary to west addition	Approved	Architect	\$536	Change Order #2
RFCOP #35	12/15/2017	Additional exterior windows	Approved	Owner	\$81,609	Change Order #4
RFCOP #36	12/8/2017	Classroom mobile casework	Approved	Architect/Owner	\$33,643	Change Order #3
RFCOP #37	12/14/2017	Backflow preventer B141	Rejected	Architect	\$8,720	Rejected
RFCOP #38	12/14/2017	New radiation room A112	Approved	Architect	\$7,809	Change Order #2
RFCOP #39	12/14/2017	Water cooler B205	Approved	Architect	\$4,850	Change Order #3
RFCOP #40	12/14/2017	New door to conf. rm. B	Approved	Owner	\$10,163	Change Order #3
RFCOP #41	1/8/2018	Power & IT requirements	Approved	Architect	\$23,431	Change Order #5
RFCOP #42	1/10/2018	Storefront finish	Approved	Architect	(\$4,037)	Change Order #2
RFCOP #43	1/12/2018	Reroute stormwater	Approved	Architect	\$3,439	Change Order #3
RFCOP #44	1/12/2018	Replace 2 existing columns	Approved	Architect	\$12,527	Change Order #4
RFCOP #45	1/12/2018	City water main revisions	Approved	City	\$6,441	Change Order #2
RFCOP #46	2/27/2018	Gym floor striping	Approved	Architect	\$6,214	Change Order #7
RFCOP #47	1/29/2018	Fritz tile	Approved	Owner/Architect	\$31,425	Change Order #4
RFCOP #48	1/30/2018	Subfloor patching/prep				T&M
RFCOP #49	1/30/2018	Fire pump	Approved	Architect	\$53,959	Change Order #5
RFCOP #50	Void	Void	Void	Void	Void	Void
RFCOP #51	Void	Void	Void	Void	Void	Void
RFCOP #52	2/12/2018	MCT floor patterns	Approved	Architect	\$0	Change Order #4
RFCOP #53	2/19/2018	Emergency shower floor drains	Approved	Architect	\$67,234	Change Order #7
RFCOP #54	2/16/2018	Revise tempered water	Approved	Architect	\$23,582	Change Order #7
RFCOP #55	2/14/2018	Frosted glass @ Science rooms	Approved	Architect	\$657	Change Order #3
RFCOP #56	2/14/2018	Water cooler A106 & A127	Approved	Architect	\$12,215	Change Order #6
RFCOP #57	2/15/2018	Ceiling modifications B140 & B141	Approved	Architect	\$4,088	Change Order #3
RFCOP #58	2/15/2018	Modify existing light wells	Approved	Architect	\$7,187	Change Order #5
RFCOP #59	2/16/2018	Safety goggle cabinets	Approved	Architect	\$3,849	Change Order #4
RFCOP #60	2/21/2018	B213 mechanical chase	Approved	Architect	\$858	Change Order #6



RFCOP #61	2/21/2018	Sensory room/tech room revisions	Approved	Architect	\$12,615	Change Order #5
RFCOP #62	2/21/2018	Band/Orchestra exterior windows	Approved	Architect	\$1,154	Change Order #4
RFCOP #63	2/21/2018	Science B213 wall modification	Approved	Architect	\$11,652	Change Order #6
RFCOP #64	2/27/2018	Locker revision	Approved	Architect	\$6,464	Change Order #6
RFCOP #65	2/27/2018	Marker board modifications	Approved	Architect	(\$183)	Change Order #4
RFCOP #66	3/6/2018	Cafeteria ceiling tile revision	Rejected	Architect	\$8,354	Rejected
RFCOP #67	3/12/2018	Subfloor remedial work		Architect		
RFCOP #68	3/26/2018	Connect existing roof drains	Pending	Architect	\$14,232	T&M NTE
RFCOP #69	3/22/2018	Spandrel glass modifications	Approved	Architect	\$6,269	Change Order #5
RFCOP #70	4/4/2018	Synthetic turf field	Pending	Owner	\$842,791	
RFCOP #71	4/17/2018	Added window E206	Approved	Architect/Owner	\$11,665	Change Order #6
RFCOP #72	4/18/2018	Sensory room swivel hoist	Approved	Architect/Owner	\$0	Change Order #5
RFCOP #73	4/18/2018	Light well access panel	Approved	Architect	\$0	Change Order #5
RFCOP #74	4/18/2018	Retaining wall cap		Contractor RFI/Arch.		
RFCOP #75	5/2/2018	Acoustic panels	Approved	Architect	\$51,569	Change Order #7
RFCOP #76	4/23/2018	Main office security	Approved	Architect/Owner	\$5,799	Change Order #7
RFCOP #77	4/23/2018	Gym & lobby graphics	Approved	Architect/Owner	\$5,145	Change Order #7
RFCOP #78	4/24/2018	B133 ceiling modifications	Pending	Architect	\$18,141	
RFCOP #79	5/2/2018	Stairs C120 & D101	Approved	Architect	\$9,181	Change Order #7
RFCOP #80	5/2/2018	B133B Ceiling	Approved	Architect	\$3,249	Change Order #6
RFCOP #81	5/2/2018	Visual annunciation strobe	Approved	Architect/Owner	\$6,422	Change Order #6
RFCOP #82	5/7/2018	Gym bleacher feeder	Approved	Architect	\$5,602	Change Order #7
RFCOP #83	5/8/2018	Science window sills	Approved	Architect/Contractor	(\$3,494)	Change Order #7
RFCOP #84	5/24/2018	East plaza stairs		Architect/Contractor		
RFCOP #85	5/24/2018	Loading dock slab	Approved	Architect/Contractor	\$7,038	Change Order #7
RFCOP #86	6/5/2018	Elevator circuits	Approved	Architect	\$1,386	Approved
RFCOP #87	6/7/2018	Remove north hydrant	Approved	Plumbing inspector	\$16,060	Change Order #7
RFCOP #88	6/12/2018	Replace existing wire mold		Architect/Owner		
RFCOP #89	6/13/2018	Extrend bus parking		Architect/Owner		
RFCOP #90	6/13/2018	Provide VAV piping		Architect		
RFCOP #91	6/19/2019	Pond 3 fill	Pending	Owner	\$35,028	NTE
RFCOP #92	6/19/2019	Stair C101		Architect/Contractor		
RFCOP #93	6/19/2019	East plaza stairs	Void	Architect/Contractor	Void	Void
RFCOP #94	6/19/2019	Room signage allowance	Approved	Architect	(\$18,000)	Change Order #7

RFCOP #95	6/19/2019	Stair D101		Architect/Contractor		
RFCOP #96	6/25/2018	Sump pump discharge		Architect/Contractor		
RFCOP #97	7/9/2018	Unit F roof drain revisions		Architect/Contractor		
RFCOP #98	6/25/2018	Unit F hydronic piping	Void	Void	Void	Void
RFCOP #99	7/2/2018	EIFS at east soffits		Architect		
RFCOP #100	6/26/2018	North parking lot undercut		Architect		
RFCOP #101	6/28/2018	Electric for OH doors	Approved	Architect/Contractor	\$2,594	Approved
RFCOP #102	6/29/2018	East side site revisions		Architect/Owner		
RFCOP #103	7/2/2018	Lighting rooms F210 & F211	Approved	Architect	\$16,517	Approved
COR #1	9/20/2017	Remove & Replace 2 Existing Manholes	Approved	Katco/RFI	\$15,462	Change Order #1
COR #2	9/27/2017	Remove & Replace Water Lines Corr 108	Approved	Owner	\$28,175	Change Order #1
COR #3	10/4/2017	Lintel Replacement	Approved	Iwanski/Architect	\$97,818	Change Order #1
COR #3A	3/27/2018	Lintel replacement Area 1D	Approved	Iwanski/Architect	\$28,577	Change Order #6
COR #4	10/4/2017	Parapet Wall Replacement	Approved	Iwanski/Architect	\$61,655	Change Order #6
COR #5	11/6/2017	Mezzanine demolition RFI #47	Approved	Miller/RFI	\$7,482	Change Order #2
COR #6		New chase walls RFI #5	Void	Void	Void	Void
COR #7	11/4/2017	Barrier curb removal RFI #7&8	Approved	Miller/RFI	\$9,075	Change Order #1
COR #8	11/1/2017	Remove floor substrate RFI #19	Approved	Miller/RFI	\$6,795	Change Order #1
COR #9	11/4/2017	Revised ramp curb detail RFI #20	Approved	Miller/RFI	\$427	Change Order #1
COR #10	11/4/2017	Revised foundation wall detail RFI #21	Approved	Miller/RFI	\$1,573	Change Order #1
COR #11	2/23/2018	Infill openings @ duct RFI #27	Approved	Miller/RFI	\$9,262	Change Order #5
COR #12	11/4/2017	Concrete infills RFI #30&73	Approved	Miller/RFI	\$5,008	Change Order #1
COR #13	11/28/2017	Demolition of LBP RFI #35	Approved	Miller/RFI	(\$5,432)	Change Order #2
COR #14	1/3/2018	Remove blower motor	Approved	Miller/RFI	\$3,584	Change Order #2
COR #15	11/28/2017	Furring @ exterior walls RFI #45,46&70	Approved	Miller/RFI	\$35,114	Change Order #7
COR #16		Sump pit @ elevator RFI #52	Void	Void	Void	Void
COR #17		Revise mezz wall construction RFI #53	Void	Void	Void	Void
COR #18	11/3/2017	Brick ledge @ retaining wall RFI #54&57	Approved	Miller/RFI	\$1,879	Change Order #1
COR #19	2/22/2018	Demo conc. wall in lieu of mas. RFI #55	Approved	Miller/RFI	\$2,986	Change Order #3
COR #20		Chilled water piping RFI #58	Void	Void	Void	Void



COR #21		Floor underlayment RFI #64	Void	Void	Void	Void
COR #22		Undercuts per Oz Engineering				
A	11/3/2017	Pond #1 9/15 - 9/17	Approved	Oz Engineering	\$66,776	Change Order #1
B	11/3/2017	Report #24 & #28	Approved	Oz Engineering	\$36,924	Change Order #1
C	11/3/2017	Report #38, #40 & #44	Approved	Oz Engineering	\$16,932	Change Order #1
D	11/3/2017	Report #48, #52 & #58	Approved	Oz Engineering	\$44,880	Change Order #1
E	11/3/2017	Report #73 & #81	Approved	Oz Engineering	\$2,584	Change Order #1
F	11/21/2017	Report 11/1/17, 11/2/17	Approved	Oz Engineering	\$11,900	Change Order #2
G	11/21/2017	Report 11/6/17 - 11/11/17	Approved	Oz Engineering	\$53,924	Change Order #2
H	12/18/2017	Report 11/13/17 - 11/25/17	Approved	Oz Engineering	\$6,392	Change Order #3
I	12/18/2017	Report 11/27/17 - 12/2/17	Approved	Oz Engineering	\$62,356	Change Order #3
J	4/18/2018	Report 11/16/17, 12/4/17 - 2/26/18	Approved	Oz Engineering	\$19,244	Change Order #6
K	4/18/2018	Report 3/5/18 - 3/28/18	Approved	Oz Engineering	\$67,320	Change Order #6
COR #23	11/3/2017	Drain tile @ retaining wall RFI #77	Approved	Miller/RFI	\$8,139	Change Order #2
COR #24		Roof parapet replacement	Void	Void	Void	Void
COR #25	11/28/2017	Electric cost above allowance	Approved	Miller/Allowance	\$1,700	Change Order #2
COR #26	1/3/2018	Manhole 33 to parkway	Approved	Rettler	\$41,447	Change Order #3
COR #27		Hot and chilled water ERU-6	Void	Void	Void	Void
COR #28		Piping to VAV	Void	Void	Void	Void
COR #29	2/2/2018	Kitchen piping revisions	Approved	Miller/RFI	\$2,768	Change Order #3
COR #30	2/22/2018	Coal shoot infill @ courtyard	Approved	Miller/RFI	\$2,082	Change Order #3
COR #31	2/23/2018	Deadwall revisions	Approved	Miller/RFI	\$693	Change Order #3
COR #32	2/23/2018	Infill opening 107	Approved	Miller/RFI	\$5,143	Change Order #5
COR #33	2/23/2018	Retaining wall demo	Approved	Miller/RFI	\$5,916	Change Order #4
COR #34	2/2/2018	CR Leonard RFI #109	Approved	Miller/RFI	\$6,450	Change Order #3
COR #35	2/2/2018	Additional piping RFI #115	Approved	Miller/RFI	\$1,680	Change Order #3
COR #36	12/22/2017	Remove T&G flooring room 107A	Approved	Miller/RFI	\$2,602	Change Order #2
COR #37		Waterline revision per City	Void	Void	Void	Void
COR #38		Void	Void	Void	Void	Void
COR #39	2/22/2018	ASI #10	Approved	Architect	\$2,300	Change Order #3
COR #40	1/31/2018	Sound door & frames to match window	Rejected	Miller	(\$31,300)	Rejected
COR #41	2/23/2018	CUH-B2 RFI #86	Approved	Miller/RFI	\$3,114	Change Order #5
COR #42	2/2/2018	ASI #9 ductwork B212	Approved	Architect	\$3,918	Change Order #3
COR #43	2/2/2018	ASI #3 RTU-4	Void	Void	Void	Void

COR #44	2/23/2018	Chilled beams added after bid	Approved	Miller/RFI	\$4,496	Change Order #5
COR #45	2/21/2018	Fire sprinkler plan review	Approved	Miller	\$788	Change Order #4
COR #46	3/6/2018	Hardware finish	Approved	Miller/RFI	\$11,025	Change Order #4
COR #47	3/8/2018	Remove additional UG tank	Approved	Miller	\$13,352	Change Order #4
*COR #48	3/8/2018	Remove CMU @ windows	Approved	Architect	\$18,025	Change Order #5/ATSR Pay
COR #49	3/8/2018	Revise steel 2nd floor cafeteria	Approved	Architect	\$15,822	Change Order #4
COR #50	3/8/2018	Outlet for water cooler B126	Approved	Architect	\$315	Change Order #4
COR #51	3/8/2018	Remove burried conc pad water line	Approved	Miller	\$3,928	Change Order #4
COR #52	3/19/2018	IT floor mounted cabinet	Approved	Owner	\$1,848	Change Order #4
COR #53	3/19/2018	AT&T allowance	Approved	Miller	\$4,375	Change Order #4
COR #54	3/23/2018	Beam lead paint removal	Approved	Miller	\$4,656	Change Order #4
COR #55	3/23/2018	Anti-static flooring	Rejected	Miller	\$2,247	Rejected
COR #56	3/23/2018	Steel allowance	Rejected	Architect	(\$10,002)	Rejected
COR #57	3/27/2018	Additional tuckpointing	Pending	Iwanski/Architect	\$11,620	
COR #58	4/30/2018	Delete FA conduit above ceiling	Approved	Kellenberger	(\$22,575)	Change Order #6
COR #59	5/11/2018	Parapet wall repair	Approved	Iwanski/Architect	\$42,576	Change Order #7
COR #60	6/1/2018	Additional security cameras	Approved	Owner	\$12,390	Change Order #7
COR #61	6/1/2018	Night lighting	Approved	Architect	\$4,232	Change Order #7
COR #62	6/11/2018	ASI #14	Approved	Architect	\$6,486	Change Order #7
COR #63	6/11/2018	ASI #14	Approved	Architect	\$1,651	Change Order #7
COR #64	6/11/2018	Additional space sensors	Approved	Architect	\$5,772	Change Order #7
COR #65	6/15/2018	Plaster patching	Approved	Architect/Contractor	\$97,578	Change Order #7
COR #66	6/15/2018	Additional tuckpointing	Pending	Iwanski/Architect	\$7,200	
COR #67	6/18/2018	Relocate storm line @ cafeteria	Approved	CR Leonard	\$2,736	Change Order #7
COR #68	6/18/2018	Water tie in for hose bibs	Pending	CR Leonard	\$4,784	
COR #69	6/20/2018	Replace existing Allerton controllers	Pending	ABC	\$7,809	
COR #70	6/27/2018	Procenium opening, color change	Pending	HDS	\$1,948	
COR #71	7/7/2018	Investigate storm structure @ plaza	Approved	Katco	\$3,455	Change Order #7
COR #72	7/7/2018	Add cleanouts @ urnials	Approved	State inspector	\$2,814	Change Order #7



			Change Order #1	\$400,013	
			Change Order #2	\$62,384	
			Change Order #3	\$248,505	
			Change Order #4	\$283,910	
			Change Order #5	\$143,501	
			Change Order #6	\$206,746	
			Change Order #7	\$390,734	
			Approved Changes	\$189,872	Includes track
			Pending Changes	\$943,553	Includes turf
*COR #48		ATS&R to reimburse cost \$18,025			
			Total Changes	\$2,869,218	
			Rejected Changes	\$175,889	

Thompson Middle School		7/16/2018			%
K.R. Miller Contract				\$36,724,550.00	
		Change Order #1		\$400,013.00	
		Change Order #2		\$62,384.00	
		Change Order #3		\$248,505.00	
		Change Order #4		\$283,910.00	
		Change Order #5		\$143,501.00	
		Change Order #6		\$206,746.00	
		Change Order #7		\$390,734.00	
	Paid to Date	Pay App 1		-670,788.90	
		Pay App 2		-691,703.10	
		Pay App 3		-1,251,562.50	
		Pay App 4		-1,696,042.75	
		Pay App 5		-2,269,936.97	
		Pay App 6		-1,067,888.49	
		Pay App 7		-992,700.01	
		Pay App 8		-2,037,801.92	
		Pay App 9		-2,457,713.94	
		Pay App 10		(\$3,100,294.45)	
		Balance Due		\$22,223,909.97	58%
		Contingency Allocation		\$ 2,500,000.00	
		Contingency Items			
		Approved		(\$1,415,336)	
		Pending		(\$101,118)	
		Remaining Contingency		\$ 983,546.00	39%
		Scope Changes			
		Approved		\$330,729	
		Pending		\$1,032,685	



<u>Added Scope</u>	7/17/2018	<u>Contingency</u>	
Synthetic turf	842,791	Undercuts thru 3/28/18	389,232
Modify running track	132,825	Masonry lintel replacement	97,818
Additional windows	81,609	Plaster patching	97,578
Pond 3 fill	35,028	Cafeteria/kitchen modification	71,722
Additional mobile casework	33,643	Revise water & storm	68,689
Fritz tile	31,425	Emergency shower drains	67,234
Prep for field turf	28,712	Parapet wall replacement	61,655
Repalce galvanize water lines	28,175	Sitework	55,612
Acoustic wall panels	25,784	Fire pump	53,959
Power & IT revisions	23,431	Revisions to FACS	51,206
Sensory room revision	21,127	Parapet wall repair	42,576
Revisions to band & choir	14,650	Manhole 33 to parkway	41,447
Connect existing roof drains	14,232	Sitework	36,928
Added window E206	11,665	Revised furring	35,114
Acoustic windows	10,835	Lintel replacement	28,577
LRC conference room door	10,163	Toilet room revisions	28,534
Replace Allerton Controllers	7,809	Acoustic wall panels	25,785
Visual strobe music wing	6,422	Revise tempered water	23,582
Gym floor striping	6,214	Cafeteria ceiling modifications	18,141
Main office security	5,799	*Remove CMU @ windows	18,025
Existing gym graphics	5,145	Lighting for fitness rooms	16,517
Renumber existing lockers	2,082	Remove north hydrant	16,060
Floor mounted IT cabinet	1,848	Sanitary revisions	15,853
Room signage allowance	-18,000	Revise steel 2nd fl cafeteria	15,822
		Replace 2 existing manholes	15,462
		Revise heating & tertiary piping	13,894
Total	1,363,414	Additional U.G. tank	13,352
		Cafeteria ceiling modifications	12,638
		Sensory/tech closet	12,615
Approved	330,729	Replace 2 existing columns	12,527
Pending	1,032,685	Additional security cameras	12,390
		Water cooler A106 & A127	12,215
		Science B213 wall modification	11,652
		Additional tuckpointing	11,620
Rejected changes	175,889	Hardware finish	11,025
		B sanitary revision	9,455
		Infill duct openings	9,262
		Stairs C120 & D101	9,181
		Skylight shaft revisions	9,175
		Barrier curb removal	9,075
		Water cooler A108	8,801
		Drain tile @ retaining wall	8,139
		ASI 14	8,137
		Revise radiation A112	7,809

Casework revisions A114	1,106
Mechanical chase	858
Fire sprinkler review fee	788
Deadwall revisions	693
Frosted glass @ science	657
Delete sanitary line @ west	536
Revised ramp/curb detail	427
Water cooler outlet	315
Marker board modifications	-183
Delete new door/use existing	-2,099
Science window sills	-3,494
Storefront finish	-4,037
Revise wall tile	-4,050
Demo lead based paint	-5,432
Delete fire alarm conduit	-22,575
VCT @ cafeteria	-35,216
Marmoleum tile @ corridor	-54,514
Marmoleum tile @ classrooms	-145,254
Subfloor patching/prep	
Subfloor remedial work	
Total	1,516,454
Approved	1,415,336
Pending	101,118
*ATS&R to reimburse	18,025



ARMSTRONG, TORSETH, SKOLD AND RYDEEN, INC.  
ARCHITECTS AND ENGINEERS  
MEMORANDUM NO. 51C

Project Number: 16045  
Page 1

DATE July 12 2018

PROJECT Thompson Middle School Additions and Alterations

SUBJECT Construction Meeting

PRESENT School District #303  
Craig Lamp  
Seth Chapman

K.R. Miller  
Robert Richards  
Cody LaBeck  
Michael Cwienkala  
Paul Ingraham

Rettler Corporation  
Buck Barker

City of St. Charles  
Jeff Stengler  
Rainier Galliano

ATS&R  
Stewart Haugen  
Ben Williamson

BY Stewart Haugen

**1. PROGRESS SCHEDULE / LOOK AHEAD:**

- a. Units C & D: ACT ceiling grid, gypsum board, painting, tiling, mechanical rough-ins, locker base electrical rough-ins, elevator, and system tests continuing on both floors.
- b. Units C & D Second floor: casework, locker bases and interior glazing being installed.
- c. Units E & F: selective demolition and roofing occurring throughout.
- d. Unit G locker room: MEP rough-ins continuing.
- e. Unit G gym: majority of foundation walls and micro piles installed. Gym interior demolition underway.
- f. Chimney demolition underway, steel to be delivered next week, then concrete floor infill.
- g. Unit J: building demolition underway. During this major demolition phase the fire alarm system will be turned off during the work time (Fire Watch) and back on at night.
- h. Overall Site: Site demolition and site utility installation occurring on east side of site. North parking lot replacement and new trench drain at Hwy 64 entrance work to begin next week.
- i. Courtyard pad turf is installed. Glazing installer finishing up on courtyard side of structures.
- j. Elevator inspection once district has land line installed.
- k. Kitchen equipment being installed.

**2. SUBMITTALS:**

- a. Approximately 6 items to be submitted/ reviewed

**3. REQUEST FOR INFORMATION:**

- a. RFIs: 1-265 issued to date.
- 4. **CHANGES IN THE WORK:**
  - a. ASIs: 1-34 issued to date.
  - b. RFCOPs: 1-103 issued to date.
  - c. CORs: 1- 72 issued to date.
- 5. **BUILDING ACCESS:**
  - a. Review issues.
- 6. **OLD BUSINESS:**

**(New Business from 06.28.18 meeting)**


  - a. Elec. contractor to install temporary heat detectors
  - b. Need emergency exiting plans for occupied rooms. (Owner)
  - c. GPM calculations needed for building and irrigation systems to that water meters can be obtained from City. (ATSR & Rettler)
  - d. Remaining chilled beam delivery has been delayed, working with supplier to potentially obtain another manufacturer's product. Needs to be equal to Trox units.
  - e. Owner working on phone line to elevator.
  - f. Owner will need to shut off power to building before start of school due to St. Charles electrical utility issue.
  - g. Rettler to confirm location of light poles due to changes in site/grading plans.
  - h. Any upcoming changes in work scope will need to be prioritized and pricing may include Overtime charges as time is running short to complete existing work scope

**NEW BUSINESS:**

  - a. Due to schedule constraints, K.R. Miller will perform the balance of work per the contract documents and currently issued RFCOP's and ASI's. Pending revisions to the scope of work currently being executed, scheduled, or under fabrication will require an executed change order which includes additional time and costs to correct work in place. A written notice to stop work from the Owner or ATS&R will be required if pending revisions are to be accommodated prior to base contract work being executed.
  - b. Rettler to provide revised striping diagram for west side bus parking area.
  - c. Components of the new sprinkler piping components the existing gym sprinkler shall be painted to match the adjacent structure, either roof or wall.
  - d. MCT flooring install begins next week.
  - e. City to install permanent water meter within the next two weeks.
  - f. Doors that have faces painted blue shall also have the latch-side edge painted blue.
  - g. City needs smoke detector plan document for unsprinkled building spaces.
  - h. Classroom furniture delivery scheduled to begin on 7.30.
  - i. Single HM framed borrow lites with multiple panes of glass, at interior classrooms, may need to be modified. ATS&R to coordinate with district.
- 8. **The next Construction Meeting is on Thursday, July 19, 2018 at 11:00 AM in Main Office Conference Room A.**

**These notes represent the author's understanding of items discussed and decisions made at this meeting. Any comments or corrections should be forwarded to ATS&R within seven (7) days.**



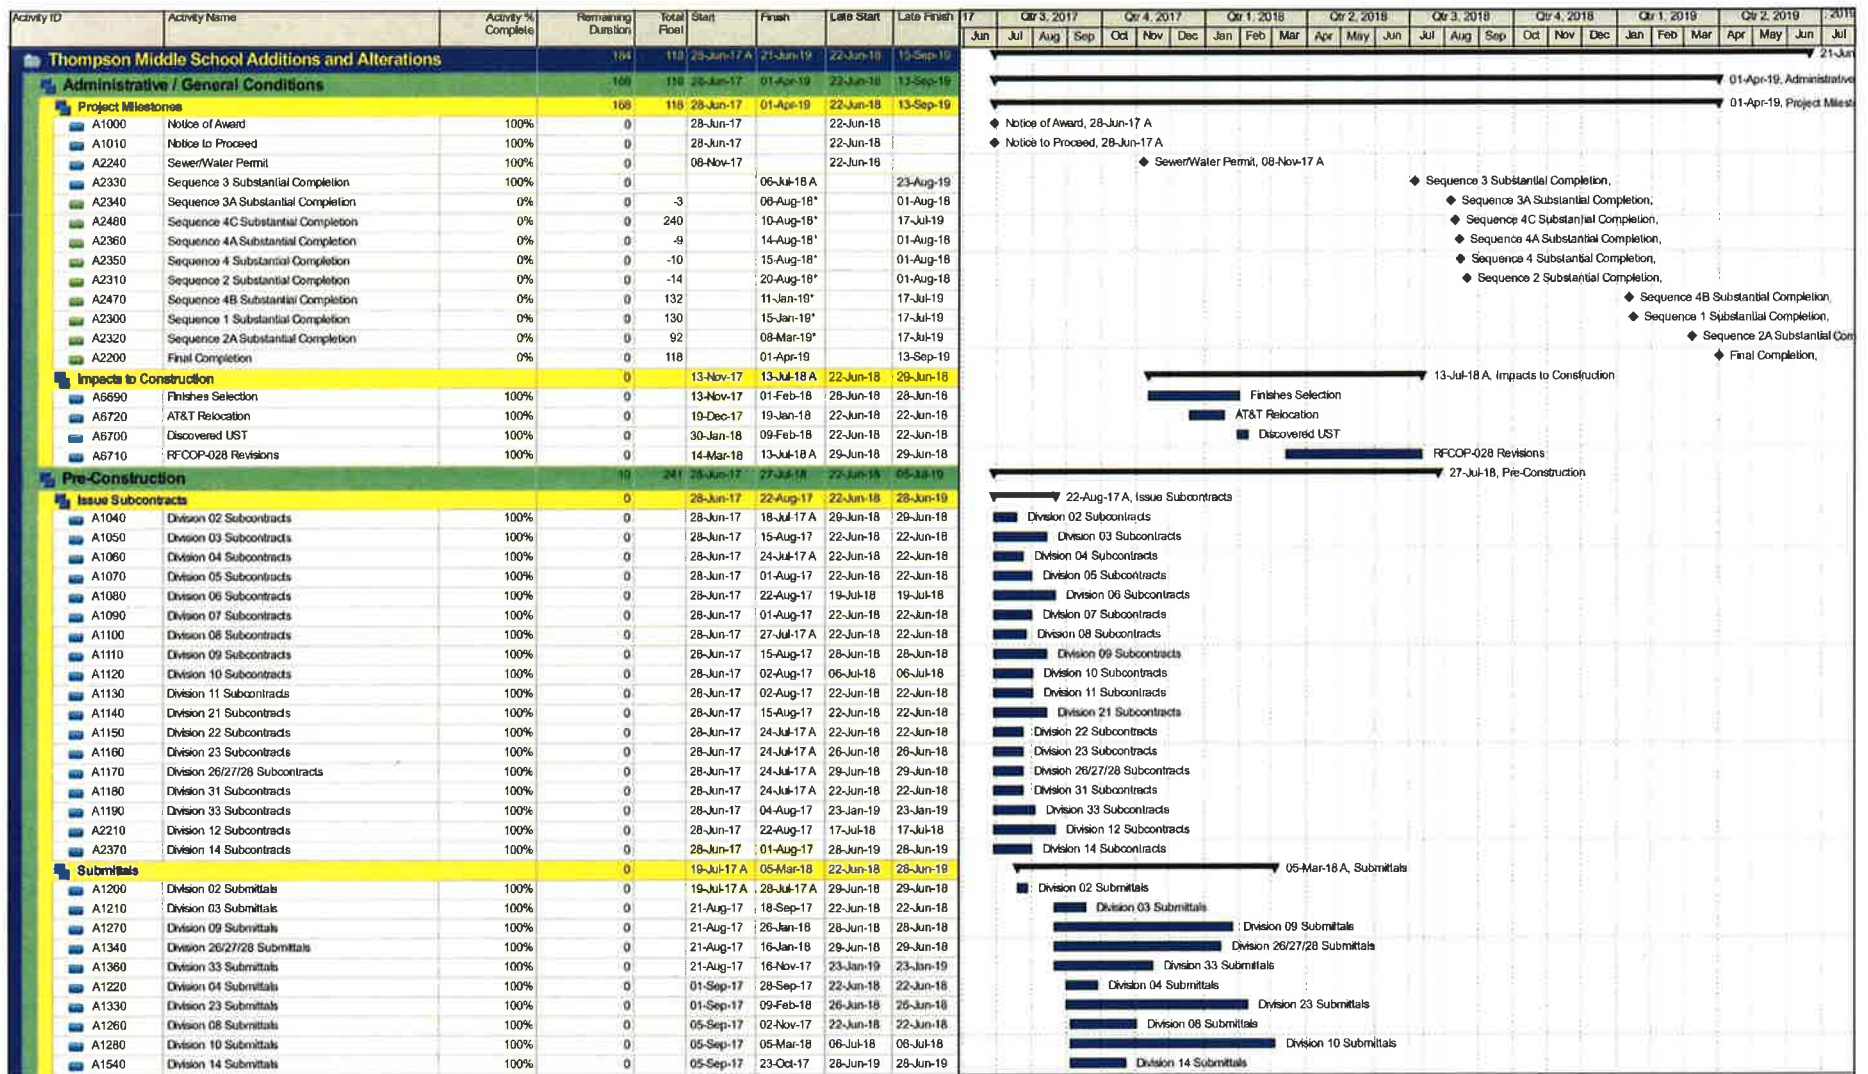


Data Date 15-Jul-18

Page 1 of 12

## Thompson Middle School Additions and Alterations Schedule Update

Submitted July 17, 2018



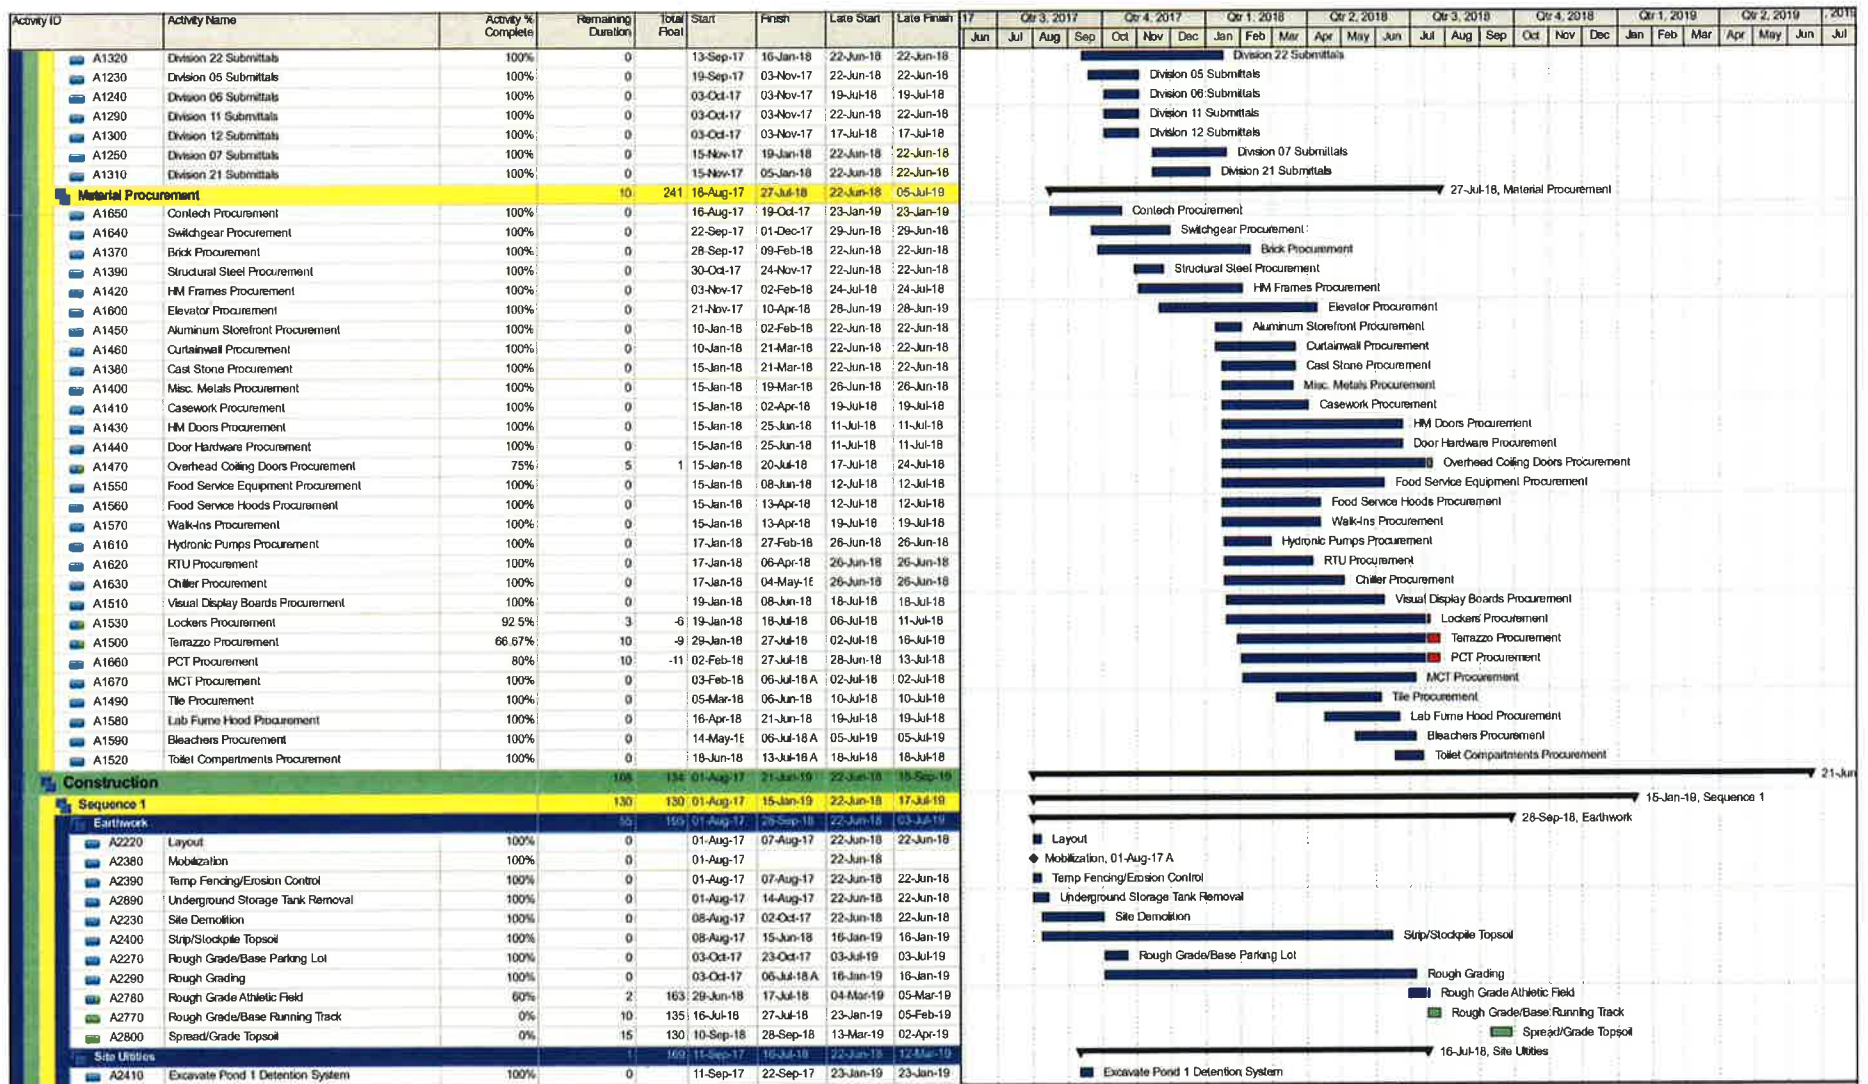

Data Date 15-Jul-18

Page2 of 12

## Thompson Middle School Additions and Alterations Schedule Update

Submitted July 17, 2018








Activity ID	Activity Name	Activity % Complete	Remaining Duration	Total Pct	Start	Finish	Late Start	Late Finish	17	Qtr 3, 2017	Qtr 4, 2017	Qtr 1, 2018	Qtr 2, 2018	Qtr 3, 2018	Qtr 4, 2018	Qtr 1, 2019	Qtr 2, 2019	2019				
									Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	Interior Buildout - Unit C, D, G		20	-11	09-Apr-18	10-Aug-18	22-Jun-18	27-Jul-18														
	Masonry		0		09-Apr-18	15-Jun-18	22-Jun-18	22-Jun-18														
	A3090 Classroom/Corridor CMU Partitions	100%	0		09-Apr-18	15-Jun-18	22-Jun-18	22-Jun-18														
	A3080 Toilet Room CMU Partitions	100%	0		16-Apr-18	15-Jun-18	22-Jun-18	22-Jun-18														
	Milwork		7	0	18-Jun-18	24-Jul-18	18-Jul-18	25-Jul-18														
	A3100 Install Casework	60%	2	3	18-Jun-18	17-Jul-18	19-Jul-18	23-Jul-18														
	A3110 Install Science Casework	60%	2	3	25-Jun-18	17-Jul-18	19-Jul-18	23-Jul-18														
	A3120 Install Countertops	60%	2	3	02-Jul-18 A	19-Jul-18	23-Jul-18	25-Jul-18														
	A3300 Install Display Cases	0%	5	0	18-Jul-18	24-Jul-18	18-Jul-18	25-Jul-18														
	Doors/Frames/Hardware		7	0	23-Apr-18	24-Jul-18	18-Jul-18	25-Jul-18														
	A3130 Set Interior HM Frames	100%	0		23-Apr-18	06-Jul-18 A	18-Jul-18	18-Jul-18														
	A3150 Install Glazing	80%	1	6	25-Jun-18	16-Jul-18	24-Jul-18	25-Jul-18														
	A3160 Install Interior Storefront	0%	5	2	25-Jun-18	20-Jul-18	18-Jul-18	25-Jul-18														
	A3140 Install Interior Doors/Hardware	50%	5	0	02-Jul-18 A	24-Jul-18	18-Jul-18	25-Jul-18														
	Drywall		0		23-Apr-18	06-Jul-18 A	22-Jun-18	22-Jun-18														
	A3170 Frame Interior Partitions	100%	0		23-Apr-18	08-Jun-18	22-Jun-18	22-Jun-18														
	A3180 Drywall/Tape Partitions	100%	0		14-May-18	06-Jul-18 A	22-Jun-18	22-Jun-18														
	Ceilings		15	-13	28-May-18	10-Aug-18	22-Jun-18	18-Jul-18														
	A3190 Frame/Drywall Soffits/Ceilings	100%	0		28-May-18	15-Jun-18	26-Jun-18	26-Jun-18														
	A3200 Install ACT Grid	90%	2	-15	11-Jun-18	17-Jul-18	22-Jun-18	26-Jun-18														
	A3210 Install ACT Panels	50%	5	-13	02-Jul-18 A	03-Aug-18	11-Jul-18	18-Jul-18														
	Flooring		15	-11	13-Jun-18	13-Aug-18	11-Jul-18	27-Jul-18														
	A3220 Install Ceramic Tile	100%	0		13-Jun-18	13-Jul-18 A	18-Jul-18	18-Jul-18														
	A3230 Install Resilient Flooring	0%	10	-5	18-Jul-18	31-Jul-18	11-Jul-18	25-Jul-18														
	A3250 Install Carpeting	0%	10	-5	18-Jul-18	31-Jul-18	11-Jul-18	25-Jul-18														
	A3260 Install Stair Treads	0%	5	-3	23-Jul-18	27-Jul-18	18-Jul-18	25-Jul-18														
	A3580 Install PCT	0%	10	-11	30-Jul-18	10-Aug-18	13-Jul-18	27-Jul-18														
	Painting		12	-13	11-Jun-18	03-Aug-18	22-Jun-18	18-Jul-18														
	A3270 Prime/Blockfiller Partitions	100%	0		11-Jun-18	29-Jun-18	22-Jun-18	22-Jun-18														
	A3280 Finish Painting	40%	12	-13	02-Jul-18 A	03-Aug-18	29-Jun-18	18-Jul-18														
	Specialties		20	-13	16-Jul-18	10-Aug-18	11-Jul-18	25-Jul-18														
	A3320 Install Toilet Compartments/Accessories	0%	5	2	18-Jul-18	20-Jul-18	18-Jul-18	25-Jul-18														
	A3350 Install Projection Screens	0%	5	0	18-Jul-18	24-Jul-18	18-Jul-18	25-Jul-18														
	A3330 Install Fire Extinguisher Cabinets	0%	5	-1	19-Jul-18	25-Jul-18	18-Jul-18	25-Jul-18														
	A3340 Install Lockers	0%	10	-6	19-Jul-18	01-Aug-18	11-Jul-18	25-Jul-18														
	A3360 Install Window Shades	0%	10	-13	30-Jul-18	10-Aug-18	11-Jul-18	25-Jul-18														
	A3290 Install Visual Display Boards	0%	5	-13	06-Aug-18	10-Aug-18	18-Jul-18	25-Jul-18														
	A3310 Install Signage	0%	5	-13	06-Aug-18	10-Aug-18	18-Jul-18	25-Jul-18														
	MEP Systems - Unit C, D, G		25	-15	13-Dec-17	17-Aug-18	22-Jun-18	30-Jul-18														
	Fire Protection		5	-4	02-Apr-18	20-Jul-18	22-Jun-18	11-Jul-18														
	A3370 Rough-In Fire Sprinkler Piping	100%	0		02-Apr-18	01-Jun-18	22-Jun-18	22-Jun-18														
	A3380 Trim Fire Sprinklers	66.67%	5	-8	02-Jul-18 A	20-Jul-18	03-Jul-18	11-Jul-18														
	Plumbing		3	-4	13-Dec-17	18-Jul-18	22-Jun-18	25-Jul-18														
	A3390 Underground Plumbing	100%	0		13-Dec-17	20-Apr-18	22-Jun-18	22-Jun-18														
	A3400 Rough-In Plumbing	100%	0		23-Apr-18	29-Jun-18	22-Jun-18	22-Jun-18														
	A3410 Trim Plumbing	70%	3	4	02-Jul-18 A	18-Jul-18	20-Jul-18	25-Jul-18														
	HVAC		25	-15	09-Apr-18	17-Aug-18	22-Jun-18	30-Jul-18														
	A3420 Rough-In Hydronic Piping	100%	0		09-Apr-18	29-Jun-18	22-Jun-18	22-Jun-18														
	A3430 Rough-In Ductwork	100%	0		09-Apr-18	13-Jul-18 A	22-Jun-18	22-Jun-18														
	A3450 Install Roof-Top Equipment	100%	0		23-Apr-18	11-May-18	26-Jun-18	28-Jun-18														
	A3440 Install Unit Heaters	100%	0		02-Jul-18 A	13-Jul-18 A	25-Jul-18	25-Jul-18														
	A3480 Install Chilled Beams	25%	15	-15	02-Jul-18 A	03-Aug-18	22-Jun-18	16-Jul-18														
	A3460 Trim Hydronic Piping/Equipment	33.33%	10	-13	09-Jul-18 A	27-Jul-18	26-Jun-18	11-Jul-18														

Data Date 15-Jul-18

Page4 of 12

## Thompson Middle School Additions and Alterations Schedule Update

Submitted July 17, 2018

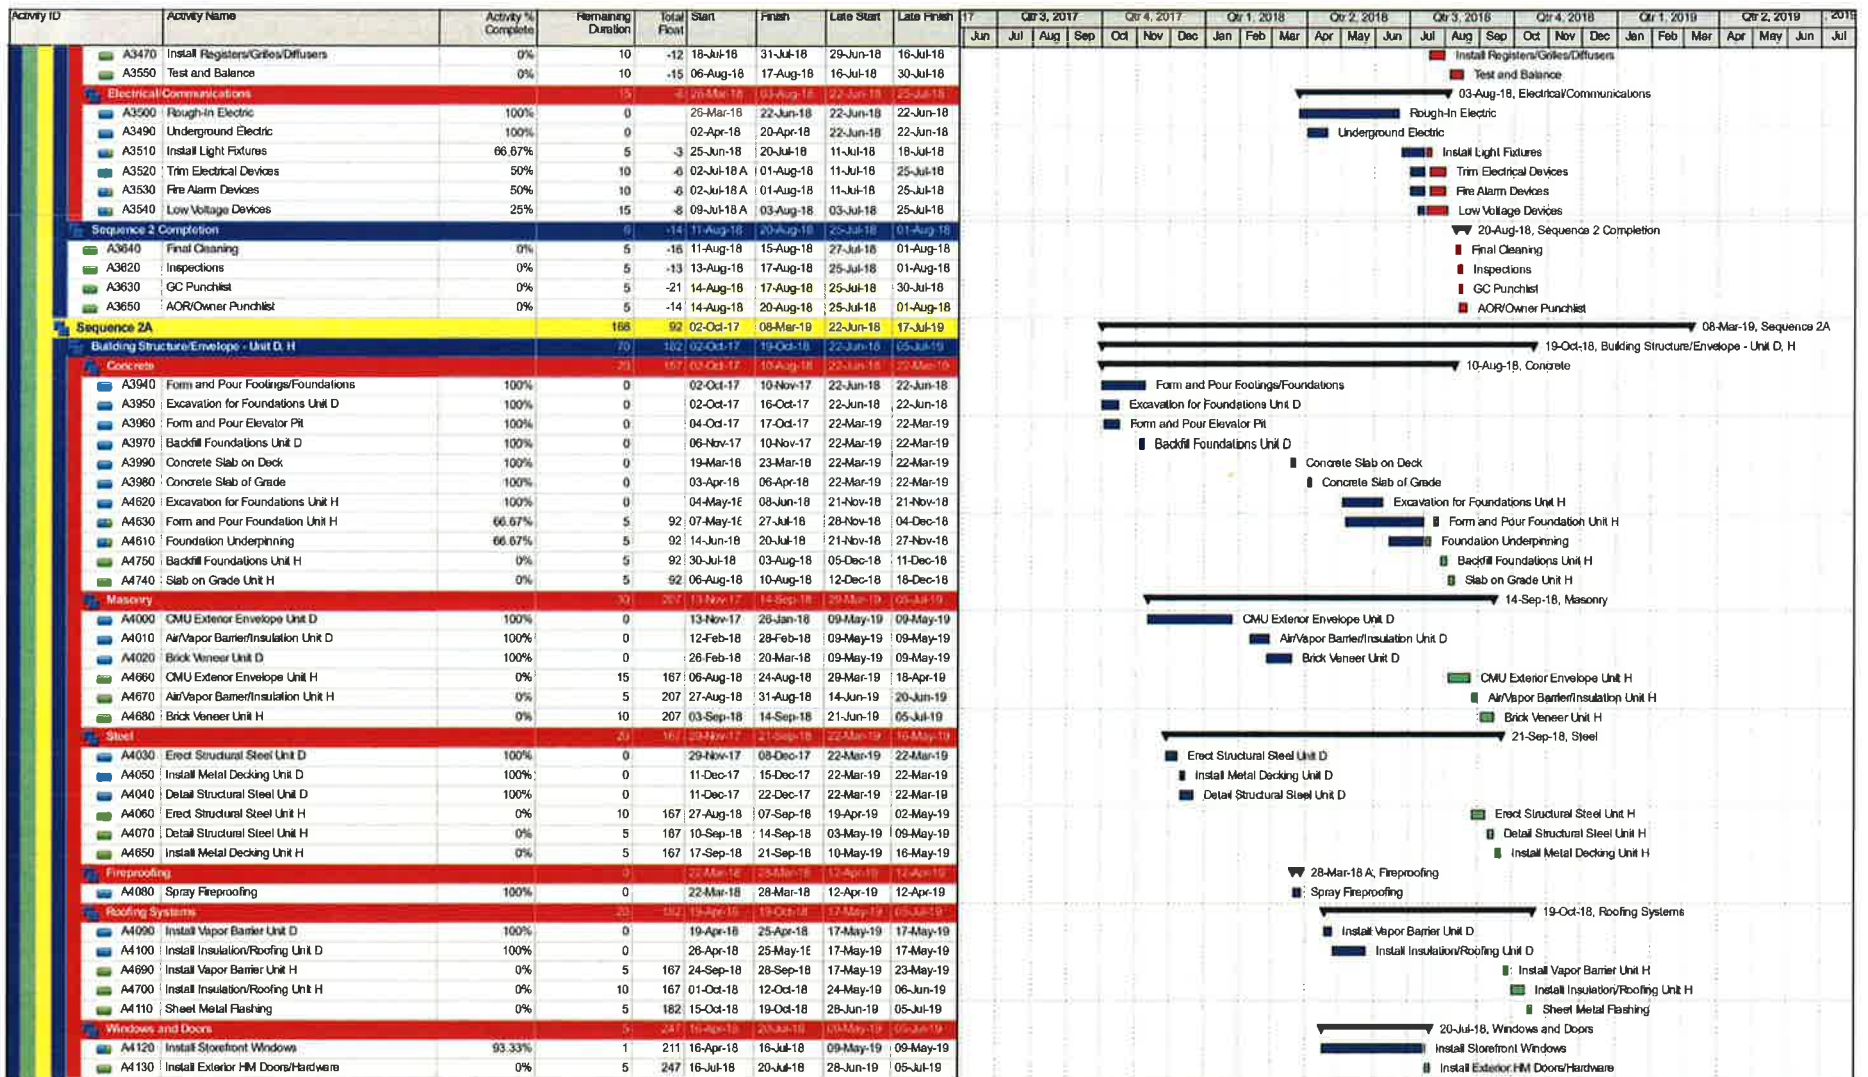

Data Date 15-Jul-18


Page5 of 12

## Thompson Middle School Additions and Alterations Schedule Update

Submitted July 17, 2018





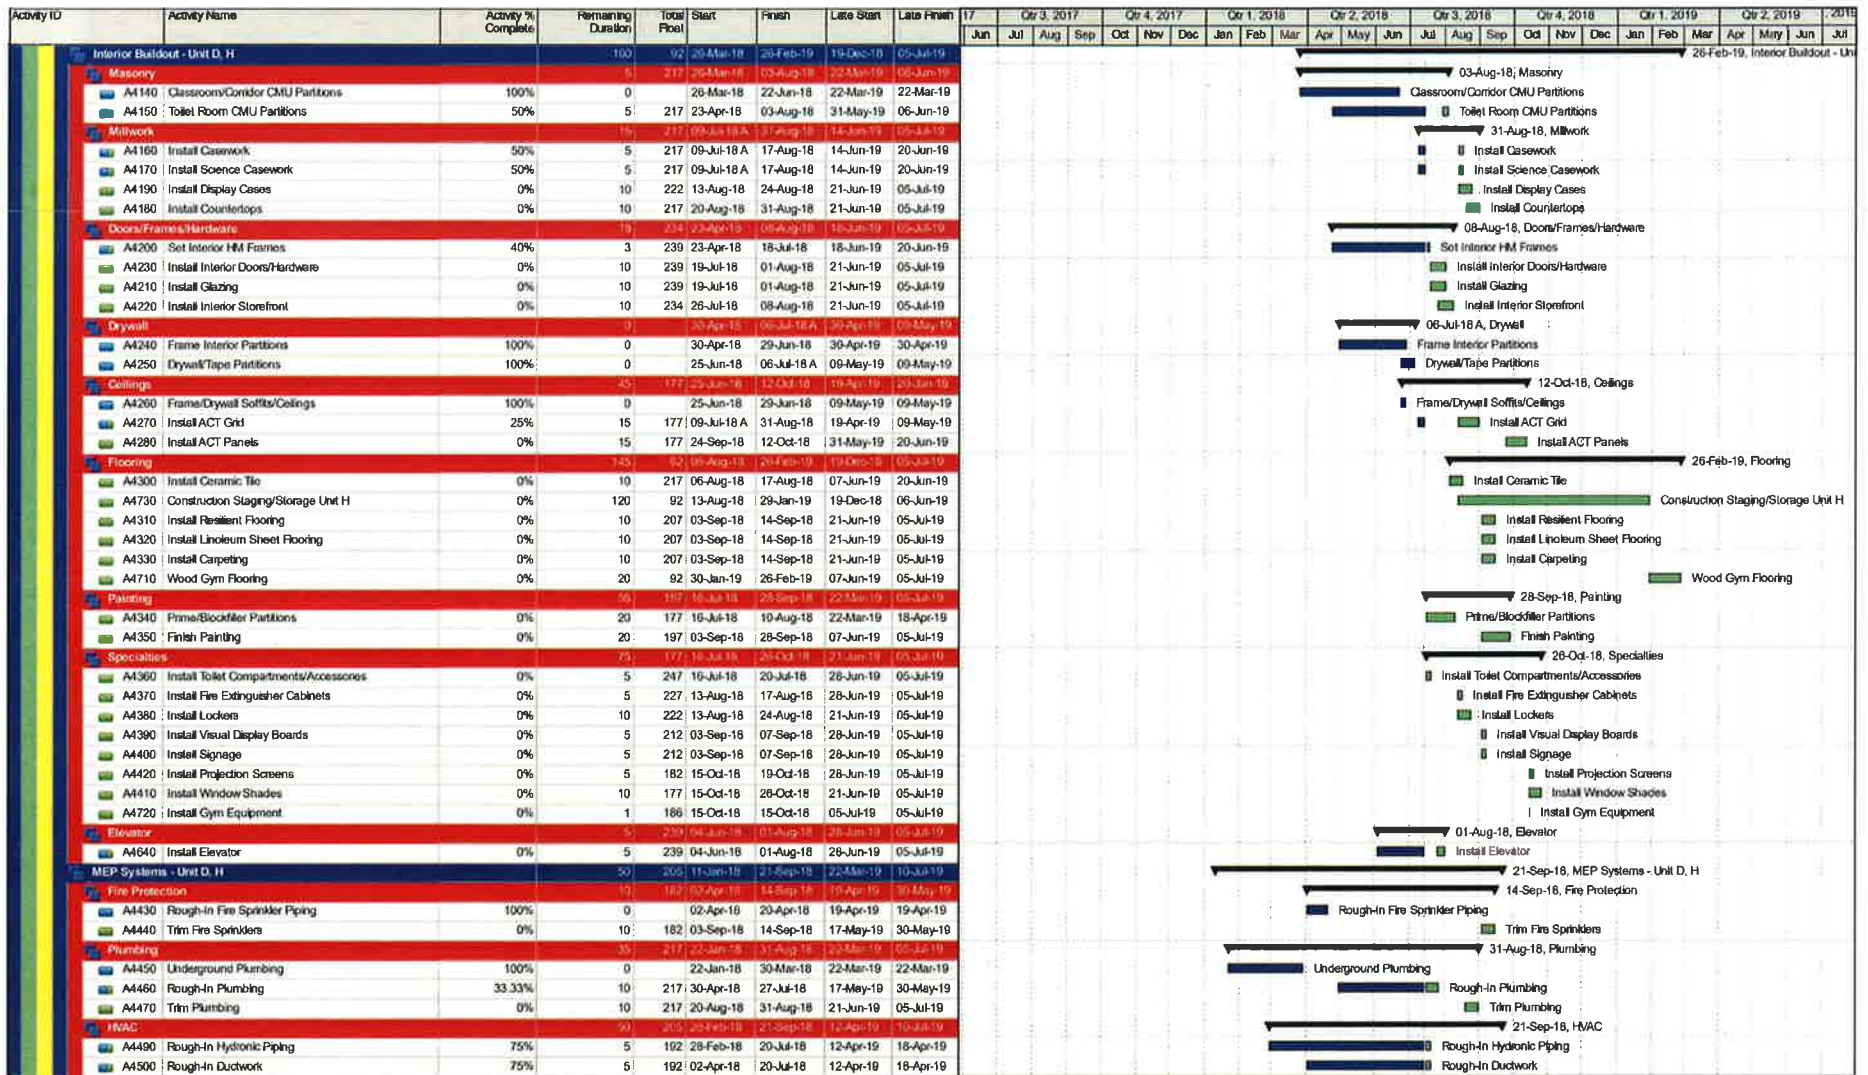

Data Date 15-Jul-18

Page 6 of 12


## Thompson Middle School Additions and Alterations

### Schedule Update

Submitted July 17, 2018





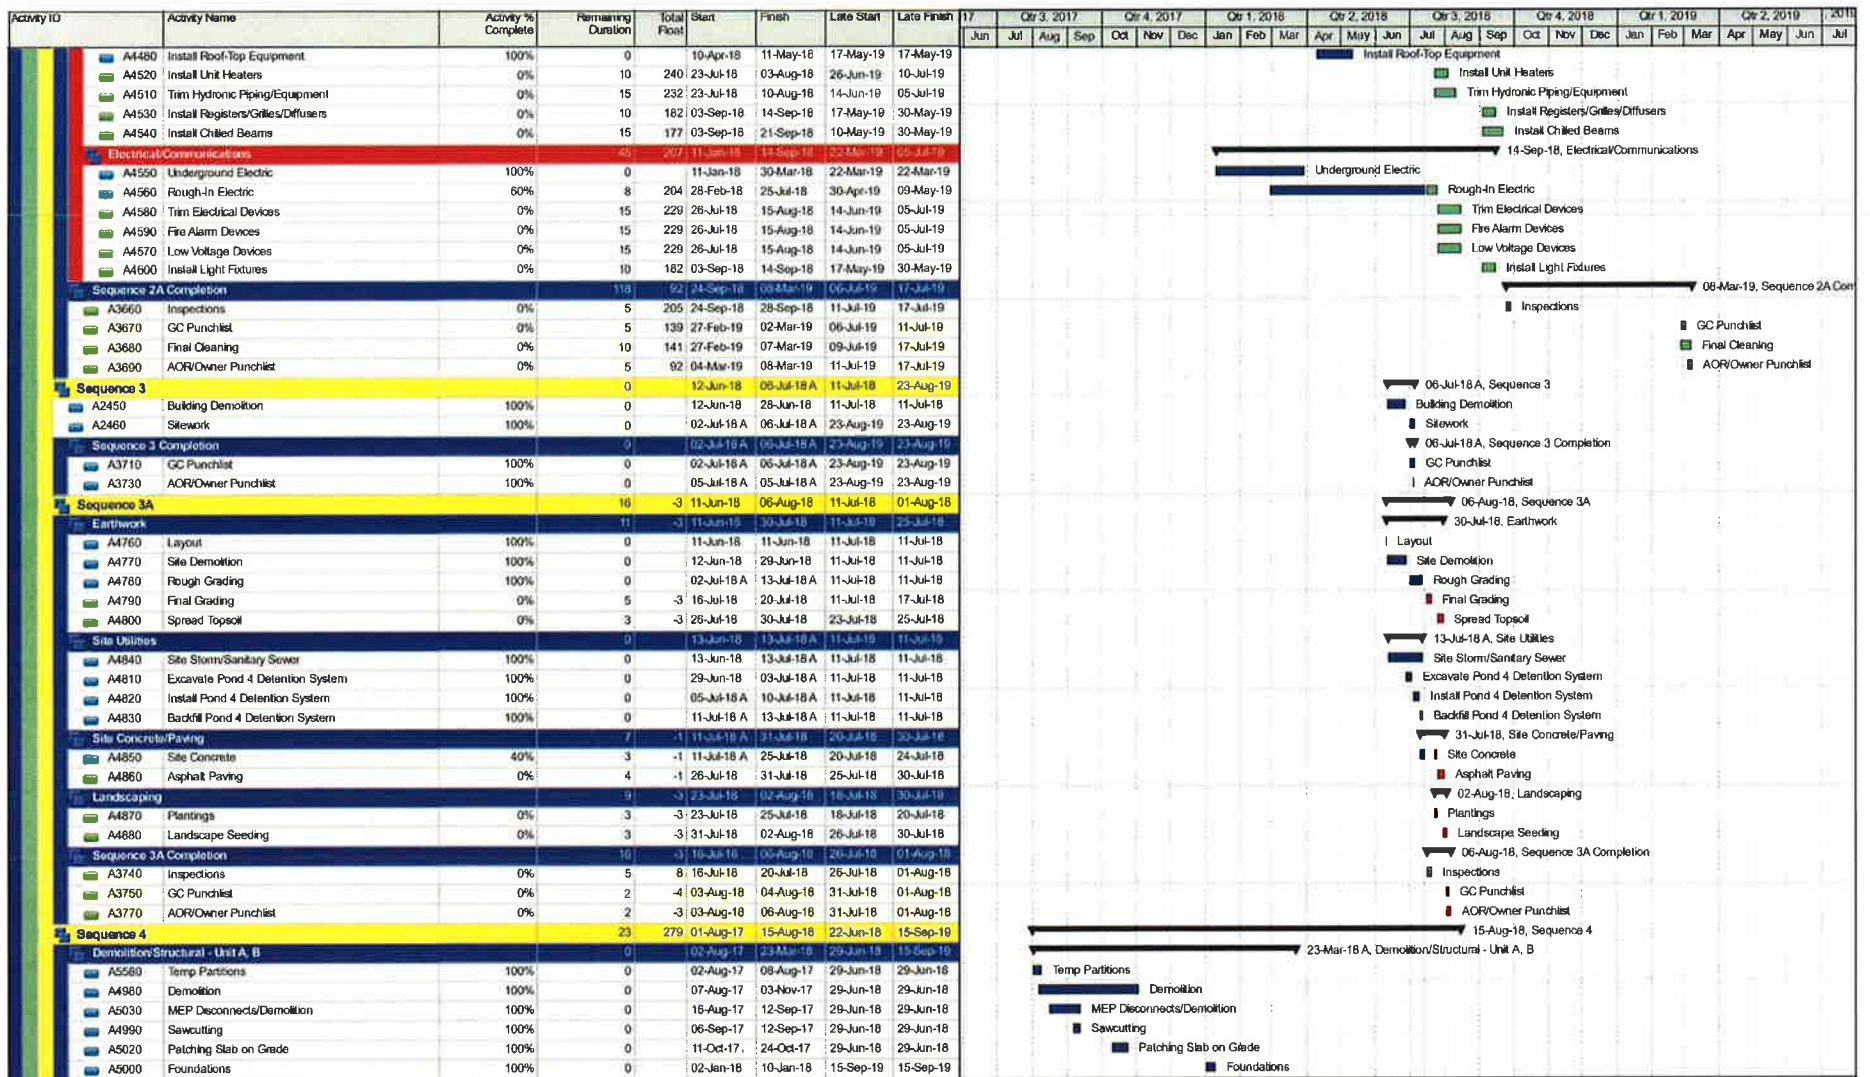

Data Date 15-Jul-18

Page 7 of 12

## Thompson Middle School Additions and Alterations

### Schedule Update

Submitted July 17, 2018





Data Date 15-Jul-18 Page9 of 12	<p align="center"><b>Thompson Middle School Additions and Alterations</b></p> <p align="center">Schedule Update</p> <p align="center">Submitted July 17, 2018</p>	
------------------------------------	---	--





Activity ID	Activity Name	Activity % Complete	Remaining Duration	Total Float	Start	Finish	Late Start	Late Finish	17	Qtr 3, 2017	Qtr 4, 2017	Qtr 1, 2018	Qtr 2, 2018	Qtr 3, 2018	Qtr 4, 2018	Qtr 1, 2019	Qtr 2, 2019	2019				
									Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
A6290	Install Interior Doors/Hardware	0%	10	162	05-Nov-18	16-Nov-18	21-Jun-19	05-Jul-19														
A6300	Drywall	0%	40	132	15-Jul-18	07-Sep-18	18-Jan-19	14-Mar-19														
A6310	Frame Interior Partitions/Furring	0%	25	132	16-Jul-18	17-Aug-18	18-Jan-19	21-Feb-19														
A6330	Drywall/Tape Partitions	0%	15	132	20-Aug-18	07-Sep-18	22-Feb-19	14-Mar-19														
A6340	Ceilings	0%	30	132	08-Oct-18	14-Dec-18	12-Apr-19	25-Jun-19														
A6350	Install ACT Grid	0%	20	132	08-Oct-18	02-Nov-18	12-Apr-19	09-May-19														
A6370	Install ACT Panels	0%	10	132	03-Dec-18	14-Dec-18	07-Jun-19	20-Jun-19														
A6380	Flooring	0%	75	157	20-Aug-18	30-Nov-18	29-May-19	12-Jul-19														
A6400	Install Ceramic Tile	0%	20	200	20-Aug-18	14-Sep-18	29-May-19	25-Jun-19														
A6410	Install Linoleum Sheet Flooring	0%	20	157	05-Nov-18	30-Nov-18	14-Jun-19	12-Jul-19														
A6430	Install Carpeting	0%	10	167	05-Nov-18	16-Nov-18	28-Jun-19	12-Jul-19														
A6440	Painting	0%	40	172	10-Sep-18	02-Nov-18	15-Mar-19	08-Jul-19														
A6450	Prime/Block/Filler Partitions	0%	20	132	10-Sep-18	05-Oct-18	15-Mar-19	11-Apr-19														
A6470	Finish Painting	0%	20	172	08-Oct-18	02-Nov-18	07-Jun-19	05-Jul-19														
A6480	Specialties	0%	25	137	17-Sep-18	31-Dec-18	21-Jun-19	12-Jul-19														
A6490	Install Toilet Compartments/Accessories	0%	5	202	17-Sep-18	21-Sep-18	28-Jun-19	05-Jul-19														
A6500	Install Visual Display Boards	0%	5	187	08-Oct-18	12-Oct-18	28-Jun-19	05-Jul-19														
A6520	Install Signage	0%	5	187	08-Oct-18	12-Oct-18	28-Jun-19	05-Jul-19														
A6530	Install Fire Extinguisher Cabinets	0%	5	190	08-Oct-18	12-Oct-18	03-Jul-19	10-Jul-19														
A6540	Install Lockers	0%	10	167	05-Nov-18	16-Nov-18	28-Jun-19	12-Jul-19														
A6550	Install Projection Screens	0%	5	137	17-Dec-18	21-Dec-18	28-Jun-19	05-Jul-19														
A6560	Install Window Shades	0%	10	132	17-Dec-18	31-Dec-18	21-Jun-19	05-Jul-19														
A6570	MEP Systems - Unit E, F	0%	110	145	16-Jul-18	14-Dec-18	15-Feb-19	10-Jul-19														
A6580	Fire Protection	0%	90	137	16-Jul-18	23-Nov-18	22-May-19	06-Jun-19														
A6590	Rough-In Fire Sprinkler Piping	0%	15	177	16-Jul-18	03-Aug-18	22-Mar-19	11-Apr-19														
A6600	Trim Fire Sprinklers	0%	15	137	05-Nov-18	23-Nov-18	17-May-19	06-Jun-19														
A6610	Plumbing	0%	110	145	16-Jul-18	14-Dec-18	15-Feb-19	10-Jul-19														
A6620	Rough-In Plumbing	0%	15	200	16-Jul-18	03-Aug-18	24-Apr-19	14-May-19														
A6630	Underground Plumbing	0%	20	216	17-Jul-18	13-Aug-18	17-May-19	13-Jun-19														
A6640	Trim Plumbing	0%	10	145	03-Dec-18	14-Dec-18	26-Jun-19	10-Jul-19														
A6650	HVAC	0%	110	145	16-Jul-18	14-Dec-18	15-Feb-19	10-Jul-19														
A6660	Rough-In Hydronic Piping	0%	40	152	16-Jul-18	07-Sep-18	15-Feb-19	11-Apr-19														
A6670	Rough-In Ductwork	0%	40	152	16-Jul-18	07-Sep-18	15-Feb-19	11-Apr-19														
A6680	Dust Collector	0%	15	230	16-Jul-18	03-Aug-18	05-Jun-19	25-Jun-19														
A6690	Install Unit Heaters	0%	10	180	10-Sep-18	21-Sep-18	22-May-19	04-Jun-19														
A6700	Install Roof-Top Equipment	0%	10	172	10-Sep-18	21-Sep-18	10-May-19	23-May-19														
A6710	Trim Hydronic Piping/Equipment	0%	15	180	24-Sep-18	12-Oct-18	05-Jun-19	25-Jun-19														
A6720	Install Registers/Grilles/Diffusers	0%	10	142	05-Nov-18	16-Nov-18	24-May-19	06-Jun-19														
A6730	Install Chilled Beams	0%	20	132	05-Nov-18	30-Nov-18	10-May-19	06-Jun-19														
A6740	Test and Balance	0%	10	145	03-Dec-18	14-Dec-18	26-Jun-19	10-Jul-19														
A6750	Electrical/Communications	0%	90	160	16-Jul-18	23-Nov-18	15-Feb-19	10-Jul-19														
A6760	Rough-In Electric	0%	40	152	16-Jul-18	07-Sep-18	15-Feb-19	11-Apr-19														
A6770	Underground Electric	0%	10	226	17-Jul-18	30-Jul-18	31-May-19	13-Jun-19														
A6780	Trim Electrical Devices	0%	20	195	10-Sep-18	05-Oct-18	12-Jun-19	10-Jul-19														
A6790	Fire Alarm Devices	0%	20	195	10-Sep-18	05-Oct-18	12-Jun-19	10-Jul-19														
A6800	Low Voltage Devices	0%	20	195	10-Sep-18	05-Oct-18	12-Jun-19	10-Jul-19														
A6810	Install Light Fixtures	0%	15	137	05-Nov-18	23-Nov-18	17-May-19	06-Jun-19														
A6820	Sequence 4B Completion	0%	5	132	15-Dec-18	11-Jan-19	06-Jul-19	17-Jul-19														
A6830	Final Cleaning	0%	5	225	15-Dec-18	19-Dec-18	13-Jul-19	17-Jul-19														
A6840	Inspections	0%	5	145	17-Dec-18	21-Dec-18	11-Jul-19	17-Jul-19														
A6850	GC Punchlist	0%	5	200	01-Jan-19	04-Jan-19	08-Jul-19	11-Jul-19														
A6860	AOR/Owner Punchlist	0%	5	132	07-Jan-19	11-Jan-19	11-Jul-19	17-Jul-19														
A6870	Sequence 4C	0%	20	240	16-Jul-18A	21-Jun-19	10-Jun-19	17-Jul-19														

Data Date 15-Jul-18

Page 11 of 12

## Thompson Middle School Additions and Alterations Schedule Update

Submitted July 17, 2018









## Three Week Look Ahead Schedule

Project: Thompson Middle School Additional and Alterations  
705 West Main Street  
St. Charles, IL 60174

Contractor: K.R. Miller Contractors, Inc.  
1624 Colonial Parkway  
Inverness, IL 60067

Architect: ATS&R  
8501 Golden Valley Road, Suite 300  
Minneapolis, MN 55427  
AOR Project No. 16045

Submitted: July 19th, 2018

Last Week							Subcontractor	Activity	Current Week							Week 2							Week 3						
Week Ending 07/14/18									Week Ending 07/21/18							Week Ending 07/28/18							Week Ending 08/04/18						
M	T	W	Th	F	Sa	Su			M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su	M	T	W	Th	F	Sa	Su
7/9	7/10	7/11	7/12	7/13	7/14	7/15			7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25	7/26	7/27	7/28	7/29	7/30	7/31	8/1	8/2	8/3	8/4	8/5
X	X	X	X	X	X		Construction Junction	Earthwork (Weather Dependant)	X	X	X	X	X		X	X	X	X	X		X	X	X	X	X				
							Construction Junction	Excavation for Foundations (Bldg H)									X	X	X										
							Construction Junction	Excavation for North Parking Lot							X	X	X	X	X										
X	X	X	X	X			Construction Junction	Site Clearing (East Side)	X	X	X	X	X																
							Schroeder Asphalt	Asphalt (North, East, West)													X	X	X	X	X				
X	X	X	X	X	X		Midwest Wrecking	Demolition (Area E & F)	X	X	X	X	X		X	X													
X	X	X	X	X	X		K.R. Miller	Site Concrete (West)	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X		
X	X	X	X	X	X		K.R. Miller	Site Concrete (East)	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X			
							K.R. Miller	Concrete Footing (E foundations)							X	X	X												
X	X				X		Iwanski Masonry	Interior CMU Partitions (Bldg E)	X	X	X						X	X			X	X	X	X					
X	X	X	X	X			Cornerstone Carpentry	Casework Install (Bldg A and B)	X	X	X	X	X		X	X	X	X	X										
X	X	X	X	X	X		K.R. Miller	Roof Blocking (Area G)																					
X	X	X	X	X	X		K.R. Miller	Roof Blocking (Area E)	X	X	X	X	X																
							L.J. Morse	Partition Walls - Framing (Bldg E&F)	X	X	X	X	X		X	X	X	X	X		X	X	X	X	X				
X	X	X	X	X			L.J. Morse	Partition Walls - Taping (Bldg A&B)	X		X		X																
X	X	X					L.J. Morse	Partition Walls - Taping (Bldg C & D)																					
							L.J. Morse	Partition Walls - Drywall (Bldg E + F)	X	X	X	X	X		X	X	X	X	X		X	X	X	X	X				
							L.J. Morse	Partiton Walls - Taping (Bldg E + F)	X	X	X	X	X		X	X	X	X	X		X	X	X	X	X				

